



21st Century Classroom Improvements

January 25, 2022 Board Update



21st Century Classroom Improvements

PROJECT CERTIFIED





January 12, 2022

Certification of Compliance

Dr. Alfonso Jimenez
Hacienda-La Puente Unified School District
15959 East Gale Avenue
City Of Industry, CA 91745

Project: LOS ALTOS ELEMENTARY SCHOOL
Application #: 03-119947
File Id #: 19-38
Scope: Alterations to 3-Classroom Upgrades Bldgs. A, B & C (A03-106050, A-19204), 2-Classroom Upgrades E & F (A03-100753, A-19909), 1-Classroom Upgrade Relo Bldgs. G1 (A03-100753), 1-Classroom Upgrade Relo Bldg. G2 (A03-118191), 1-Classroom Upgrade Relo Bldg. G3 (A03-117281)

Cedarlane Academy

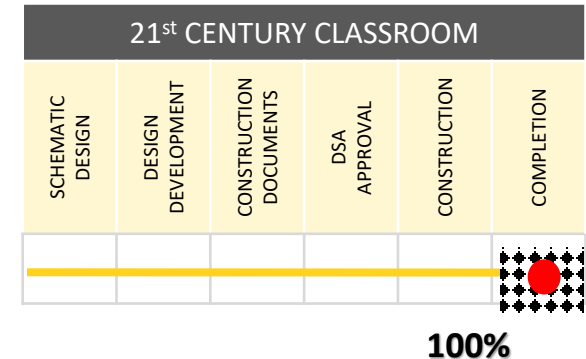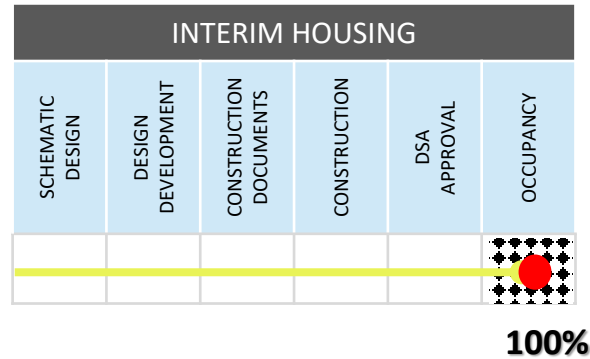


NOTES


- Interim Housing Complete Close Out Phase
- 21st Century Classroom Improvements Complete
- **CLOSEOUT & DSA CERTIFICATION**

Project Status
SUBSTANTIALLY
COMPLETE

Newton Middle School

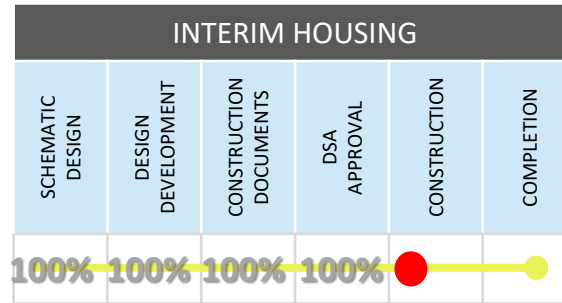


25%

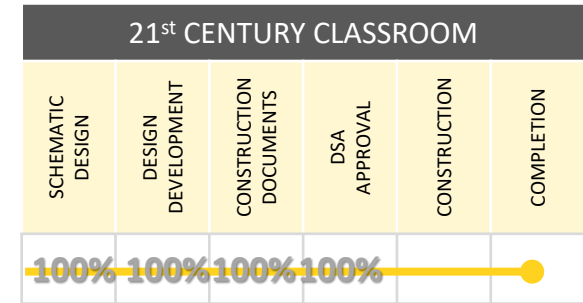

NOTES

- Interim Housing
- Construction In Progress
- Current Tasks
 - Grading
 - Paving
 - Accessible walks
 - Placing Buildings
 - Electrical & Communications

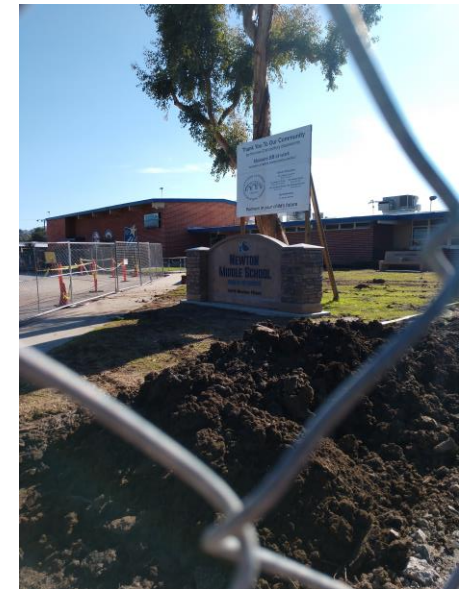


Project Status
SITE WORK & BUILDING
PLACEMENT

Newton Middle School



Under Construction

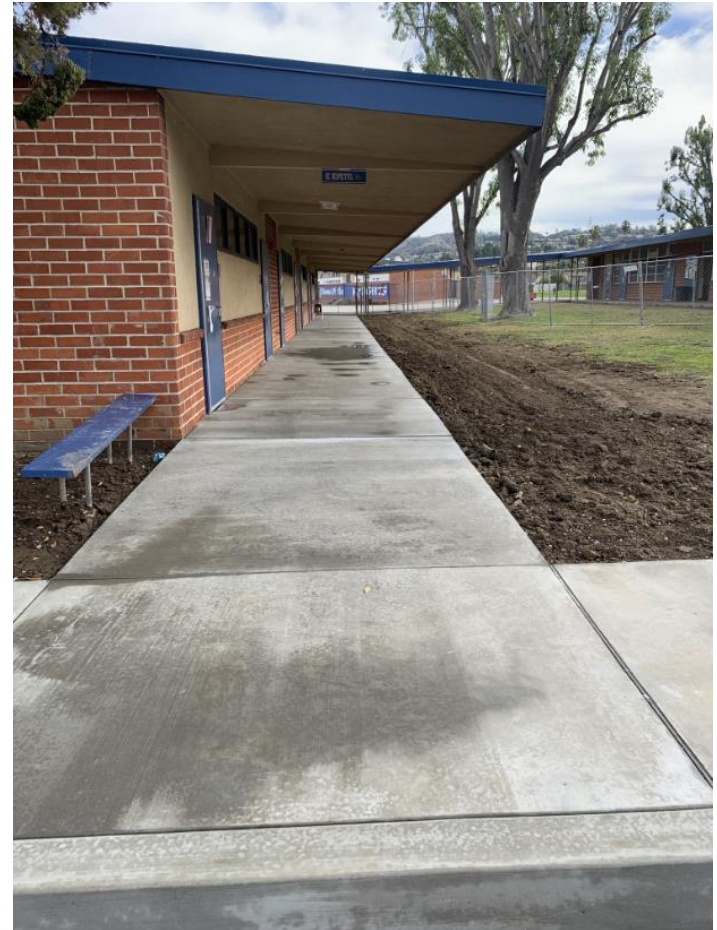


After

Accessible Walkway "B" Wing

Newton Middle School



Accessible Walk "B" Wing

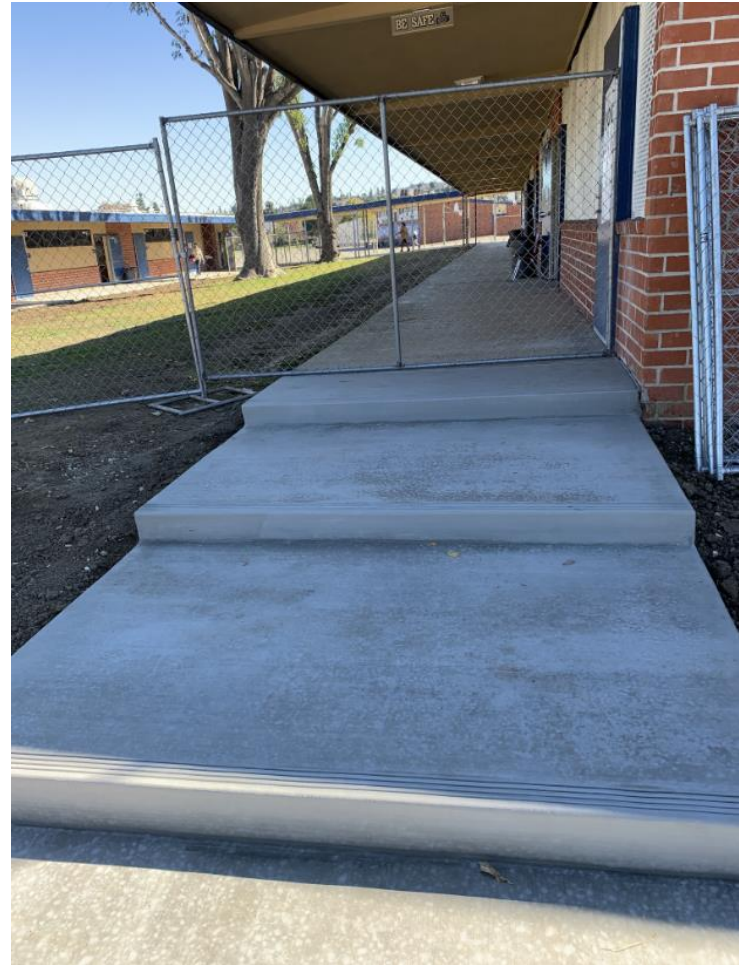

New Steps "C" Wing

Newton Middle School



Building Pads
North Parking Lot


Accessible Walks- Main Entry

PROJECT DASHBOARD: SITE FINANCIALS


KPI Overview NEWTON INTERIM HOUSING

Budget	Committed	Balance
\$ 909.8K	\$ 339.0K	\$ 570.8K


Budget Breakdown

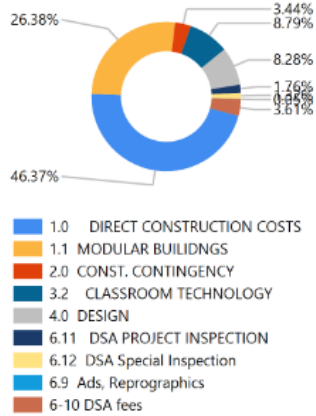


Commitments Breakdown

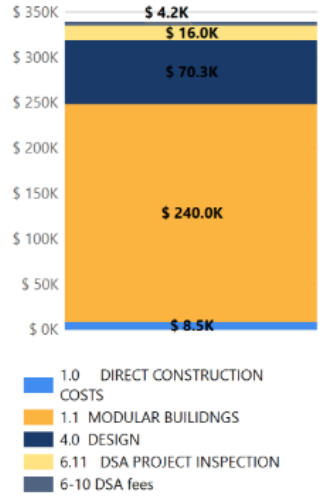


Approved Expenditures

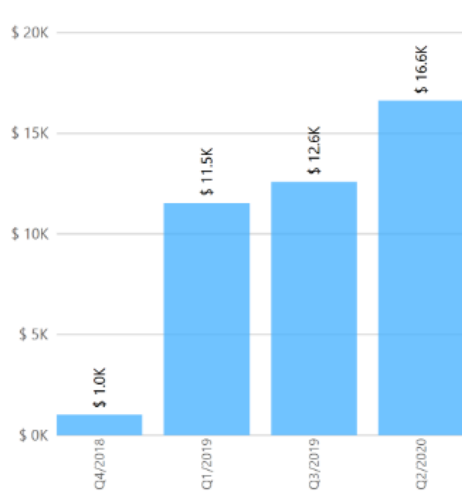

Adjustments



Cumulative Expenditures & Forecast

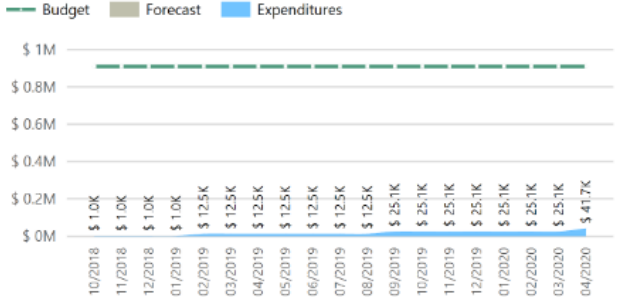

PROJECT DASHBOARD: SITE SCHEDULE

Task	Start	End	% Complete	2021		2022	
				Dec	Jan	Jan	Feb
New task	12/13/2021	12/19/2021	0%				
Mobilization	12/13/2021	12/13/2021	100%				
Grinding & Aspha	12/14/2021	12/22/2021	100%				
Demolition (front	12/17/2021	12/23/2021	100%				
Concrete (Front	12/23/2021	01/10/2022	0%				
Asphalt (Front)	01/04/2022	01/06/2022	0%				
Electrical	01/11/2022	02/01/2022	0%				
Plumbing	01/11/2022	02/01/2022	0%				
Striping	02/07/2022	02/08/2022	0%				
Railing	01/18/2022	01/24/2022	0%				
Low Voltage	01/19/2022	02/01/2022	0%				
Fire Aralrm	01/21/2022	01/31/2022	0%				
Painting	01/28/2022	02/04/2022	0%				
Signage	02/07/2022	02/08/2022	0%				
Cleaning	02/08/2022	02/09/2022	0%				
Punch Items	02/09/2022	02/18/2022	0%				

+ Add Task

Grandview Academy, Newton, Sparks MS

21st Century Classroom Projects APPROVED BY DSA

- Newton Middle School 6-30-21
- Grandview College Prep 6-30-21
- Sparks Middle School 6-30-21
- Scope review meetings with sites to gain stakeholder input per the Board's guidance at the Special Board Meeting


Re-Programing with Associations, Teachers and Principals

- Storage
- Furniture
- Technology

Preparing New Annual Contractor Pre-Qualifications Package

Project Status


Programming & Qualifying

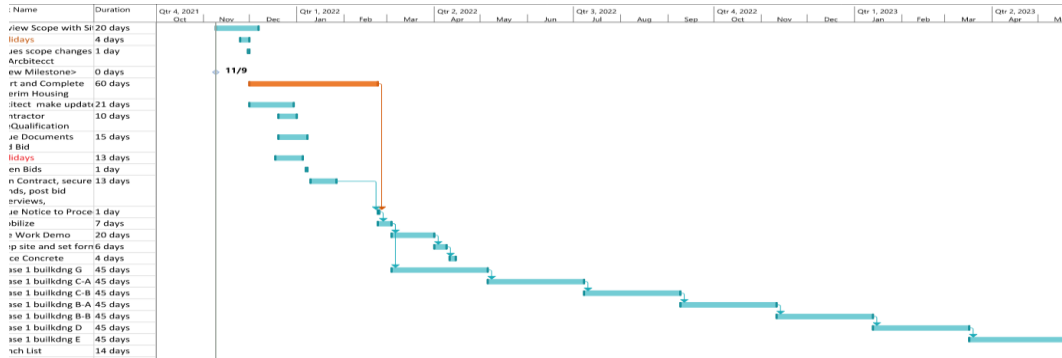

Newton 21st Century

Projected Schedule


3-23-22 to 6-30-23

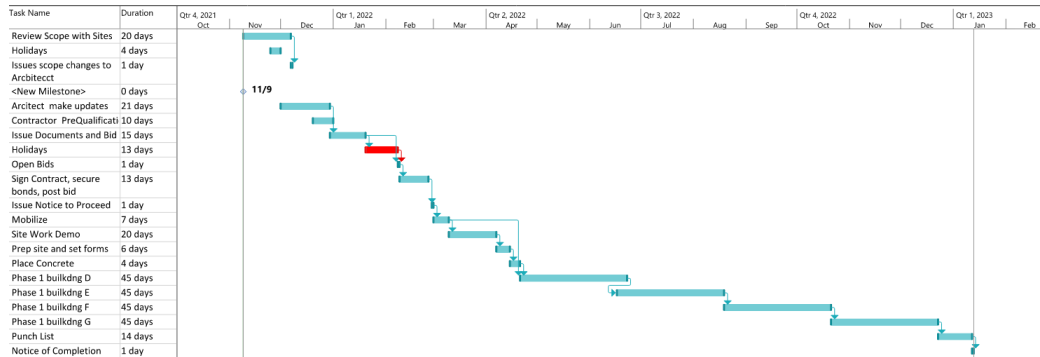

Sparks MS 21st Century

Projected Schedule


3-23-22 to 2-23-23

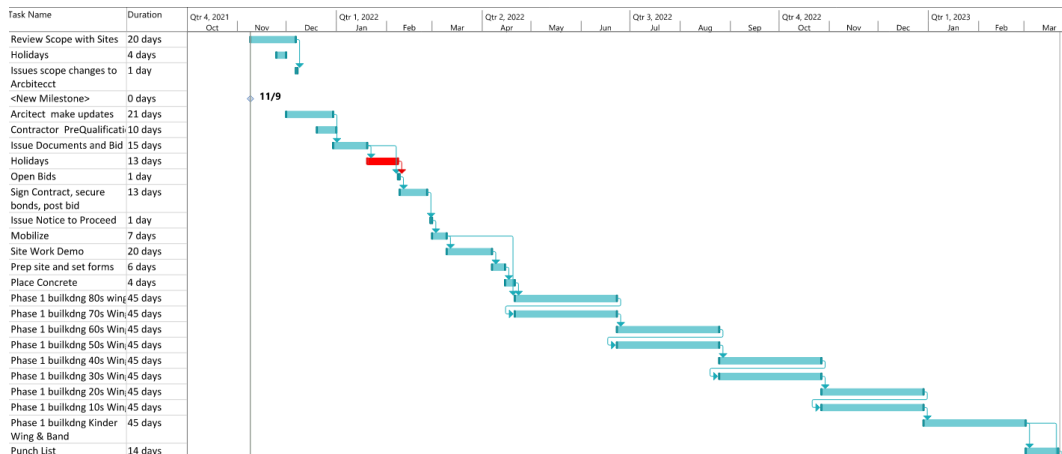

Grandview 21st Century

Projected Schedule

3-23-22 to 4-22-23



QUESTIONS + ANSWERS

CUMMING
Building Value Through Expertise
