






**21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2**  
**BOND UPDATES**  
September 24, 2020

# PROJECT STATUS

## MESA ROBLES SCHOOL



- 21st Century CR Modernization
- 21st Century CR New Construction
- Outdoor Learning
- Property Line
- Focus Area
- Existing Trees
- Admin/MR/Kitchen
- Outdoor Learning Play areas
- ES/SHade Structure
- Main Identity and Entrance
- Drop off Path
- Portables to remain CR
- Security Line
- Portables to remain

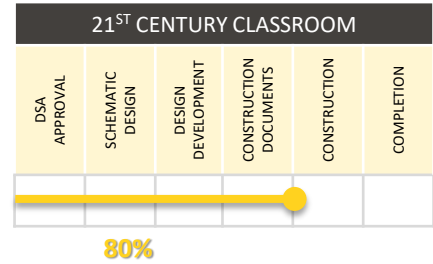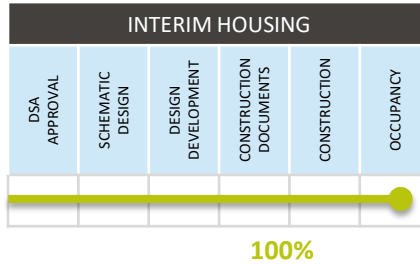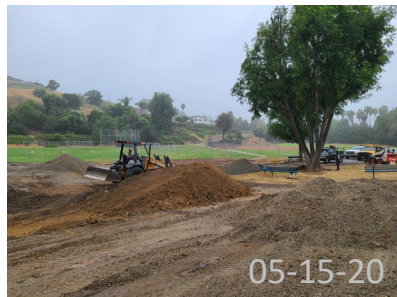

### NOTES:

- Interim Housing Construction Final Punch List 95% Complete
- Data installation complete; Fire Alarm installation in progress for serving both projects. DSA certification underway
- Interim Furnishing installed; Elementary Classrooms ready for move in.
- Construction Documents for the 21<sup>st</sup> Century Classroom Improvements in DSA Approved by DSA
- Prequalification of contractors complete
- Project **OUT TO BID**

# Interim Housing Construction Begins

## **MESA ROBLES SCHOOL**

### PROJECT KICK OFF & GROUND- BREAKING GRADING



GRADING FOR PAVING



PAVING FINISH GRADES

Interim Housing

# MESA ROBLES SCHOOL

## INFRASTRUCTURE AND UNDERGROUND



PREP AND PAVING COMPLETE



Interim Housing

# MESA ROBLES SCHOOL

## INFRASTRUCTURE AND UNDERGROUND



UTILITY PAD FORMS



NEW TRANSFORMER & GEAR SET

Interim Housing

# MESA ROBLES SCHOOL

BUILDINGS SET INTERIOR FINISHED  
POWER & DATA INSTALLED

## New Interim Housing Locations



Kindergarten Side

Interim Housing

# MESA ROBLES SCHOOL

BUILDINGS SET INTERIOR FINISHED  
POWER & DATA INSTALLED



New Permanent Dance & Choral



Middle School Side

# PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

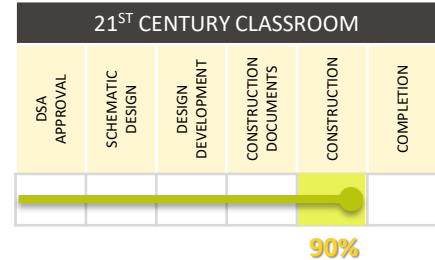

## NOTES:

- Interim Housing Project is 100% complete
- Furniture arrived on 6-12-20
- Interim housing ready to be occupied
- 21<sup>st</sup> Century Classroom Improvements Construction Notice to proceed on 6-8-20
- Site work and Construction nearing completion
- Phase 2 & 3 ran in tandem to complete ahead of schedule



PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

## CLASSROOM INTERIORS AND UTILITIES



POWER AND DATA



WALL & FLOOR FINISHES

PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL



SITE WORK AND ADA ACCESSIBLE PATH OF TRAVEL

PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

## CLASSROOM INTERIORS AND UTILITIES





WALL & FLOOR FINISHES



WALL & FLOOR FINISHES

# PROJECT STATUS

# NELSON ELEMENTARY SCHOOL

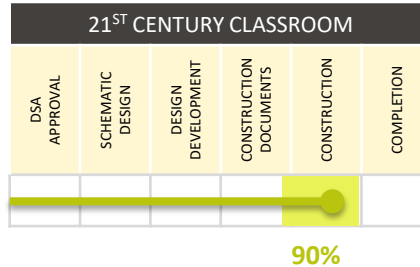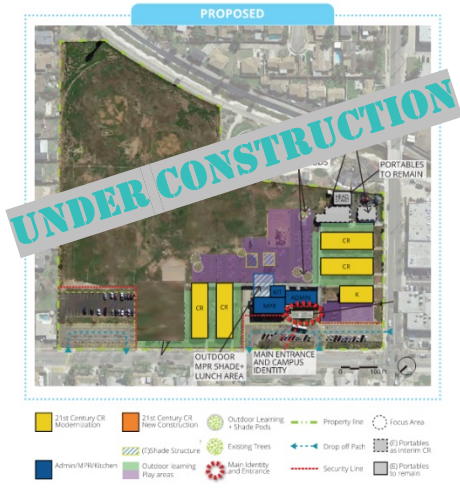

## NOTES:

- Room C-1 Pilot Classroom Complete
- 21<sup>st</sup> Century Classroom Improvements Construction Notice to proceed on 6-8-20
- Furniture arrived on 6-12-20 for C-1 and for 10 more Construction Phase 1 classrooms 7-30-20
- Construction Phases 2 and 3 nearing completion

PROJECT STATUS

# NELSON ELEMENTARY SCHOOL



1



2



3

PILOT ROOM C-1 COMPLETE



PROJECT STATUS



# NELSON ELEMENTARY SCHOOL



SITE WORK AND ADA ACCESSIBLE PATH OF TRAVEL

# PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL

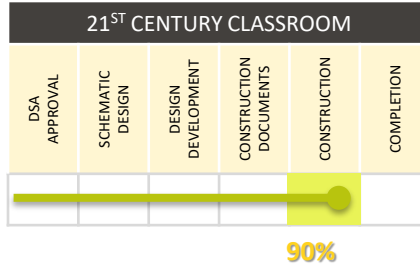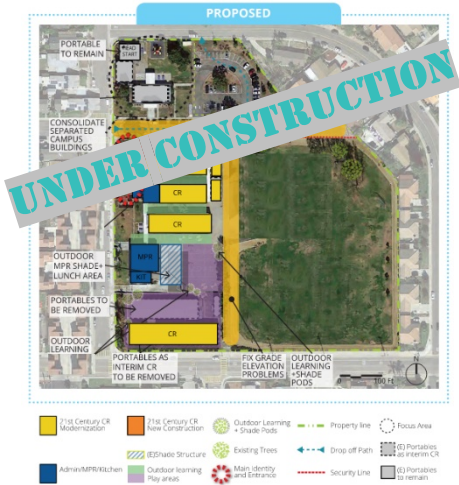

## NOTES:

- 21<sup>st</sup> Century Classroom Improvements started construction 6-15-2020; Construction Phases 2 & 3 in progress
- Site work paving installation completed
- Electrical rough-in 95% complete; Finish Electrical 85% complete
- Plumbing rough-in complete, Casework fabrication complete installed countertops in fabrication. Finish plumbing pending precursors
- Flooring installation complete permanent buildings, portables demo is 100% complete installation of new 33% complete
- Installation of tackable wall board is completed
- Painting at relocated classroom interiors underway

PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL



POWER AND DATA INTEGRATION



WALKWAYS BEFORE

PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL



WALKWAYS DEMOED



WALKWAYS DURING



WALKWAYS AFTER



PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL





FLOORS PROTECTED-WHILE NEW WALLS WERE INSTALLED THROUGHOUT CAMPUS



PROJECT STATUS

# CEDARLANE ACADEMY

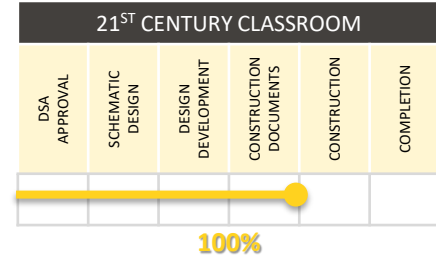
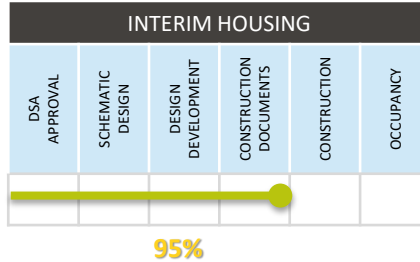


## NOTES:

- Construction Documents for the Interim Housing Project Submitted to DSA for review. DSA approval pending
- Construction Documents for the 21<sup>st</sup> Century Classroom Improvements in DSA Approved by DSA
- Prequalification of contractors complete
- Open DSA Applications resolved
- Project OUT TO BID

# PROJECT STATUS

# GRANDVIEW ACADEMY

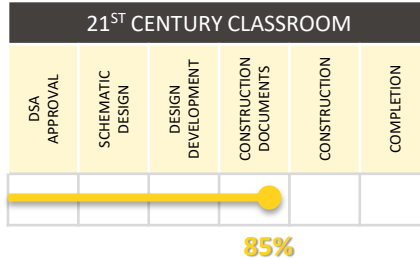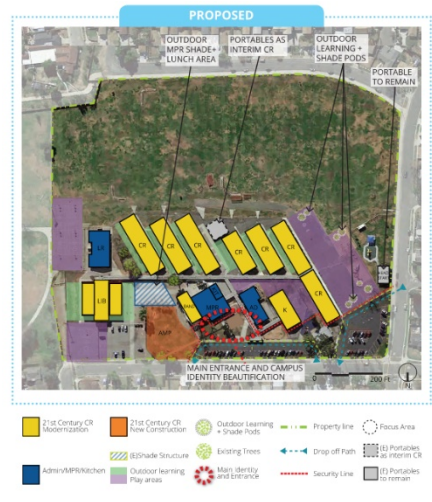

## NOTES:



- 21<sup>st</sup> Century Classroom Project construction documents are 85% complete
- DSA Submittal anticipated after Cumming and District review
- DSA Applications for Grandview are all closed with Certification

# PROJECT STATUS

## NEWTON MIDDLE SCHOOL



- 21st Century CR Modernization
- 21st Century CR New Construction
- Outdoor Learning + Shade Pods
- Property line
- Focus Area
- Admin/MPR/Other
- Existing Structure
- Existing Trees
- Drop off/Pick up
- Portables to remain CR
- Outdoor Learning Play areas
- Main Identity and Entrance
- Security Line
- Portables to remain




### NOTES:

- Interim Housing construction documents are DSA approved
- Temp power installation ready, contract awaiting contract with DSA Project Inspector
- Construction documents for the 21<sup>st</sup> Century Classroom Project are 85% complete; DSA Submittal anticipated in October after Cumming and District review
- Construction phase Documents received for review from Architect
- DSA approval contingent upon certification of (3) open DSA Applications


# PROJECT STATUS

## SPARKS MIDDLE SCHOOL

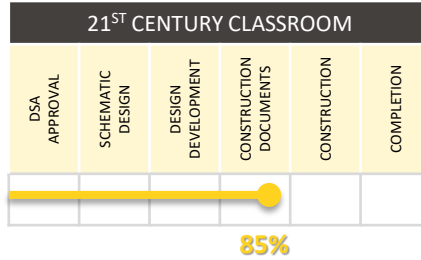

### NOTES:

- Construction Documents for the 21<sup>st</sup> Century Classroom Improvements are 85% complete
- DSA Submittal anticipated November after Cumming and District review
- DSA approval contingent upon certification of (3) open DSA Applications

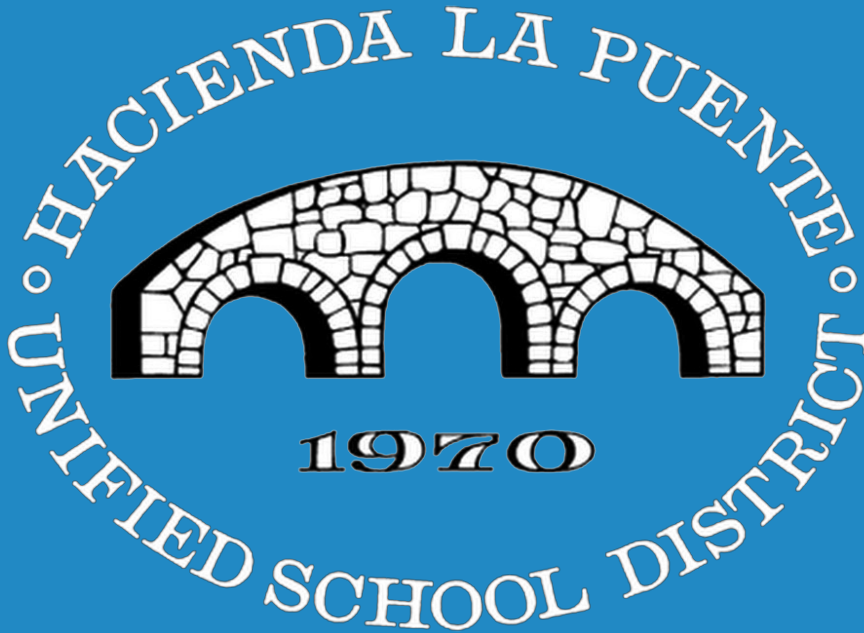

**QUESTIONS & ANSWERS**
