

LA PUENTE
UNIFIED SCHOOL DISTRICT
www.hipschools.org 626.933.1000

Welcome to the
Hacienda La Puente
Unified School District





21st CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2
BOND UPDATES

February 27, 2020

NELSON PILOT CLASSROOM: ROOM C-1 **CONSTRUCTION**

ACTION ITEMS

- Move out **COMPLETE**
- Pre-Construction project walk 12-20-2019 **COMPLETE**
- Color pallet planning and materials selection for three color schemes **IN FINAL REVIEW**
- Request for quotes 12-20-2019 **COMPLETE**
- Demo of Finishes **COMPLETED**
- Installation of Electrical Conduit for Systems
 - Fire Alarm
 - Data
 - Power
 - Signal

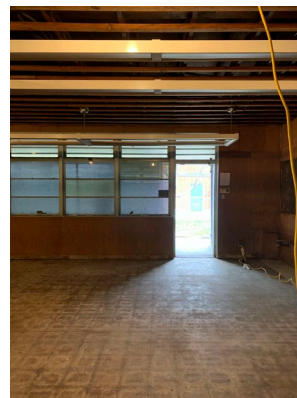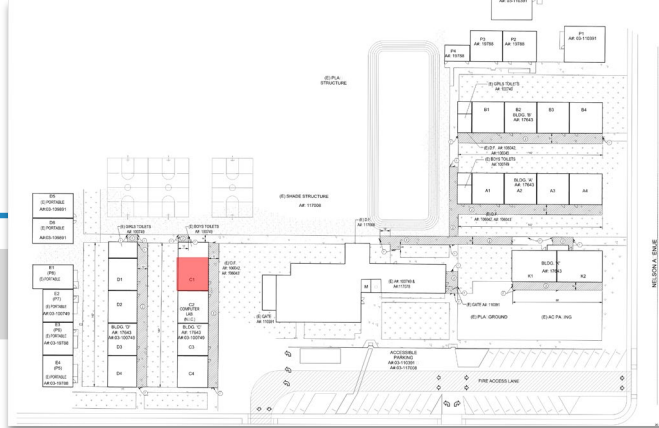

NELSON PILOT CLASSROOM: ROOM C-1

AFTER DEMOLITION



DEMOLITION OF FINISHES:
WALLS, FLOOR & CEILING REMOVED




21st Century Classroom Furnishings

SAMPLE FURNITURE

New furniture samples in the facilities office for review and test-drive

Lakeshore – People Space – Culver Newlin

Price Quotes Requested for 28 classrooms

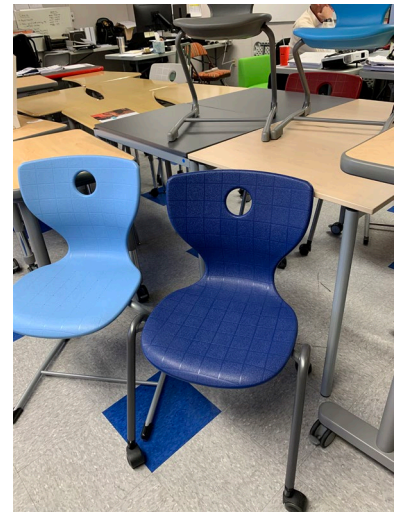

PROJECT STATUS

WORKMAN ELEMENTARY



Color Palette Sample Rooms




Set Up Planned For February 26, 2020
Viewing March 2, 2020

21st Century Classroom Improvements

WORKMAN ELEMENTARY

DSA Approved Construction Documents




PROJECT ADDRESS: 1500 WORKMAN STREET, LA PUENTE, CA 91744 PROJECT DESCRIPTION: 21st Century Classroom Improvements		WORKMAN ELEMENTARY SCHOOL 21st CENTURY CLASSROOMS HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT 1500 WORKMAN STREET, LA PUENTE, CA 91744		
PROJECT SUMMARY DESIGN OF BUILDING ARCHITECTURE DATE: 02/15/2017 DATE: 03/15/2017		GENERAL NOTES 1. ALL WORK SHALL CONFORM TO TITLE 24 CALIFORNIA CODE OF REGULATIONS... 2. ALL WORK SHALL CONFORM TO THE CALIFORNIA CODE OF REGULATIONS...		
GOVERNING AGENCIES THE PROJECT SHALL COMPLY WITH ALL FEDERAL, STATE AND LOCAL CODES... PERMITS: ACCESSORY USE PERMITS FOR BUILDINGS AND FACILITIES (ADUAG) STATE BUILDING PERMITS FOR BUILDING AND FACILITIES (ADUAG)		GENERAL NOTES 1. ALL WORK SHALL CONFORM TO TITLE 24 CALIFORNIA CODE OF REGULATIONS... 2. ALL WORK SHALL CONFORM TO THE CALIFORNIA CODE OF REGULATIONS...		
APPLICABLE CODES CALIFORNIA STATE BUILDING CODE (CSBC) - 2015 IBC WITH ALL AMENDMENTS... CALIFORNIA STATE ELECTRICAL CODE (CSEC) - 2014 NEC WITH ALL AMENDMENTS...		DEFERRED APPROVALS 001 ELECTRICAL GENERAL NOTES & SCHEDULES 002 GENERAL CONTRACTOR GENERAL NOTES 003 GENERAL CONTRACTOR GENERAL NOTES 004 GENERAL CONTRACTOR GENERAL NOTES		
ARCHITECT OF RECORD SVA ARCHITECTS 1500 WORKMAN STREET, LA PUENTE, CA 91744 TEL: 626-801-1100 FAX: 626-801-1101 WWW.SVA-ARCHITECTS.COM		NEIGHBORHOOD MAP 		OWNER: Hacienda La Puente Unified School District PROJECT NAME: Workman Elementary School - 21st Century Classrooms PROJECT NO.: 2016-0011 DATE: 02/15/2017 SCALE: GEN-1 PROJECT INFORMATION & SHEET INDEX
GENERAL CONFORMANCE STATEMENT I, the undersigned, certify that the construction documents herein were prepared by me or under my direct supervision and that I am a duly licensed architect in the State of California.		SHEET INDEX		

PROJECT STATUS

MESA ROBLES INTERIM HOUSING

New Interim Housing Locations

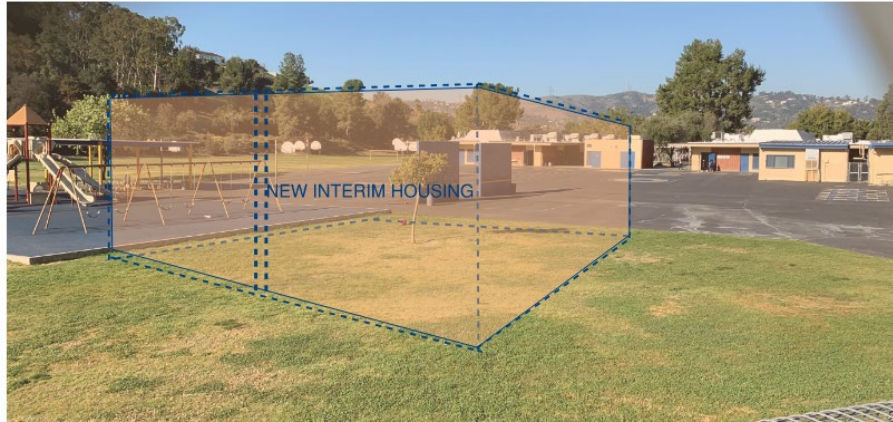


Kindergarten Side

21st Century Classroom Improvements **IN PROGRESS**



CLASSROOM FURNITURE, TECH, AND EQUIPMENT:

- Request for sound amplification test unit in Nelson C-1
- Procuring furnishings for Pilot Classroom
 - Phase 1 and Phase 2 classrooms
- Presentation of technology options to Associations, Curriculum, and Teachers on Special Assignment
- Developed performance specifications for key technology equipment
- New Technology, Furnishings and Voice Amplification Systems will require Professional Development-Training

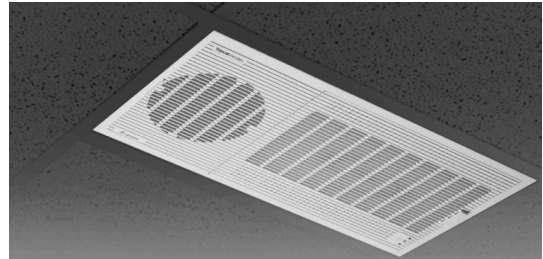

PROJECT STATUS

LOS ALTOS ELEMENTARY SCHOOL

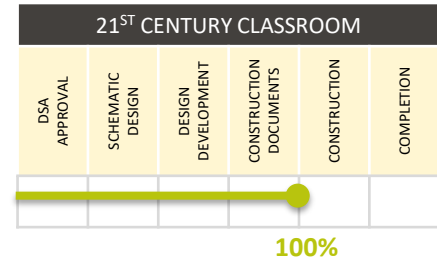
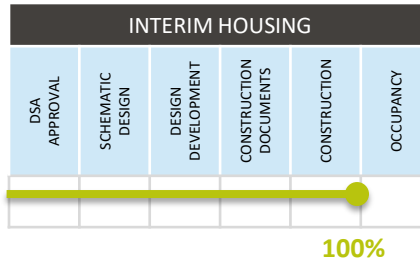


NOTES:

- 100% complete with construction of the Interim Housing Project
- Interim housing ready to be occupied
- 100% complete with construction documents for the 21st Century Classroom Project
- DSA backcheck appointment date awaiting certification of (4) open DSA Applications

PROJECT STATUS

NELSON ELEMENTARY SCHOOL

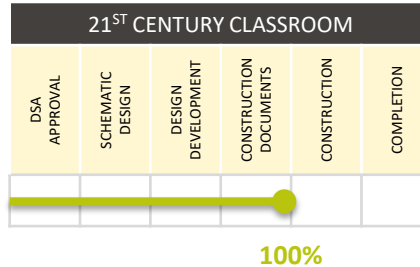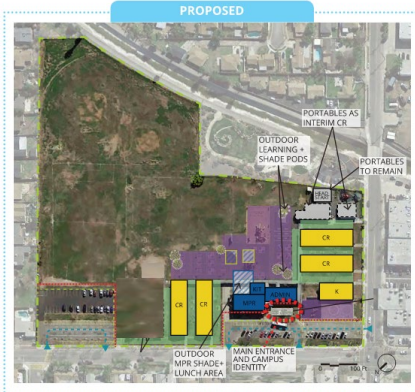


NOTES:

- 100% complete with construction documents for the 21st Century Classroom Project
- Room C-1 Pilot Classroom Construction in progress
- DSA backcheck appointment date awaiting certification of (1) open DSA Application

PROJECT STATUS

WORKMAN ELEMENTARY SCHOOL





100%

NOTES:

- 100% complete with construction documents for the 21st Century Classroom Project
- **DSA Approved Ready for Bid**

PROJECT STATUS

GRANDVIEW ACADEMY

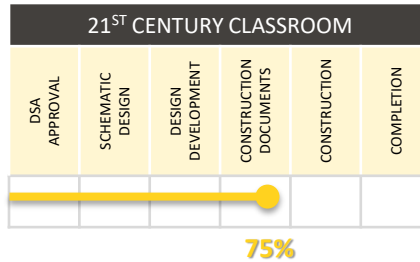
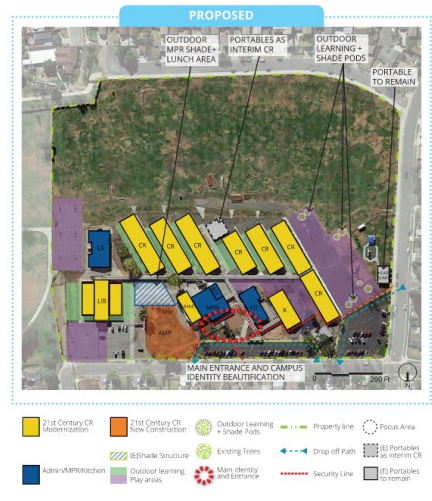


NOTES:

- 75% complete with construction documents for the 21st Century Classroom Project
- DSA Submittal in February anticipated Progress Meeting with Architect Scheduled 02-25-20
- DSA approval contingent upon certification of (3) open DSA Applications

PROJECT STATUS

NEWTON MIDDLE SCHOOL




NOTES:

- 100% complete with construction documents for the Interim Housing Project **Pre installation utilities application for temp power submitted to utility company. Quotes for site preparation requested from Unit Cost Contractors. Fire hydrant flow test completed.**
- 75% complete with construction documents for the 21st Century Classroom Project
- DSA Submittal in February anticipated **Progress meeting with architect scheduled 02-25-20**
- DSA approval contingent upon certification of (3) open DSA Applications

PROJECT STATUS

SPARKS MIDDLE SCHOOL



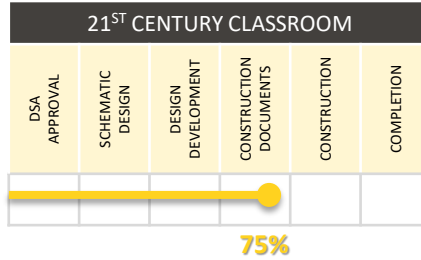


NOTES:

- 75% complete with Construction Documents for the 21st Century Classroom Improvements
- DSA Submittal anticipated In March DSA approval contingent upon certification of (3) open DSA Applications **Progress meeting with architect scheduled 02-25-20**

PROJECT STATUS

CEDARLANE ACADEMY

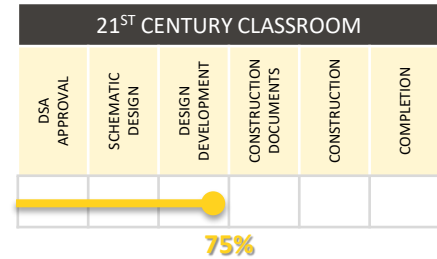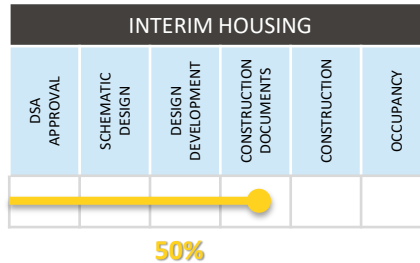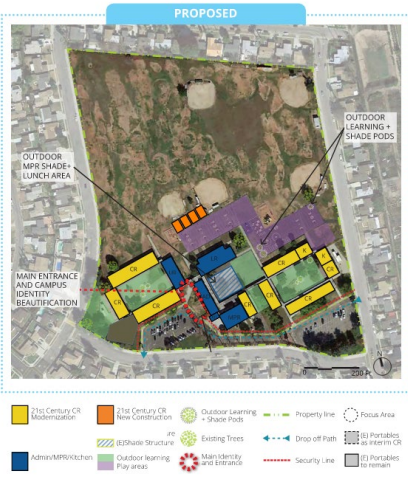


NOTES:


- 50% complete with Construction Documents for the Interim Housing Project. Milestone document set received. DSA appointment February 18, 2020. DSA returned drawings with comments. Architect to address next week 02-24-20
- 70% complete with Design Development for the 21st Century Classroom Project
- New fire hydrant with Suburban Water Systems for Design. Water company scope of work in for permitting.
- DSA approval contingent upon certification of (4) open DSA Applications

PROJECT STATUS

MESA ROBLES SCHOOL



100%




80%

NOTES:

- 100% complete with construction documents for the Interim Housing Project
- DSA approved Interim Housing on November 26, 2019
- Interim Housing construction proposals received, Requisitions for PO's next week 02-24-20 to 02-28-20
- 80% complete with Design Development for the 21st Century Classroom Improvements

21st Century Classroom Improvements **IN PROGRESS**



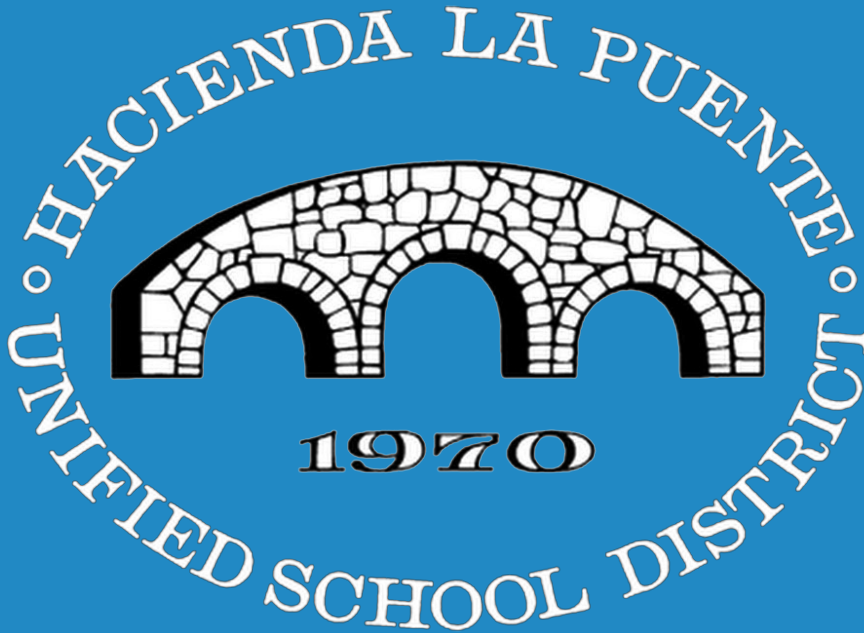

QUESTIONS & ANSWERS
