

# MEASURE BB BOND PROJECTS


**CUMMING**  
Building Value Through Expertise



21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2  
**BOND UPDATES**

June 24, 2021

PROJECT STATUS: **LOS ALTOS, NELSON & WORKMAN  
ELEMENTARY SCHOOLS**  
**PENDING FINAL DSA CLOSE OUT**

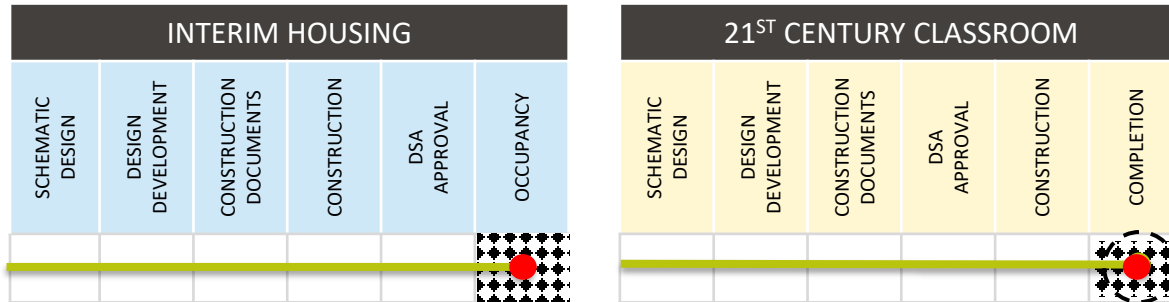

99%

NOTES:

- Interim Housing Project is 100% complete
- 21<sup>st</sup> Century
  - **Construction Complete**
  - Pending Final Close Out
  - **NCS Technology Installation On Going**

PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL



## EQUIPMENT INSTALLATION



CONSTRUCTION COMPLETE



PROJECT STATUS

# NELSON ELEMENTARY SCHOOL

NCS TECHNOLOGY INSTALLATION IN PROGRESS



CONSTRUCTION COMPLETE

PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

## NCS TECHNOLOGY INSTALLATION IN PROGRESS



CONSTRUCTION COMPLETE



## PROJECT STATUS

# MESA ROBLES SCHOOL

## UNDER CONSTRUCTION



INTERIM HOUSING					
SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION DOCUMENTS	CONSTRUCTION	DSA APPROVAL	OCCUPANCY

100% Complete

21 <sup>ST</sup> CENTURY CLASSROOM					
SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION DOCUMENTS	DSA APPROVAL	CONSTRUCTION	COMPLETION

75%


### NOTES:

- Interim Classrooms COMPLETE
- 21st Century Classroom Improvements
  - **Phase 1, AREA 1A and 2 COMPLETE**
  - School Moving Back into Completed Rooms
  - **AREA 3:** Accelerated Started March 8, 2021
  - **AREA 4:** Accelerated Started March 15, 2021
  - **AREA 5:** Accelerated Started April 27, 2021



## Interim Housing

# PHASING PLAN

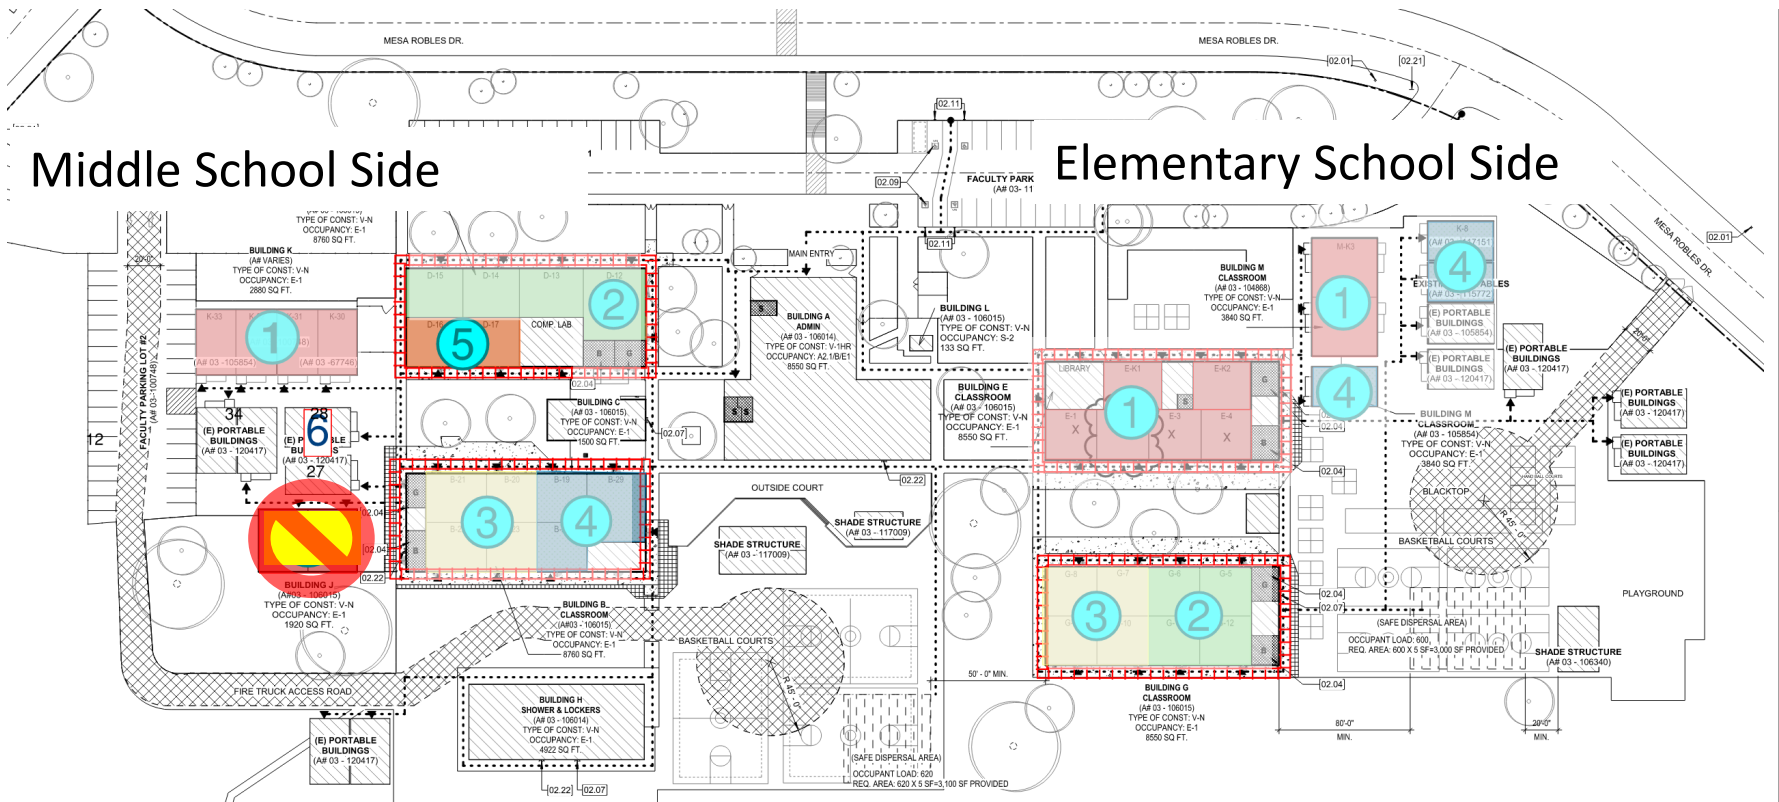

## CONSTRUCTION PHASE

Phase 3, 4, and 5 complete June 21, 2021

### Punch list June 22 to July 16



21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS

# MESA ROBLES SCHOOL


## DEMOLITION OF COMPROMISED PORTABLE



DURING



BEFORE



COMPLETE

CLASSROOM BUILDING J



# 21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS **MESA ROBLES SCHOOL**

**UNDER CONSTRUCTION**

**CLASSROOM IMPROVEMENTS AREAS 3, 4 & 5**



**FLOORING & FINISH PLUMBING**

**CUMMING**  
Building Value Through Expertise

21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS

# MESA ROBLES SCHOOL

**CONSTRUCTION COMPLETE WITH FURNITURE**



BEFORE



AFTER

CLASSROOM FURNISHING AND FINISHES

**CUMMING**  
Building Value Through Expertise

# CEDARLANE ACADEMY

**PROPOSED**

OUTDOOR MIKE SHADEN CUNYCH AREA

MAIN ENTRANCE AND CAMPUS IDENTIFICATION

OUTDOOR LEARNING & SHADE PODS



## 21<sup>ST</sup> CENTURY CLASSROOM

SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION DOCUMENTS	DSA APPROVAL	CONSTRUCTION	COMPLETION

60%

- Interim Housing Complete
- **Interior Phases 1 & 2 Complete**
- Demolition West Courtyard


- **Site Work Phase 3 Concrete Placed**
- **Site Work Phase 4 Walkway Prep Underway**
- Restroom Modifications Underway



# PROJECT STATUS

## CEDARLANE ACADEMY

### PHASING PLAN & INTERIM HOUSING

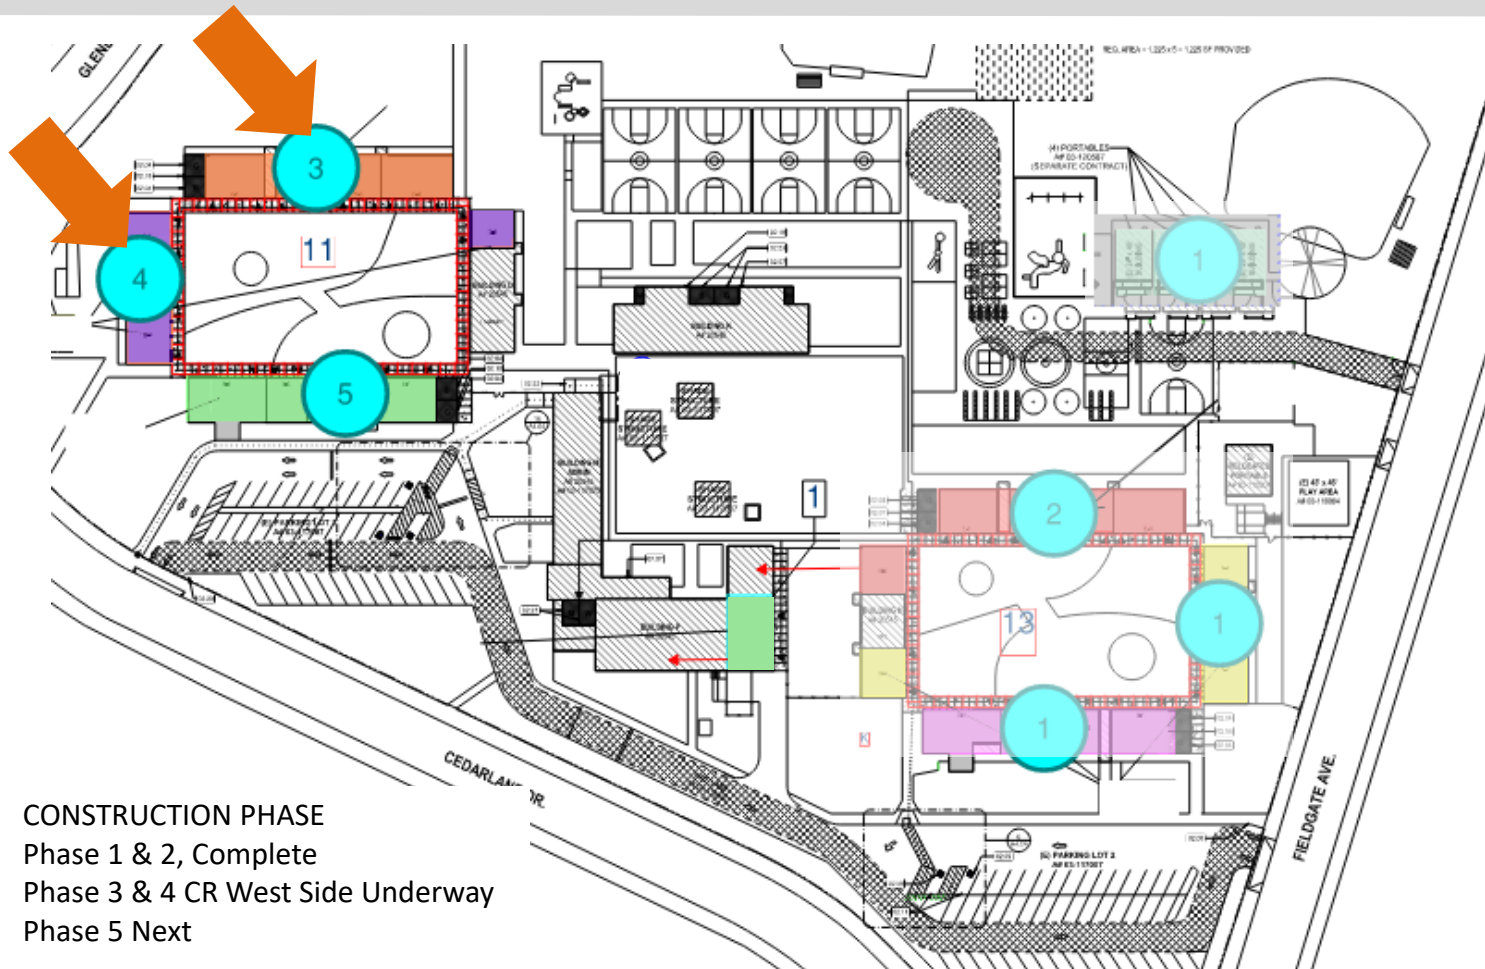

CONSTRUCTION PHASE  
Phase 1 & 2, Complete  
Phase 3 & 4 CR West Side Underway  
Phase 5 Next

21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS  
**CEDARLANE ACADEMY**  
**DEMOLITION AND FORMWORK**



3



4

SITE WORK WEST COURT YARD



PROJECT STATUS

# CEDARLANE ACADEMY

**PHASES 3 AND 4 OF 5 UNDER WAY**

## INTERIOR IMPROVEMENTS



Phase 3



Phase 4

CLASSROOM PREP FOR TACK BOARD




## PROJECT STATUS

# DSA PLAN REVIEW COMPLETE THIS MONTH

# GRANDVIEW ACADEMY NEWTON & SPARKS MIDDLE


Next Steps Bidding ✓

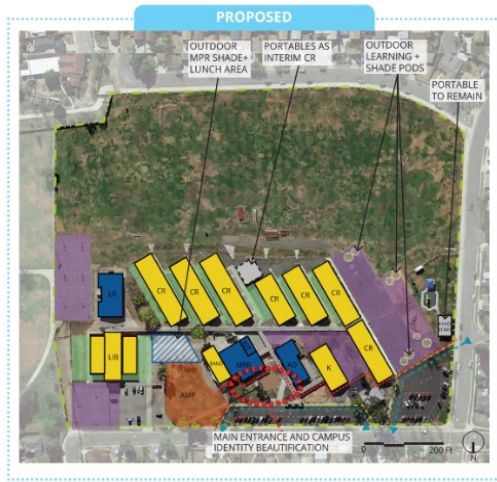

## NOTES:

- 21<sup>st</sup> Century Classroom Project Submitted to DSA
- DSA Project Inspector Assigned
- 21<sup>st</sup> Century Classroom Improvements
  - DSA Review Complete
  - Back Check Dates June 2 and 10, 2021
  - Bidding to Begin June 14, 2021





**QUESTIONS & ANSWERS**
