



School Site Improvement Projects

Business Services

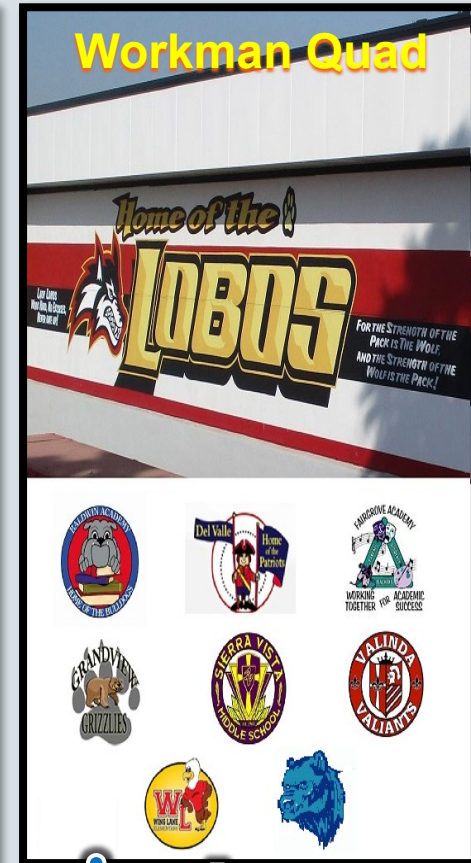



NEW!

2

Completed Projects

2020-2021



COMPLETED



Projects Completed as of June 24, 2021

Kwis – Ceiling Tiles & Lighting

3



Before



After





Projects Completed as of June 24, 2021

Los Robles – Ceiling Tiles & Lighting

4



Before



After





Projects Completed as of June 24, 2021

California – Fire Alarm

5







Projects Completed as of June 24, 2021

La Puente HS, Los Altos HS, Wilson HS, Workman HS (Gym) – Live Streaming Cameras

6

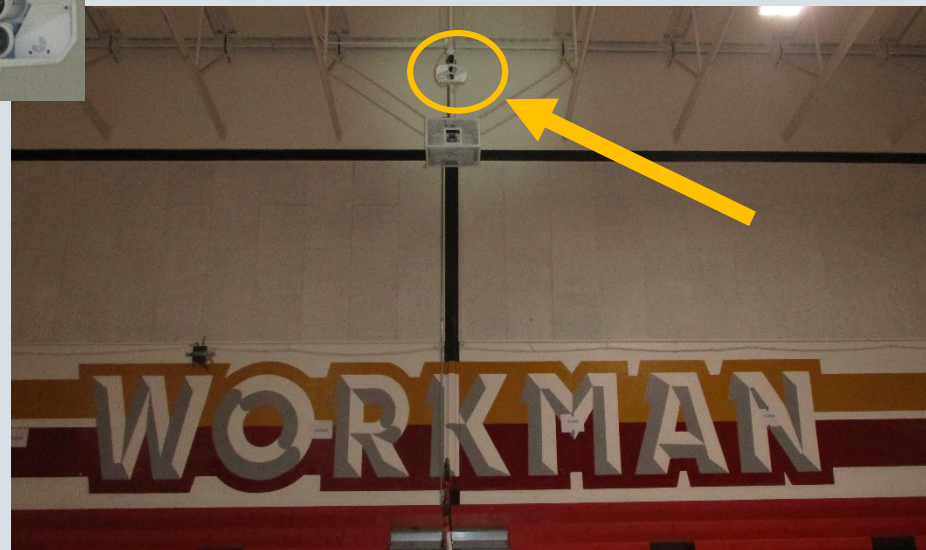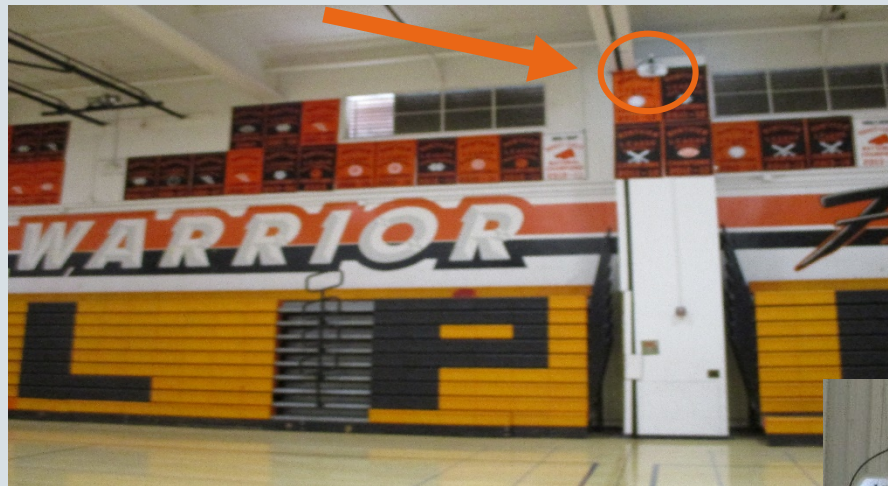



Projects Completed as of June 24, 2021

District Office – Solar Panel Arrays Installed

(Tie in pending and target date is scheduled for Mid-August 2021)



7





Projects Completed as of June 24, 2021

La Puente HS – Solar Panel Arrays Installed
(Tie in pending and target date is scheduled for Mid-August 2021)



8





Projects Completed as of June 24, 2021

ISO – Aire (Classroom)



9



UPDATE

Status: La Puente HS – Water Leak

**** (Estimated target date to be completed is Saturday June 19, 2021) ****

10



11

Projects In Progress


2020-2021



Projects In Progress as of June 24, 2021

12

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Cedarlane K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	Bond	7/30/2021
Mesa Robles K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	Bond	7/30/2021
Willow AS	Conference (South) Room Renovation	Complete	N/A	Complete	In Progress	Adult Ed.	7/30/2021
Bixby	Ceiling Tiles	N/A	N/A	N/A	In Progress	Bond	8/1/2021
Wilson HS	Fire Alarms	Complete	Complete	Complete	In Progress	Bond	8/1/2021

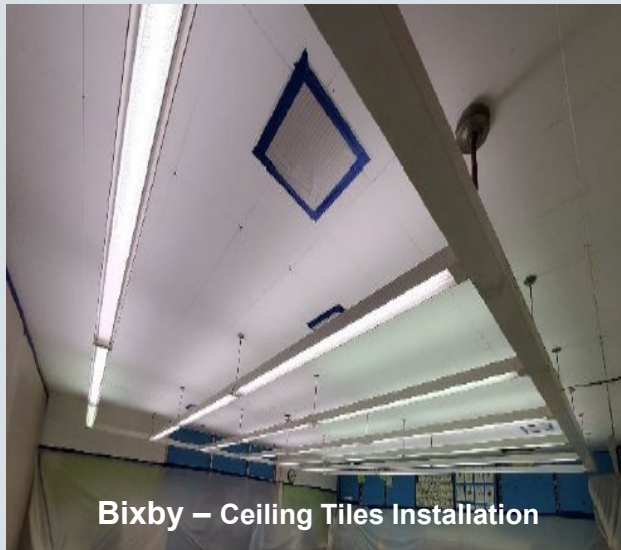

Bixby – Ceiling Tiles Installation



La Puente HS Locker Room – Lay down Rebar for concrete slab




La Puente HS Locker Room: Concrete slab was poured

Changes And Progress Since Last Report - Blue

Projects In Progress as of June 24, 2021

13

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Facilities	12/31/2021
Wilson HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Facilities	12/31/2021
Bixby	Lighting	N/A	N/A	N/A	In Progress	Bond	8/1/2021
La Puente HS	New Kitchen	Complete	Complete	Complete	In Progress	Facilities	12/21/2021
Wilson HS	Pool Heater (Install)	N/A	N/A	N/A	In Progress	Facilities	6/30/2021
La Puente HS	Pool Project	Complete	Complete	Complete	In Progress	Facilities	8/9/2021

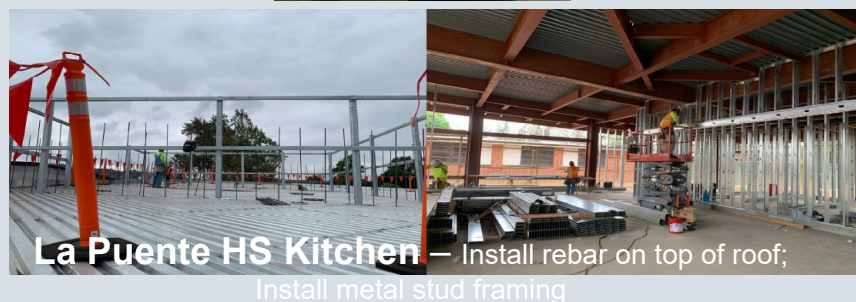


Changes And Progress Since Last Report - Blue

Projects In Progress as of June 24, 2021

14

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Cedarlane	Roofing Restoration	N/A	N/A	N/A	In Progress	Facilities	6/30/2021
Nelson ES	Roofing Restoration (Bldg: E)	N/A	N/A	N/A	In Progress	Facilities	6/30/2021
Newton MS	Roofing Restoration (Bldg: D, Band Room)	N/A	N/A	N/A	In Progress	Facilities	7/15/2021
Sparks MS	Roofing Restoration (Rm 1-4/21-23/CL)	N/A	N/A	N/A	In Progress	Facilities	6/30/2021
Workman ES	Roofing Restoration (Cafeteria)	N/A	N/A	N/A	In Progress	Facilities	7/15/2021

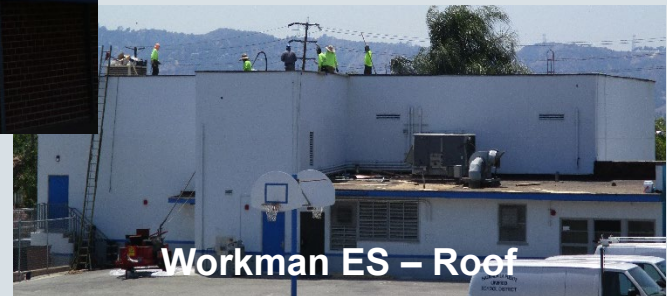

Changes And Progress Since Last Report - Blue

Projects In Progress – Pending Construction Schedule as of June 24, 2021

15

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Fairgrove K-8	Bottle Filling Stations	Complete	Complete	Complete		Bond	7/30/2021
Grandview	Roofing Restoration (Wing10/20/Library/Office/PE)	N/A	N/A	N/A		Facilities	6/30/2021
Workman ES	Roofing Restoration (Rm:13-17)	N/A	N/A	N/A		Facilities	6/30/2021

- AMAR CHILDREN CENTER
- CEDARLANE ACADEMY*
- DEL VALLE
- FAIRGROVE**
- GRANDVIEW**
- KWIS ELEMENTARY
- LA PUENTE HIGH SCHOOL
- LOS ALTOS HIGH SCHOOL**
- LOS ROBLES ACADEMY
- NELSON ELEMENTARY*
- NEWTON MIDDLE*
- ORANGE GROVE MIDDLE
- PALM ELEMENTARY
- SPARKS ELEMENTARY**
- SPARKS MIDDLE *

- VALLEY HS
- WILSON HS
- WING LANE ELEMENTARY
- WORKMAN ELEMENTARY*
- WORKMAN HS

Legend:

* IN PROGRESS

** PENDING SCHEDULES









*** PENDING SCHEDULES 2021-2022

Changes And Progress Since Last Report - Blue

Projects In Progress as of June 24, 2021



16

Site		Item Description		Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Los Altos HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	6/30/2021
Willow		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	7/30/2021
Wilson HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	7/30/2021
Workman HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	6/30/2021

Los Altos HS – Solar Panels Installed



Willow AS – Solar Panels Structure installed



Wilson HS – Solar Panels Structure Installed




Workman HS – Electrical Panels Installed



Changes And Progress Since Last Report - Blue

Projects **READY FOR PROCUREMENT**



17

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Baldwin	Bottle Filling Stations	Complete	Complete			8/1/2021
Bixby	Bottle Filling Stations	Complete	Complete			8/1/2021
California	Bottle Filling Stations	Complete	Complete			8/1/2021
Del Valle	Bottle Filling Stations	Complete	Complete			8/1/2021
Dibble AS	Bottle Filling Stations	Complete	Complete			8/1/2021
District Office	Bottle Filling Stations	Complete	Complete			8/1/2021
Grandview K-8	Bottle Filling Stations	Complete	Complete			8/1/2021
Grazide	Bottle Filling Stations	Complete	Complete			8/1/2021
Hudson AS	Bottle Filling Stations	Complete	Complete			8/1/2021
Kwis ES	Bottle Filling Stations	Complete	Complete			8/1/2021
La Puente HS	Bottle Filling Stations	Complete	Complete			8/1/2021
Lassalette K-8	Bottle Filling Stations	Complete	Complete			8/1/2021
Los Robles	Bottle Filling Stations	Complete	Complete			8/1/2021



Changes And Progress Since Last Report - Blue

Projects **READY FOR PROCUREMENT & In Progress**

18

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Newton	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Palm ES	Bottle Filling Stations	Complete	Complete			Bond	7/1/2021
Sparks ES	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Stimson LC	Bottle Filling Stations	Complete	Complete			Bond	7/1/2021
Wedgeworth	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Wilson HS	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Wing Lane	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Workman ES	Bottle Filling Stations	Complete	Complete			Bond	8/1/2021
Grazide	Exterior Painting	N/A	N/A			Facilities	8/1/2021
Dibble AS	Fire Alarms	Complete	N/A			Facilities	8/1/2021
District Office	Fire Alarms	Complete	N/A			Facilities	8/1/2021
La Puente HS	Fire Alarms	Complete	Complete			Bond	8/1/2021
Willow AS	Fire Alarms	Complete	Complete			Adult Ed.	8/15/2021
Workman HS	Fire Alarms	Complete	Complete			Bond	8/1/2021
Grazide ES	Perimeter Wall Replacement	In Progress	N/A	In Progress		Facilities	6/30/2021

GRAZIDE UPDATE

❖ Soils Test Findings





Projects with Division of State Architect (DSA) Waiting on Approval

19

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Workman HS	Artificial Track and Field Phase II (Submitted to DSA. (PENDING CEQA))	Complete	Complete			7/1/2021
Orange Grove	Bottle Filling Stations	Complete	In Progress			7/1/2021
Palm Canyon	Bottle Filling Stations	Complete	Complete			7/1/2021
Sierra Vista	Bottle Filling Stations	Complete	In Progress			7/1/2021
Sparks MS	Bottle Filling Stations	Complete	Complete			7/1/2021
Valinda	Bottle Filling Stations	Complete	Complete	Complete	In Progress	7/1/2021
Valley HS	Bottle Filling Stations	Complete	In Progress			7/1/2021
Willow AS	Bottle Filling Stations	Complete	In Progress			7/1/2021
Workman HS	Bottle Filling Stations	Complete	Complete	Complete	In Progress	7/1/2021
Wedgeworth	Permanent School	Complete	In Progress			



Projects in Design

20

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Los Altos HS	Fire Alarms	Complete				8/1/2021
Los Altos HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Workman HS	Gym & Locker Room HVAC	In Progress				8/1/2021



Changes And Progress Since Last Report - Blue

Projects **PENDING REVIEW**

21

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Lassalette K-8	Front Landscape	In Progress				Pending
Sparks MS	Front Landscape	In Progress				Pending
Workman ES	Front Landscape	In Progress				Pending
Baldwin	Irrigation Replacement	In Progress				Pending
Bixby	Irrigation Replacement	In Progress				Pending
Cedarlane K-8	Irrigation Replacement	Complete	N/A			Pending
Del Valle	Irrigation Replacement	Complete	Complete			Pending
Fairgrove K-8	Irrigation Replacement	In Progress				Pending
Grazide	Irrigation Replacement	In Progress	N/A			Pending
Sierra Vista	Irrigation Replacement	Complete	Complete			Pending
La Puente HS	Music Room Upgrades	N/A	N/A			Pending
Wilson HS	Music Room Upgrades	N/A	N/A			Pending
California	New Rubberized Playground/New Swings	N/A	N/A			Pending
Del Valle	Office entry doors and gates	Complete	Complete			Pending
Sparks ES	Office entry doors and gates	Complete	In Progress			Pending
Valinda	Office entry doors and gates	In Progress				Pending
District Office	Phase II HVAC Replacement	Complete	Complete			Pending
Amar	Shade Structure - New	Complete	Complete			Pending
Willow AS	Two-Story Building Renovation (Bldg D)	In Progress	N/A			Pending
Willow AS	Fire Alarm	In Progress	Complete			

Changes And Progress Since Last Report - Blue



PROJECT COMPLETE LIST



22

SLIDE 1 OF 2

Site	Item Description
La Puente HS	Air Purification in Gym
Los Altos HS	Air Purification in Gym
Wilson HS	Air Purification in Gym
Workman HS	Air Purification in Gym
Workman HS	Artificial Track and Field Phase I
District Office	Battery Back Up System
Amar CC	Bottle Filling Stations (Attached to Shade Structure Close Out)
Los Altos HS	Bottle Filling Stations (Attached to Shade Structure Close Out)
Mesa Robles K-8	Bottle Filling Stations (Attached to Shade Structure Close Out)
Nelson ES	Bottle Filling Stations
Sunset	Bottle Filling Stations
Wing Lane	Bottle Filling Stations (Attached to Shade Structure Close Out)
Baldwin	Ceiling Tiles
California	Ceiling Tiles
Del Valle	Ceiling Tiles
Los Altos ES	Ceiling Tiles
Los Molinos	Ceiling Tiles
Palm	Ceiling Tiles
Sunset ES	Ceiling Tiles
Nelson	Ceiling Tiles
Sparks ES	Ceiling Tiles

Site	Item Description
Wing Lane	Ceiling Tiles
Workman ES	Ceiling Tiles
Valinda	Concrete and New Gates
Los Altos	Concrete Pads
Willow AS	Concrete Replacement – Lunch Area
Willow AS	Conference (North) Room Renovation
California	Exterior Painting
Palm ES	Exterior Painting
Sparks ES	Exterior Painting
Sparks MS	Exterior Painting
Wing Lane	Exterior Painting
Workman HS	Exterior Painting
Cedarlane K-8	Fire Alarms
Grandview	Fire Alarms
Los Altos ES	Fire Alarms
Mesa Robles	Fire Alarms
Nelson	Fire Alarms
Newton	Fire Alarms
Sparks MS	Fire Alarms
Valley HS	Fire Alarms

PROJECT COMPLETE LIST



23

SLIDE 2 OF 2

Site	Item Description
Workman ES	Fire Alarms
Los Molinos	Floor Replacement - Interior Hallways
Wilson HS	Floor Replacement - D9, D12 Carpets
Workman HS	Front Entry Gate
La Puente HS	Front Office Flooring
La Puente HS	Front Office Painting
Los Molinos	Hallway Flooring and Painting
Cedarlane K-8	Head Start Shade Structure Installation
All Sites	HVAC Assessment
Los Altos ES	Interim Housing
Mesa Robles	Interim Housing & Permanent Portables
Lassalette	Kinder Reroof
Willow AS	Kitchen Remodel
Baldwin	Lighting (Ceiling)
Del Valle	Lighting (Ceiling)
Sparks ES	Lighting (Ceiling)
Los Altos ES	Lighting (Ceiling)
Workman ES	Lighting (Ceiling)
Grazide	MPR Lighting
Kwis	MPR Lighting
Los Altos ES	MPR Lighting
Los Molinos	MPR Lighting
Los Robles	MPR Lighting
Nelson	MPR Lighting

Site	Item Description
Palm	MPR Lighting
Sparks ES	MPR Lighting
Sunset	MPR Lighting
Temple	MPR Lighting
Wing Lane	MPR Lighting
Amar	New Furniture Replacement
All Preschool	New Furniture Round 1 (Baldwin, California, Lassalette, Sparks ES, Sunset, Temple)
All Preschool	New Furniture Round 2 (Bixby, Cedarlane, Del Valle, Grandview, Valinda, Workman ES)
All Preschool	New Furniture Round 3 (Fairgrove, Kwis, Nelson, Palm, Wing Lane)
Workman ES	Office Entry Doors and Gates
Wilson HS	Photoshop Renovation
Los Altos HS	Re-Stripping of Tracks (Warranty Work)
Wilson HS	Re-Stripping of Tracks (Warranty Work)
Willow AS	Restroom Renovation
Grandview K-8	Roof Replacement
Nelson	Roofing (Building A/B/C/K1-K2)
Los Molinos	Room 6 – 21 st Century Remodel
Valinda	Shade Structure Concrete
Sunset	Shade Structure Demolition
Nelson	Synthetic Turf Installation
La Puente HS	Track Re-Surface
Palm	Wall Repainting
Nelson	21 st Century Sample Classroom



21st CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2
BOND UPDATES
