





21st CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2
BOND UPDATES
September 24, 2020

PROJECT STATUS

MESA ROBLES SCHOOL




100%



80%

NOTES:

- Interim Housing Construction Final Punch List 95% Complete
- Data installation complete; Fire Alarm installation in progress for serving both projects. DSA certification underway
- Interim Furnishing installed; Elementary Classrooms ready for move in.
- Construction Documents for the 21st Century Classroom Improvements in DSA Approved by DSA
- Prequalification of contractors complete
- Project **OUT TO BID**

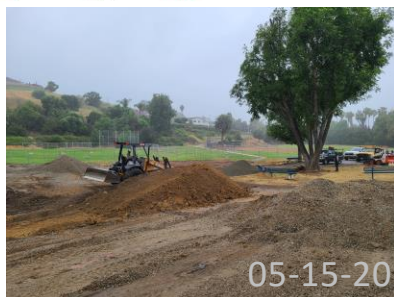

Interim Housing Construction Begins **MESA ROBLES SCHOOL**

PROJECT KICK OFF & GROUND- BREAKING GRADING



GRADING FOR PAVING



PAVING FINISH GRADES

Interim Housing

MESA ROBLES SCHOOL

INFRASTRUCTURE AND UNDERGROUND



PREP AND PAVING COMPLETE

Interim Housing

MESA ROBLES SCHOOL

INFRASTRUCTURE AND UNDERGROUND



UTILITY PAD FORMS



NEW TRANSFORMER & GEAR SET

Interim Housing

MESA ROBLES SCHOOL

BUILDINGS SET INTERIOR FINISHED
POWER & DATA INSTALLED

New Interim Housing Locations



Kindergarten Side

Interim Housing

MESA ROBLES SCHOOL

BUILDINGS SET INTERIOR FINISHED
POWER & DATA INSTALLED



New Permanent Dance & Choral



Middle School Side

PROJECT STATUS

LOS ALTOS ELEMENTARY SCHOOL

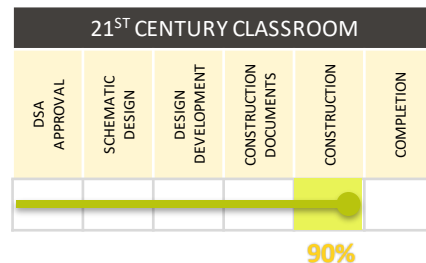


NOTES:

- Interim Housing Project is 100% complete
- Furniture arrived on 6-12-20
- Interim housing ready to be occupied
- 21st Century Classroom Improvements Construction Notice to proceed on 6-8-20
- Site work and Construction nearing completion
- Phase 2 & 3 ran in tandem to complete ahead of schedule

PROJECT STATUS

LOS ALTOS ELEMENTARY SCHOOL

CLASSROOM INTERIORS AND UTILITIES

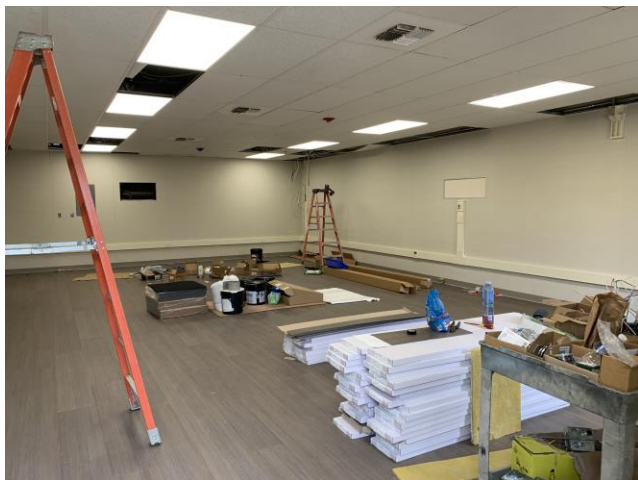


POWER AND DATA



WALL & FLOOR FINISHES

PROJECT STATUS

LOS ALTOS ELEMENTARY SCHOOL

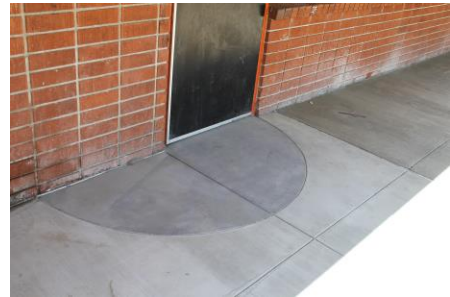

SITE WORK AND ADA ACCESSIBLE PATH OF TRAVEL

PROJECT STATUS

LOS ALTOS ELEMENTARY SCHOOL

CLASSROOM INTERIORS AND UTILITIES




WALL & FLOOR FINISHES



WALL & FLOOR FINISHES

PROJECT STATUS

NELSON ELEMENTARY SCHOOL

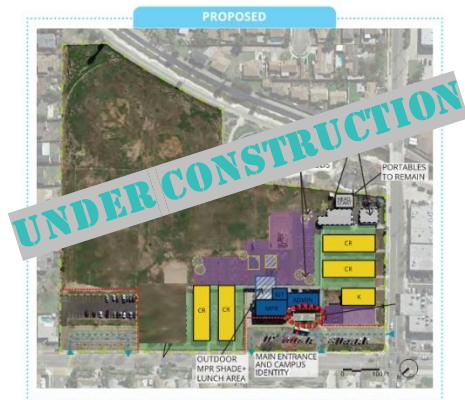

21 ST CENTURY CLASSROOM						
DSA APPROVAL	SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION DOCUMENTS	CONSTRUCTION	COMPLETION	

90%

NOTES:

- Room C-1 Pilot Classroom Complete
- 21st Century Classroom Improvements Construction Notice to proceed on 6-8-20
- Furniture arrived on 6-12-20 for C-1 and for 10 more Construction Phase 1 classrooms 7-30-20
- Construction Phases 2 and 3 nearing completion

PROJECT STATUS

NELSON ELEMENTARY SCHOOL



1



2



3

PILOT ROOM C-1 COMPLETE


PROJECT STATUS

NELSON ELEMENTARY SCHOOL



SITE WORK AND ADA ACCESSIBLE PATH OF TRAVEL

WORKMAN ELEMENTARY SCHOOL

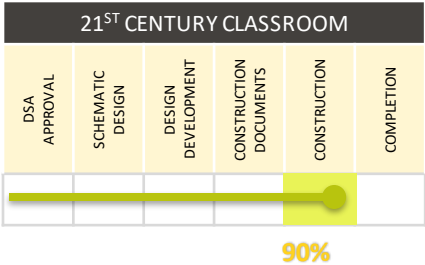

NOTES:

- 21st Century Classroom Improvements started construction 6-15-2020; Construction Phases 2 & 3 in progress
- Site work paving installation completed
- Electrical rough-in 95% complete; Finish Electrical 85% complete
- Plumbing rough-in complete, Casework fabrication complete installed countertops in fabrication. Finish plumbing pending precursors
- Flooring installation complete permanent buildings, portables demo is 100% complete installation of new 33% complete
- Installation of tackable wall board is completed
- Painting at relo classroom interiors underway

PROJECT STATUS

WORKMAN ELEMENTARY SCHOOL



POWER AND DATA INTEGRATION



WALKWAYS BEFORE

PROJECT STATUS

WORKMAN ELEMENTARY SCHOOL



WALKWAYS DEMOED



WALKWAYS DURING



WALKWAYS AFTER



PROJECT STATUS

WORKMAN ELEMENTARY SCHOOL



FLOORS PROTECTED-WHILE NEW WALLS WERE INSTALLED THROUGHOUT CAMPUS

CEDARLANE ACADEMY

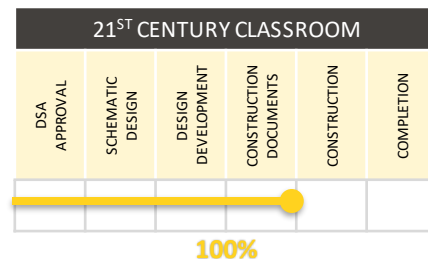
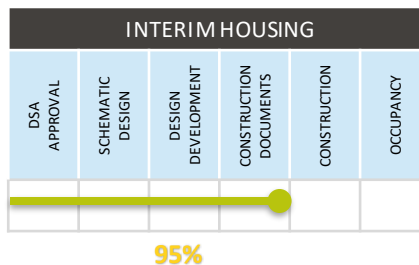


NOTES:

- Construction Documents for the Interim Housing Project Submitted to DSA for review. DSA approval pending
- Construction Documents for the 21st Century Classroom Improvements in DSA Approved by DSA
- Prequalification of contractors complete
- Open DSA Applications resolved
- Project OUT TO BID

PROJECT STATUS

GRANDVIEW ACADEMY

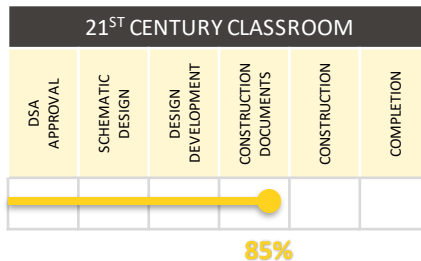
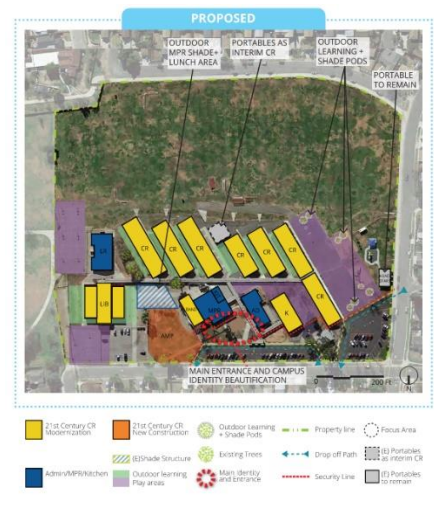


NOTES:

- 21st Century Classroom Project construction documents are 85% complete
- DSA Submittal anticipated after Cumming and District review
- DSA Applications for Grandview are all closed with Certification

PROJECT STATUS

NEWTON MIDDLE SCHOOL




NOTES:

- Interim Housing construction documents are DSA approved
- Temp power installation ready, contract awaiting contract with DSA Project Inspector
- Construction documents for the 21st Century Classroom Project are 85% complete; DSA Submittal anticipated in October after Cumming and District review
- Construction phase Documents received for review from Architect
- DSA approval contingent upon certification of (3) open DSA Applications


PROJECT STATUS

SPARKS MIDDLE SCHOOL

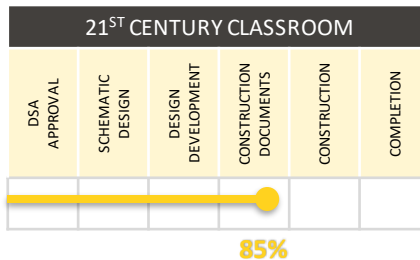

NOTES:

- Construction Documents for the 21st Century Classroom Improvements are 85% complete
- DSA Submittal anticipated November after Cumming and District review
- DSA approval contingent upon certification of (3) open DSA Applications

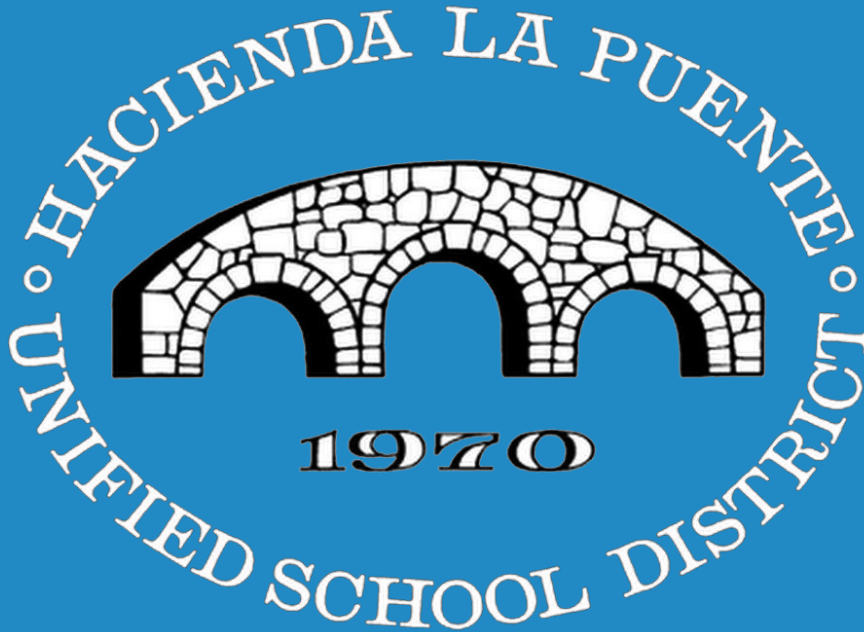

QUESTIONS & ANSWERS
