



FAYETTE COUNTY PUBLIC SCHOOLS

Update on FCPS Construction/Renovation Projects

August 2022



Tates Creek High – New Construction

- Architect: Tate Hill Jacobs Architects
- General Contractor: D.W.Wilburn, Inc.
- GC Contract Sum: \$70,971,000.00
- Total Project Cost: \$84,570,295.16
- Change Orders to Date (30): \$1,830,731.03
 - Scheduled Contract Completion Date: July 2022 (Building)
November 2022 (Site)
- % of Contract Completed: 96%
 - Revised Completion Date per GC: No Change

Tates Creek High – New Construction


Aerial View



August 2022

Tates Creek High – New Construction


Completed Site Plan View

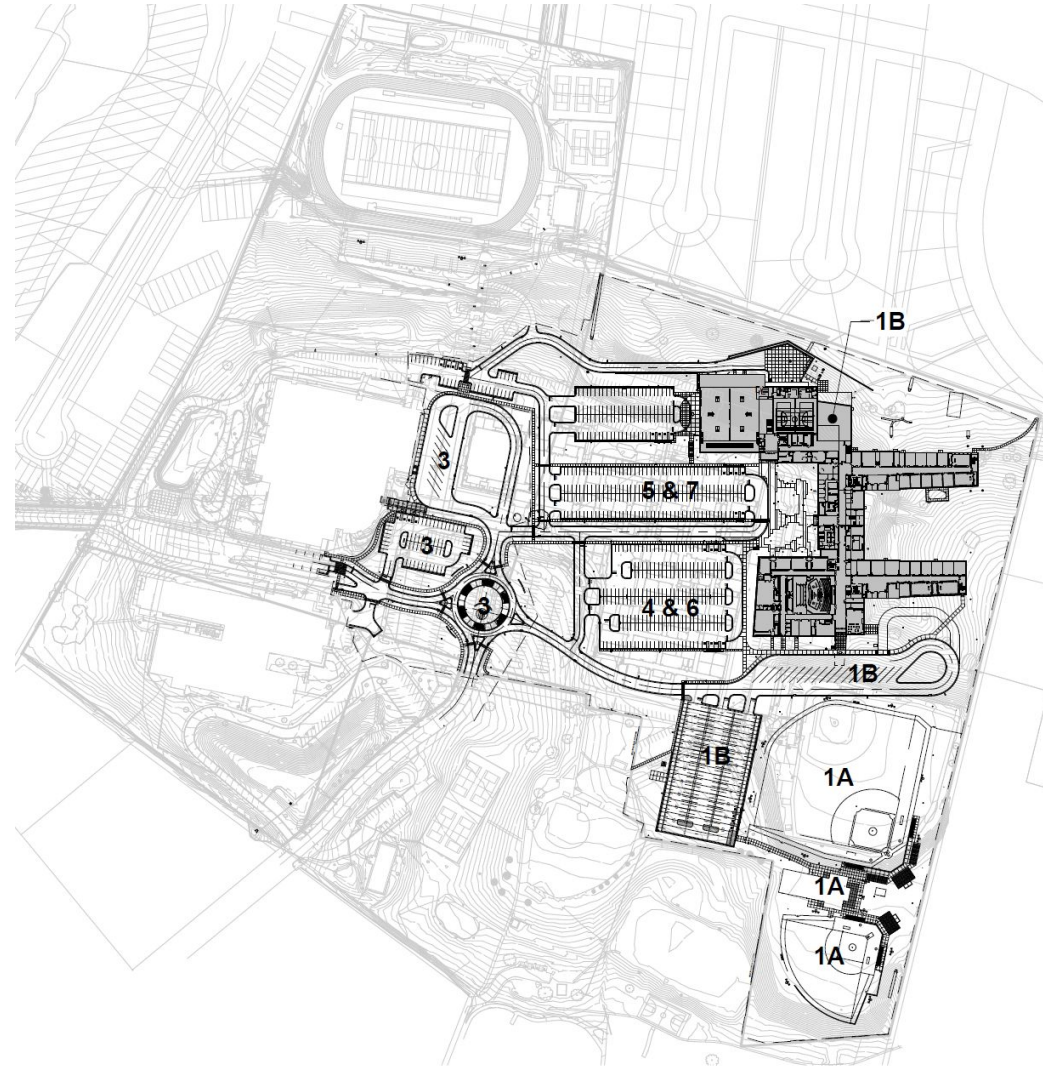

Tates Creek High – New Construction

▣ **Work Completed (July):**


- ▣ Stage equipment installation completed.
- ▣ Gym floor finish completed.
- ▣ Earthwork in front parking island continued.
- ▣ Basecourse on all parking and roads completed.
- ▣ Parking striping on band lot and bus lot completed.
- ▣ HVAC and electrical testing continued.

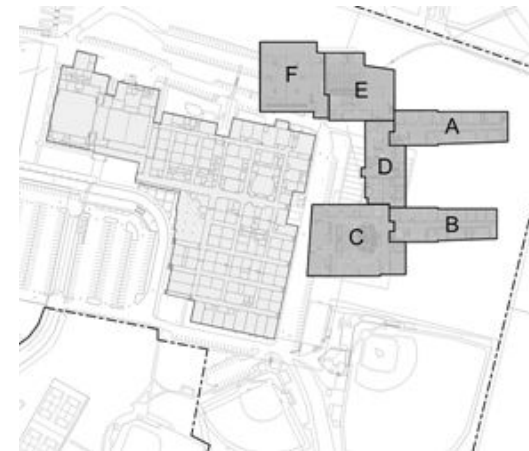

Tates Creek High – New Construction

□ **Current Work Effort (August):**

- Continue pavers in front plaza.
 - Continue earthwork in front parking islands.
 - Continue curbs and sidewalk.
 - Complete building signage.
 - Complete card access installation.
 - Continue troubleshooting mechanical and electrical systems.
-
- Building commissioning & site work to continue thru November 2022.

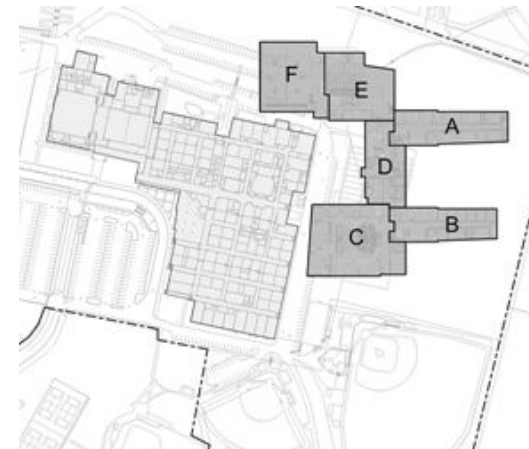


Tates Creek High – New Construction

Front Exterior



Gym

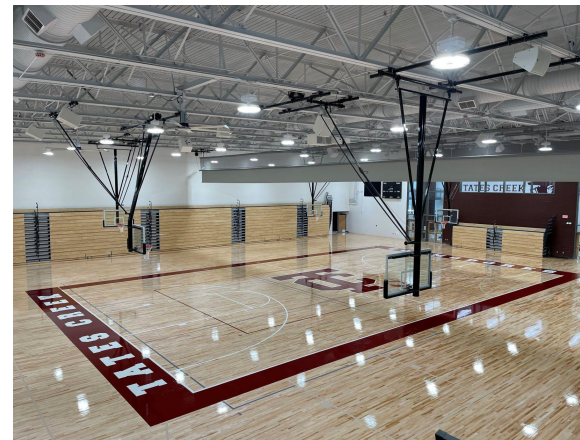

Front Parking




Gym Parking




Tates Creek High – New Construction


BEE Academy

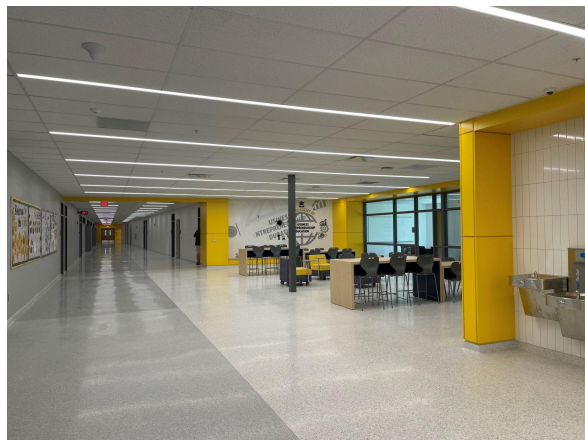

Building Signage

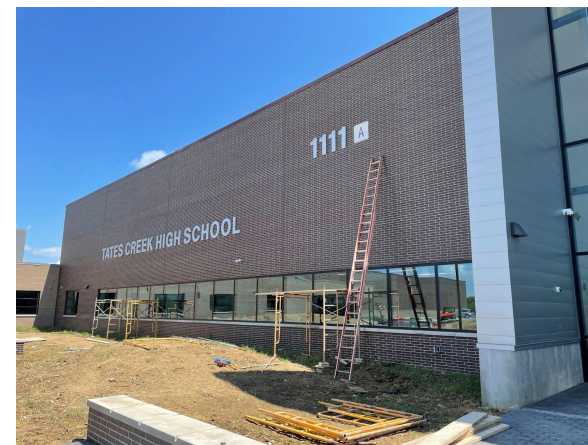

Cafeteria

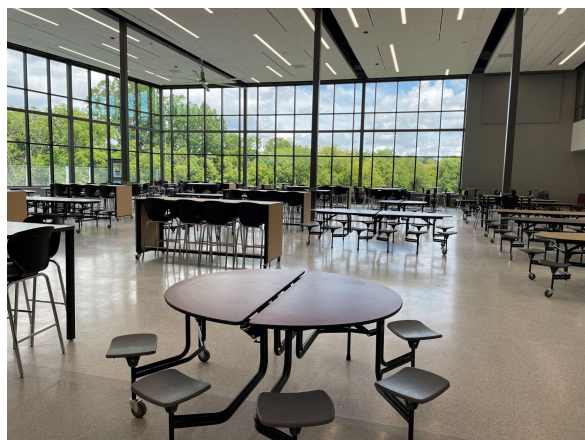

Typical Classroom



Tates Creek High – Dedication August 4, 2022



August 2022
