

Update on FCPS Construction/Renovation Projects

November 2021

Architect: Tate Hill Jacobs Architects

General Contractor:
D.W. Wilburn, Inc.

• GC Contract Sum: \$70,971,000.00

▶ Total Project Cost: \$84,570,295.16


Change Orders to Date (22): \$1,181,547.80

Scheduled Contract Completion Date: July 2022 (Building)
 November 2022 (Site)

% of Contract Completed:
72%


Revised Completion Date per GC:
No Change

3D Rendering

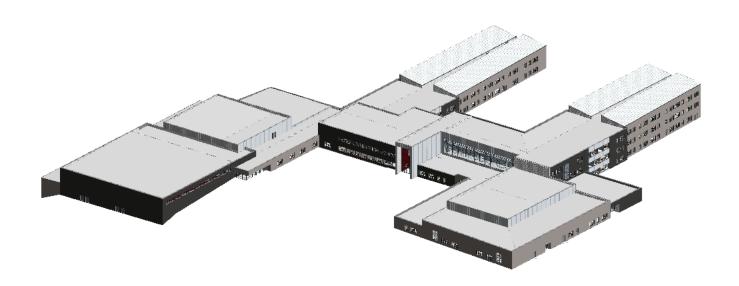


Work Completed (October):

- Continued sod and topsoil at Baseball and Softball Fields
- Asphalt base course installed at Band Practice Field.
- Drywall and paint continued in Areas A, B, C and D.
- Ceiling grid started.
- Roofing dry-in of building complete.
- Piping and duct installation in all areas continued.

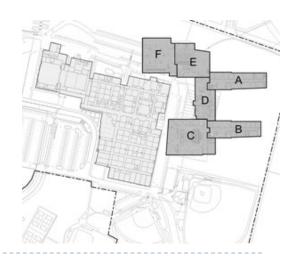

Current Work Effort (November):

- Continue curtainwall installation in Areas A & B.
- Continue brick installation at Areas E and F.
- Complete geothermal wellfield drilling.
- Continue gyp finishing, paint, terrazzo floor, ceramic tile and ceiling grid in Areas A and B.
- Continue above ceiling ductwork and piping.

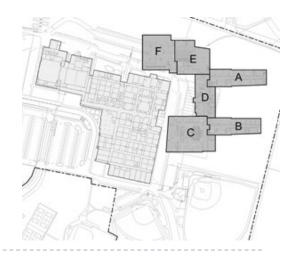

Area A - Main Level Ceiling Grid



Area E – Café Outdoor Patio



Area C - Orchestra Room Gyp



Area F – Gym Lobby



Baseball Field & Field House



Area D - Front Entrance



Area A – North Façade



Area E – Café Façade

