



# Update on FCPS Construction/Renovation Projects

February 2022



# Tates Creek High -- New Construction

---

- ▶ Architect: Tate Hill Jacobs Architects
- ▶ General Contractor: D.W.Wilburn, Inc.
- ▶ GC Contract Sum: \$70,971,000.00
- ▶ Total Project Cost: \$84,570,295.16
- ▶ Change Orders to Date (27): \$1,381,841.50
- ▶ Scheduled Contract Completion Date: July 2022 (Building)  
November 2022 (Site)
- ▶ % of Contract Completed: 82%
- ▶ Revised Completion Date per GC: No Change

# Tates Creek High -- New Construction

Aerial View (New Construction next to Existing)



# Tates Creek High -- New Construction

---

## ▶ **Work Completed (January):**

- ▶ Lights installed in Areas A & B.
- ▶ Ceiling grid installed in Areas A, B and D.
- ▶ Roof flashing and trim continues.
- ▶ Terrazzo floor grinding occurred in Areas A and B.
- ▶ Piping and duct installation in Area A completed.



# Tates Creek High -- New Construction

---

## ▶ **Current Work Effort (February):**

- ▶ Continue rubber floor tile and casework installation in Areas A & B.
- ▶ Continue sitework in front plaza.
- ▶ Begin terrazzo floor in Area E – Cafeteria.
- ▶ Begin installation of ceiling grid.
- ▶ Continue above ceiling ductwork and piping.





# Tates Creek High -- New Construction


Area A – Lower Science



Area A – Main Casework



Area C – Auditorium

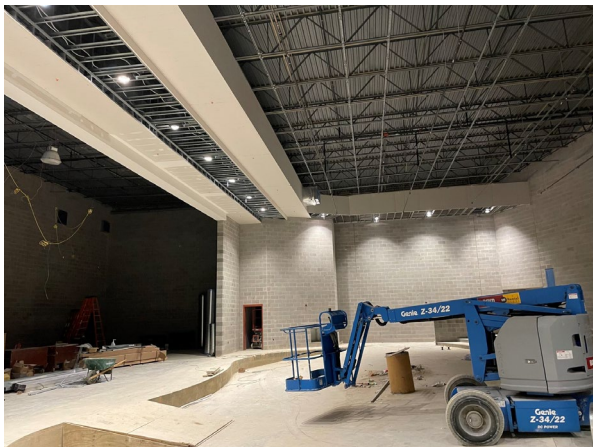


Area D – 3<sup>rd</sup> Curtainwall



# Tates Creek High -- New Construction

Area F – Gym Lobby

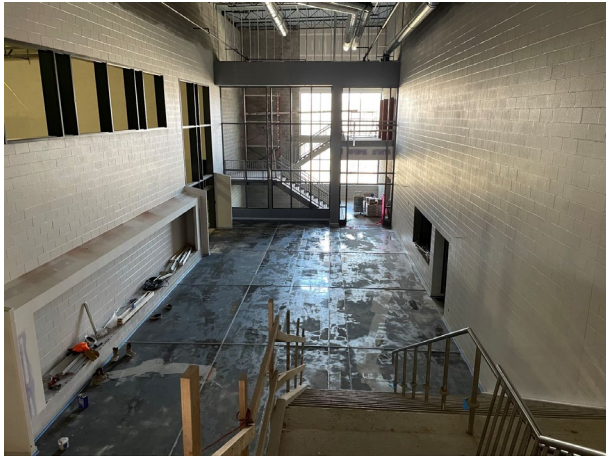

Exterior Front Entry



Area E – Café Ceiling & Lights



Exterior Café

