



# Update on FCPS Construction/Renovation Projects

April 2022



# Tates Creek High -- New Construction

---

- ▶ Architect: Tate Hill Jacobs Architects
- ▶ General Contractor: D.W.Wilburn, Inc.
- ▶ GC Contract Sum: \$70,971,000.00
- ▶ Total Project Cost: \$84,570,295.16
- ▶ Change Orders to Date (28): \$1,776,610.79
- ▶ Scheduled Contract Completion Date: July 2022 (Building)  
November 2022 (Site)
- ▶ % of Contract Completed: 86%
- ▶ Revised Completion Date per GC: No Change

# Tates Creek High -- New Construction

Aerial View (New Construction next to Existing)




# Tates Creek High -- New Construction

---

## ▶ **Work Completed (March):**

- ▶ Casework installation continued.
- ▶ Ceiling tile continued in Areas C, D, E and F.
- ▶ Rubber floor tile and carpet installation continued.
- ▶ Exterior metal panel installation continued at front entrance.
- ▶ Terrazzo floor installation occurred in Areas C and D.
- ▶ Wood gym floor installation occurred in Areas E and F.

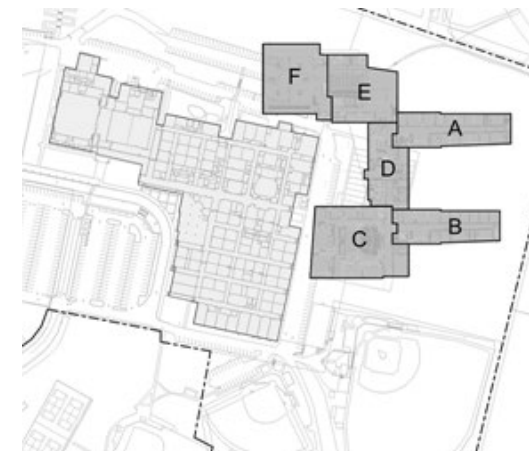

# Tates Creek High -- New Construction

---

## ▶ **Current Work Effort (April):**

- ▶ Continue rubber floor tile and casework installation in Areas B, C and D.
- ▶ Continue sitework in front plaza.
- ▶ Continue terrazzo floor grinding and polishing in Areas C and D.
- ▶ Continue installation of ceiling tiles in Areas C, D and E.
- ▶ Start installation of kitchen equipment.
- ▶ Continue exterior metal panel installation at front entrance.





# Tates Creek High -- New Construction


**Area B – 2<sup>nd</sup> Level Corridor**




**Area D – Front Entrance Metal Panels**



**Area E – Auxiliary Gym Floor**

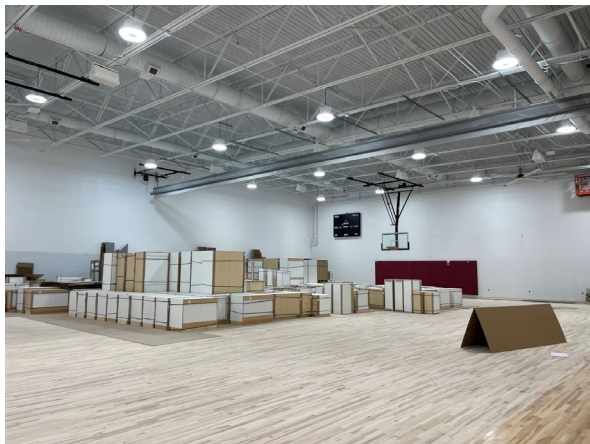

**Area E – Café Ceiling**

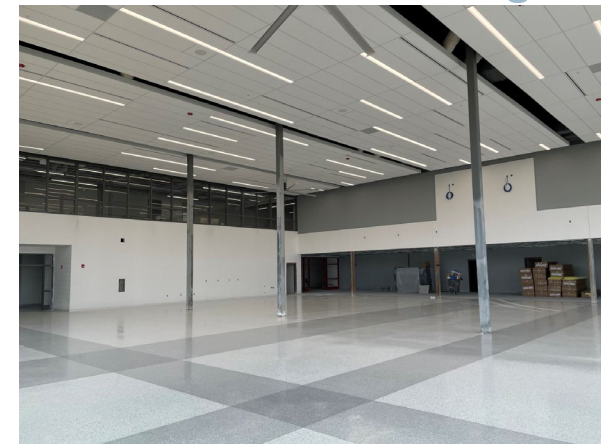

# Tates Creek High -- New Construction

Area E – Café Exterior



Area E – Café Terrazzo



Area F – Main Gym Floor



Area F – Main Gym

