



# Update on FCPS Construction/Renovation Projects

May 2022



# Tates Creek High – New Construction

---

- ▶ Architect: Tate Hill Jacobs Architects
- ▶ General Contractor: D.W.Wilburn, Inc.
- ▶ GC Contract Sum: \$70,971,000.00
- ▶ Total Project Cost: \$84,570,295.16
- ▶ Change Orders to Date (29): \$1,799,311.79
- ▶ Scheduled Contract Completion Date: July 2022 (Building)  
November 2022 (Site)
- ▶ % of Contract Completed: 88%
- ▶ Revised Completion Date per GC: No Change

# Tates Creek High – New Construction

Aerial View (New Construction next to Existing)



# Tates Creek High – New Construction

## ▶ **Work Completed (April):**

- ▶ Casework installation continued.
- ▶ Painting continued in Areas C, D, E and F.
- ▶ Exterior metal panel installation completed at front entrance.
- ▶ Terrazzo floor installation continued in Area D.
- ▶ Acoustical wall panel installation started.



# Tates Creek High – New Construction

## ▶ **Current Work Effort (May):**


- ▶ Continue bleacher installation in main gym.
- ▶ Continue sitework in front plaza.
- ▶ Continue terrazzo floor grinding and polishing in Area D.
- ▶ Continue installation of ceiling tiles in Areas C, D and E.
- ▶ Continue installation of kitchen equipment.





# Tates Creek High – New Construction


**Area B – 3<sup>rd</sup> Level Commons Area**

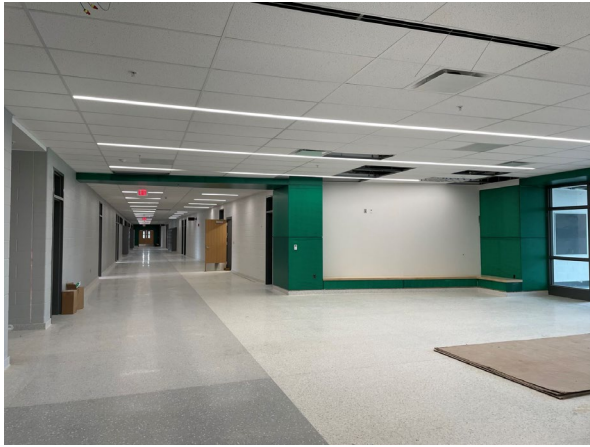

**Area C – Auditorium**



**Area D – Lobby Terrazzo Logo**

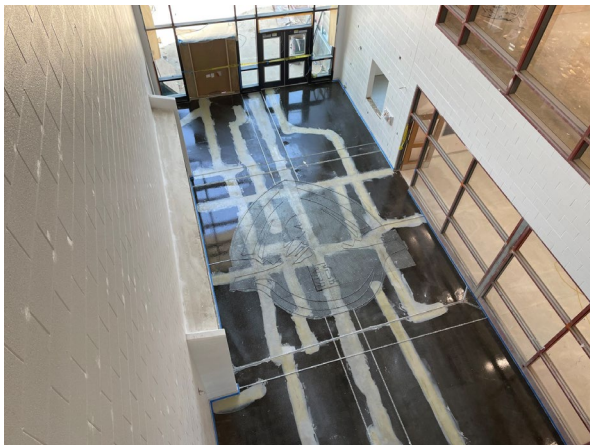

**Area E – Basement Mechanical Room**



# Tates Creek High – New Construction

Area F – Main Gym Bleachers



Exterior Front Entrance



Exterior Entrance Plaza



Exterior West Façade

