



FAYETTE COUNTY PUBLIC SCHOOLS

# Update on FCPS Construction/Renovation Projects

June 2022



# Tates Creek High – New Construction

---

- ▶ Architect: Tate Hill Jacobs Architects
- ▶ General Contractor: D.W.Wilburn, Inc.
- ▶ GC Contract Sum: \$70,971,000.00
- ▶ Total Project Cost: \$84,570,295.16
- ▶ Change Orders to Date (29): \$1,799,311.79
- ▶ Scheduled Contract Completion Date: July 2022 (Building)  
November 2022 (Site)
- ▶ % of Contract Completed: 90%
- ▶ Revised Completion Date per GC: No Change

# Tates Creek High – New Construction


Aerial View (New Construction next to Existing)



# Tates Creek High – New Construction

## ▶ **Work Completed (May):**

- ▶ Casework installation continued.
- ▶ Painting continued in Areas C, D, E and F.
- ▶ Terrazzo polishing completed.
- ▶ HVAC testing continued.
- ▶ Roof coping continued.

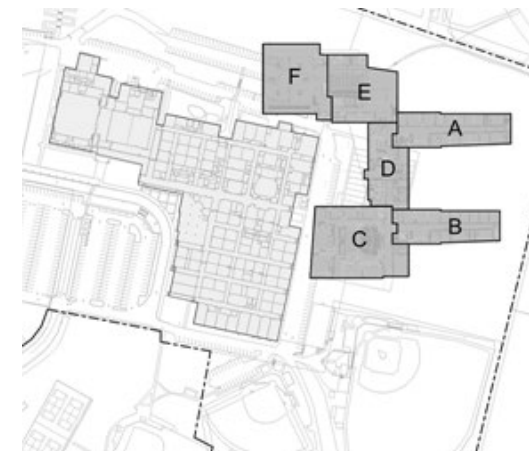

# Tates Creek High – New Construction

## ▶ **Current Work Effort (June):**

- ▶ Demolition of existing building began June 1.
  - ▶ Building demolition to complete by June 15.
  - ▶ Removal of demolition debris to continue over next several weeks.
- ▶ Continue sitework in front plaza and earthwork in front parking areas.
- ▶ Continue BDA installation.
- ▶ Continue paint and rubber floor tile installation.
- ▶ Continue pulling electrical wire.
- ▶ Sitework to continue to November 2022.





# Tates Creek High – New Construction

Area B – Exterior South Façade



Area B – Exterior Woodshop



Area C – Auditorium Seating



Area C – Band Room




# Tates Creek High – New Construction

Area D – Entrance Lobby



Area D – Lobby Ceiling

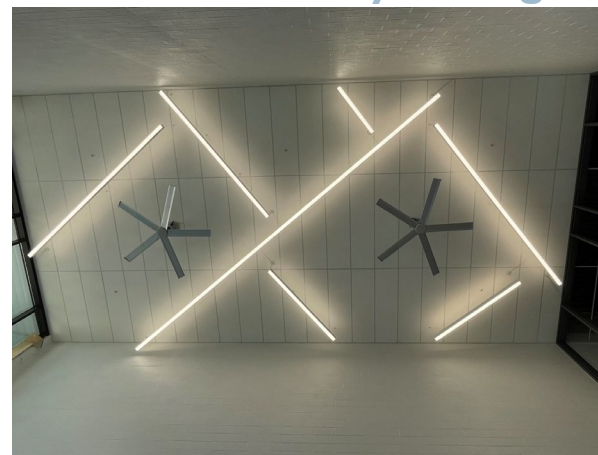

Area D -- Media Center





# Tates Creek High – New Construction

## Demolition of Existing Building

