

Stonewall Elementary -- Renovation

- ▶ Architect: Tate.Hill.Jacobs:Architects
- ▶ General Contractor: Burchfield & Thomas
- ▶ GC Contract Sum: \$12,577,700
- ▶ Total Project Cost: \$15,591,297
- ▶ Change Orders to Date (23): \$271,046
- ▶ Scheduled Contract Completion Date: December 2013
- ▶ % of Contract Completed: 92.05%
- ▶ Revised Completion Date per GC: September 2014

Stonewall Elementary -- Renovation

Rendering of Final Façade



STONEWALL ELEMENTARY - EAST ELEVATION

Stonewall Elementary -- Renovation

▶ **Work Completed to Date:**

- ▶ Permeable pavers installed in all parking areas.
- ▶ Entry canopy lighting installation completed.
- ▶ Substantial completion for Media Center.
- ▶ Casework installation completed.
- ▶ Phase Four classrooms - VCT installation completed.

▶ **Current Work Effort (August):**


- ▶ Asphalt paving installed on all driveway areas.
- ▶ Final paint coats on concrete masonry units.
- ▶ Terrazzo flooring completion.
- ▶ Substantial completion for PH 4 Classroom Wing.
- ▶ Substantial completion on full project.

Stonewall Elementary -- Renovation

New Front Façade



New Media Center Entry

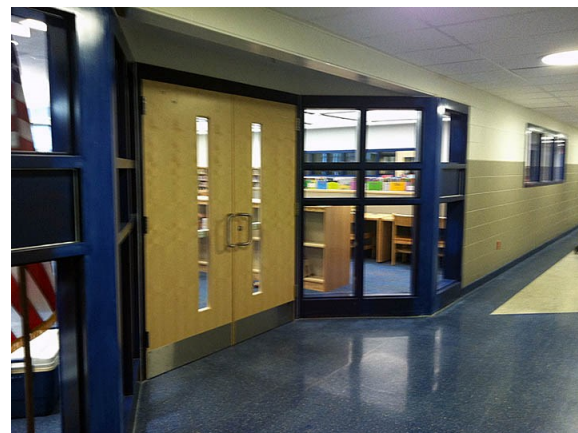

Media Center



Media Center Reading Area



Stonewall Elementary -- Renovation

Gym



Terrazzo – Classroom Wing



Music Room



Entrance

