

New Middle School @ Polo Club



Week Ending June 23, 2023

New Middle School @ Polo Club


➤ Completed Work:

- Poured 95% of Area A Slab on Grade
- Area B foundations to 100% Complete
- ICF pour at Area E. ICF Complete in Area E
- Completed ICF at the Locker Room
- Subgrade and stone ready for Curb and Gutter/Paving at east parking lot
- Continue Geothermal Continuing (62 are Completed)
- MEP Continuing following masonry
- CMU at locker room nearly complete
- Hollow core in Area C at 50%

➤ Upcoming Work/Look Ahead:

- Complete Slab on Grade area A
- Complete Foundations in Area A and C
- Finish Prep for curb and gutter
- Storm Sewer at west drive to bus parking
- ICF in Area A and Complete Area E
- CMU Complete at Area C
- Door Frames in Area A
- Continue MEP Rough in
- **Continue Geothermal (could be loud)**

Key Plan

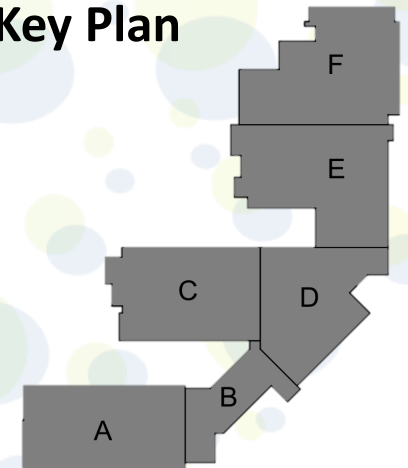

Area A – Plumbing Roughin Continue



Week Ending June 23, 2023

Area A – Wood Buck Installation for Windows



Week Ending June 23, 2023

Area B – Foundations Starting



Week Ending June 23, 2023

Area C – 2nd Floor Hollow Core Planks Going In



Week Ending June 23, 2023

Area C – Steel Framing Starting



Week Ending June 23, 2023

Area F – ICF and CMU Continues at the Gym



Week Ending June 23, 2023

Area F – Gym Locker Room CMU Almost Complete



Week Ending June 23, 2023

Geothermal Drilling Continues



Week Ending June 23, 2023

Front Entry/Media Center Rendering



Week Ending June 23, 2023
