

# New Middle School @ Polo Club



Week Ending June 16, 2023

# New Middle School @ Polo Club


## ➤ Completed Work:

- Poured 60% of Area A Slab on Grade
- Area B foundations are 80% Complete
- ICF pour at Area E. ICF Complete in Area E
- Completed ICF at the Locker Room
- Subgrade and stone ready for Curb and Gutter/Paving at east parking lot
- Continue Geothermal Continuing (62 are Completed)
- MEP Continuing following masonry
- CMU at locker room is almost complete

## ➤ Upcoming Work/Look Ahead:

- Complete Slab on Grade in Area A
- Complete Foundations in Area A and C
- Finish Prep for curb and gutter
- Storm Sewer at west drive to bus parking
- ICF in Area A and Complete Area E
- CMU Complete at Area C
- Setting Door Frames in Area A
- Continue MEP Rough in
- **Continue Geothermal (could be loud)**

Key Plan

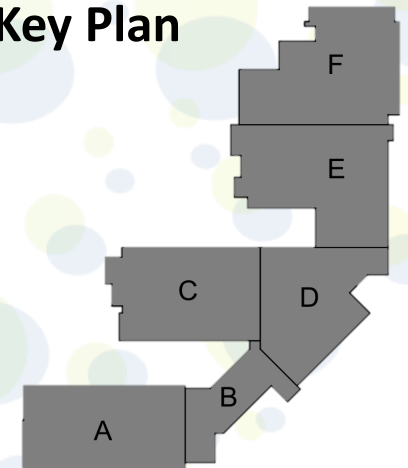



## Aerial of Site



Week Ending June 16, 2023



## Aerial View – Overall Work from Gym looking towards Classroom Wings



Week Ending June 16, 2023



## Area F – Mechanical Platform Hollow Core Planks In Place



Week Ending June 16, 2023



## Area F – Gym ICF Continuing, Locker Room is Complete



Week Ending June 16, 2023



## Area E – Cafeteria ICF Continuing for ICF Pour



Week Ending June 16, 2023



## Area C – CMU Walls up to 2<sup>nd</sup> Floor



Week Ending June 16, 2023



## Area A – CMU Base Course and Slab Prep



Week Ending June 16, 2023



## East Parking Lot - Finish Prep for Curbs and Gutters



Week Ending June 16, 2023



## Front Entry/Media Center Rendering



Week Ending June 16, 2023
