

New Middle School @ Polo Club



Week Ending June 9, 2023

New Middle School @ Polo Club


➤ Completed Work:

- Poured 60% of Area A Slab on Grade
- Area B foundations are 70% Complete
- ICF pour at Area E. ICF Complete in Area E
- Complete ICF at Locker Room
- Subgrade and stone ready for Curb and Gutter/Paving at east parking lot
- Continue Geothermal Continuing (51% Complete)
- MEP Continuing following masonry
- CMU remediations nearly complete at Area C
- CMU at locker room nearly complete

➤ Upcoming Work:

- Complete Slab on Grade in Area A
- Complete Foundations in Area A and C
- Finish Prep for curb and gutter
- Storm Sewer at west drive to bus parking
- ICF in Area A and Complete Area E
- CMU Complete at Area C
- Door Frames at Area A
- Continue MEP Rough in
- **Continue Geothermal (could be loud)**

Key Plan

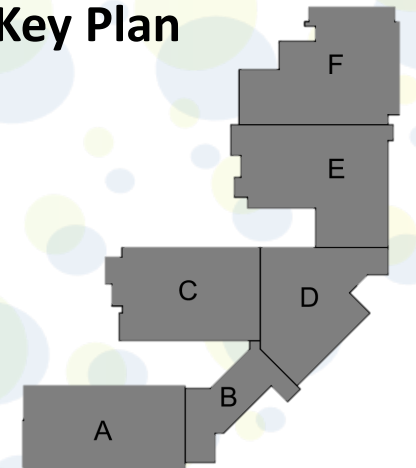

Area A- Vapor Barrier in for Slab Prep



Week Ending June 9, 2023

Area A – Classroom Slab Prep



Week Ending June 9, 2023

Area A – Restroom Plumbing Rough in Continues



Week Ending June 9, 2023

Area B – Foundations Starting



Week Ending June 9, 2023

Area C – CMU Continuing in the Corridors



Week Ending June 9, 2023

Area C – CMU Installed to 2nd Floor



Week Ending June 9, 2023

Area C – Pumping Concrete in ICF



Week Ending June 9, 2023

Site Grading at Parking Lot



Week Ending June 9, 2023

Front Entry/Media Center Rendering



Week Ending June 9, 2023
