

July 31st – August 4th

- Complete installation of toilet partitions.
- Complete installation of plumbing fixtures.
- Floor burnishing.
- Final Clean.



August 7th – August 11th

- Punch list work.
- State Fire Marshal final inspection 8/8.





July 24th – 28th

- Finish flooring throughout, base included.
- Installing wall tile, division 10 items, toilet partitions, plumbing fixtures.
- Electrical trim out completed.



July 31st – August 4th

- Complete installation of toilet partitions.
- Complete installation of plumbing fixtures.
- Final clean.
- Floor burnishing.
- State Fire Marshal final inspection 8/2.





July 3rd – July 7th

- In-wall inspection in West bathroom
- Soffit build-out in West bathroom
- Drywall
- Skim-coating in the North and South classrooms

East Corridor & Classrooms

- Rough-in for casework
- Finish all walls
- Lights hung in corridor
- Began rough-in

Setting borders for ceiling in
all corridors



July 10th – July 14th

- Above ceiling inspection
- Drop all ceiling tiles
- Flooring installation in North corridor
- Set casework in East classrooms





June 19th – June 23rd

North Corridor Classrooms

- Finished Drywall
- Began Painting

East Corridor & Classrooms

- Installed Flooring/Flooring Protection
- Dropped Ceiling Tiles
- Installed Casework
- MEP Trim Out

West Corridor

- Began Floor Prep

West Bathroom

- Soffit Buildout
- Finished Drywall

South Corridor Classrooms

- Finished Drywall
- Installed Flooring/Flooring Protection



June 26th – June 30th

North Corridor Classrooms

- MEP Above Ceiling Rough in
- Overhead Inspection
- Begin Flooring Install

East Corridor & Classrooms

- Ceramic Wall Tile Install
- Install Salvaged Doors
- Finish Touch-up
- Final Clean



West Corridor


- Flooring Install

West Bathroom

- Grid Install
- Floor Prep
- Epoxy Flooring

South Corridor Classrooms

- MEP Above Ceiling Rough In
- Overhead Inspection
- Casework Install

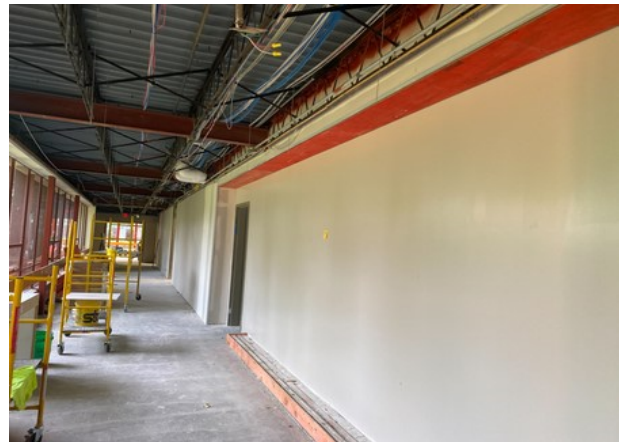

June 12th – June 16th


- East side:
 - o Rough ins
 - o Completed framing
 - o Hanging drywall
- South side
 - o NW wall demo'd
 - o Hanging drywall
 - o Finishing drywall on corridor sides
 - o Priming existing walls in classrooms
- North side
 - o Room 120 and 121 corridor walls demo'd
 - o New framing has begun
 - o Finishing drywall
 - o Priming existing classroom walls
- West side
 - o Demo'd ceiling grid in the teacher's lounge
 - o Bathroom floor leveled
 - o Began framing



June 19th – June 23rd

- East side
 - o MEP rough-ins
 - o In wall inspection
 - o Hanging drywall
 - o Priming existing walls in classrooms
- South side
 - o Finishing classroom side dry wall
 - o Start corridor ceiling grid
 - o Flooring in classrooms
- North side
 - o Casework for corridors and classrooms
 - o Corridor ceiling grid
 - o Painting corridor walls
- West side
 - o Finish framing
 - o MEP roughins
 - o Hang drywall



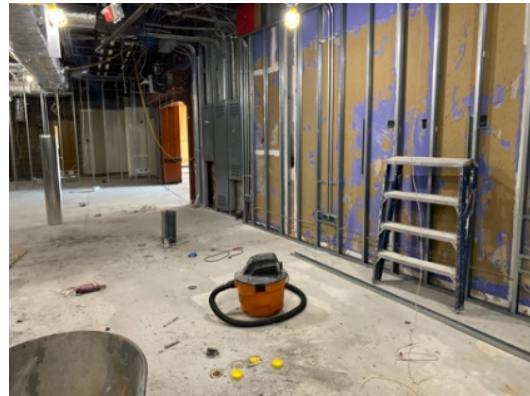

June 5th – June 9th

- Framing continued.
- Plumbing demo continued.
- Electrical rough in continued.
- Plumbing rough-in continued.
- Floor Prep began.



June 12th – June 16th

- Floor prep continues.
- Framing continues.
- Dry wall in offices and in classrooms begins.





May 30th – June 2nd

- Continued demolition of the North, East, and South corridors.
- Completed the slab pour in the East end of the building.
- Completed the plumbing demolition.
- Started framing in the North and South Corridors



June 5th – June 9th

- Finish demolition.
- Continue framing in the North and South corridors.
- Begin MEP rough in.





Touch-A-Truck Event





