



Pawnee Elementary School WEEKLY PROGRESS REPORT 08/11/2023

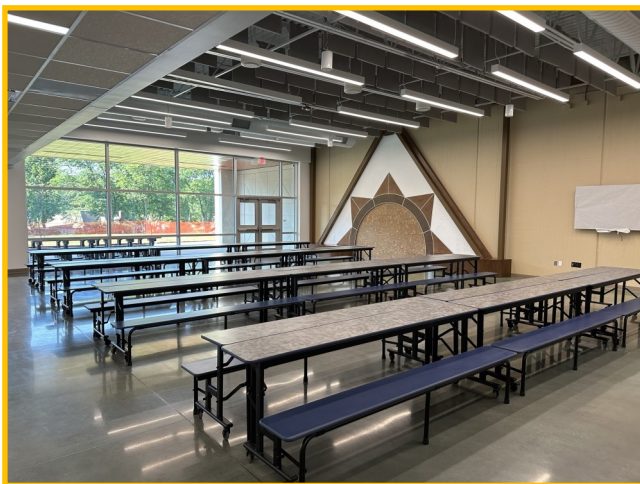

Cafeteria

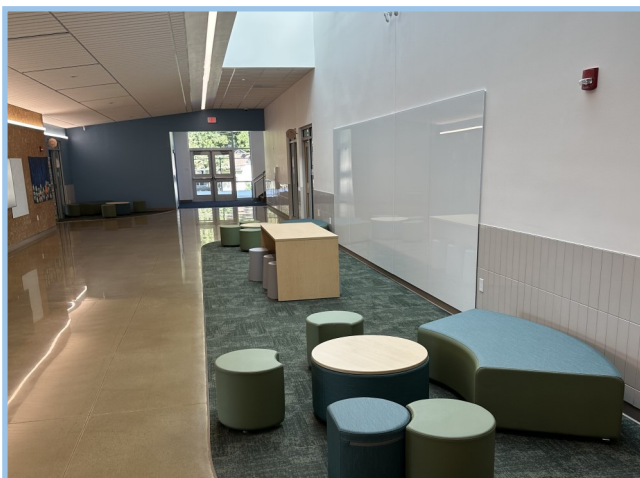

Collaboration Space

This Week: 08/07/23—08/11/23

- Completed Trash Enclosure
- Completed Retaining Wall Fence
- Completed Casework in Media Center
- Completed Concrete Sidewalks at North Parking Lot
- Completed South Landscaping
- Completed North Landscaping
- Installed Wall Graphics

Next Week: 08/14/23—08/18/23

- Final Touch Up
- Final Clean
- School Begins!

Weather Days this week: (1) Days



Maker Space




South Landscaping

Pawnee Elementary School WEEKLY PROGRESS REPORT 08/04/2023



Front Entrance

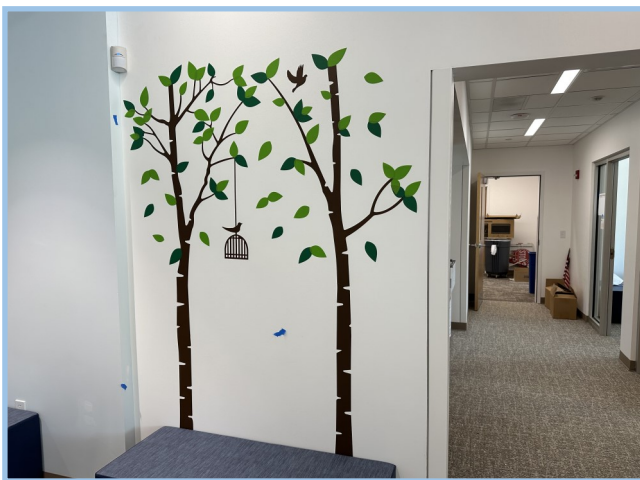

Reception Wall Graphic


This Week: 07/31/23—08/04/23

- Completed Masonry at Trash Enclosure
- Installed Wall Graphics
- Continued Retaining Wall Fence
- Installed Casework in Media Center
- Installed Lighting in Level 2 Collaboration Space
- Continued Concrete Sidewalks at North Parking Lot
- Continued South Landscaping

Next Week: 08/07/23—08/11/23

- Complete East Retaining Wall Fence
- Complete Concrete Sidewalks
- Complete Painting Stairs
- Continue Wall Graphic Install
- Begin North Landscaping
- Begin Setting Light Poles

Weather Days this week: (2) Days

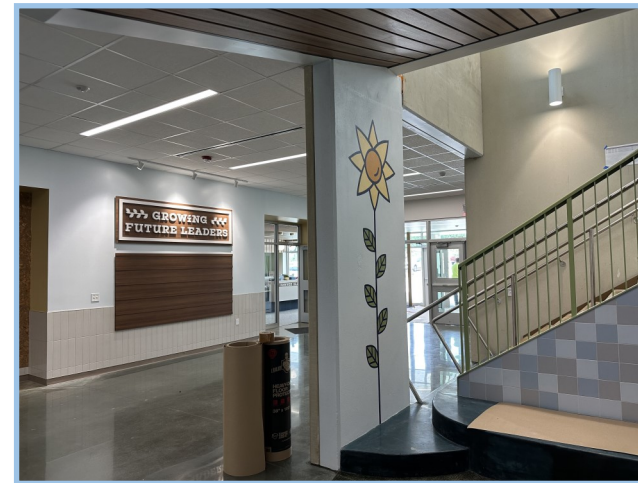

Entrance Hallway Wall Graphic




Instrumental Room

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Trash Enclosure

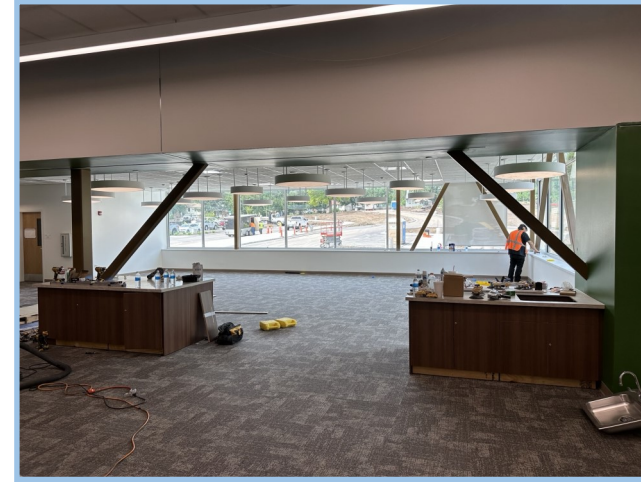

Media Center Casework



Retaining Wall Fence



Second Floor Tower

Pawnee Elementary School WEEKLY PROGRESS REPORT 07/28/2023



Panther Parkway



Second Floor Collaboration Space

This Week: 07/24/23—07/28/23

- Completed Carpet Tile in Media Center
- Completed Media Center Lights
- Completed Panther Parkway Hanging Lights
- Continued East Retaining Wall Fence
- Continued South Landscaping
- Continued Concrete Sidewalk at North Parking Lot
- Began Painting Stairs

Next Week: 07/31/23—08/04/23

- Continue East Retaining Wall Fence
- Continue Concrete Sidewalks at North Parking Lot
- Complete Painting Stairs
- Complete South Landscaping
- Begin Setting Light Poles

Weather Days this week: (0) Days



Gym



Art

Pawnee Elementary School WEEKLY PROGRESS REPORT


Page 2



Media Center Lights



Media Center Carpet

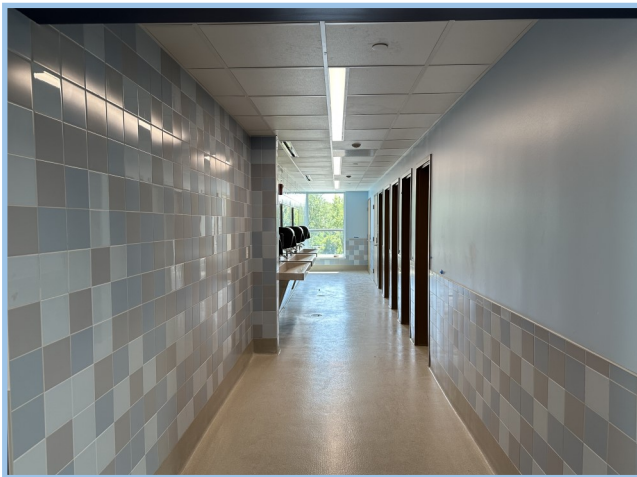

Second Level Restroom




Cafeteria Ceiling

Pawnee Elementary School WEEKLY PROGRESS REPORT 07/21/2023



ADA Crossing at North Parking Lot

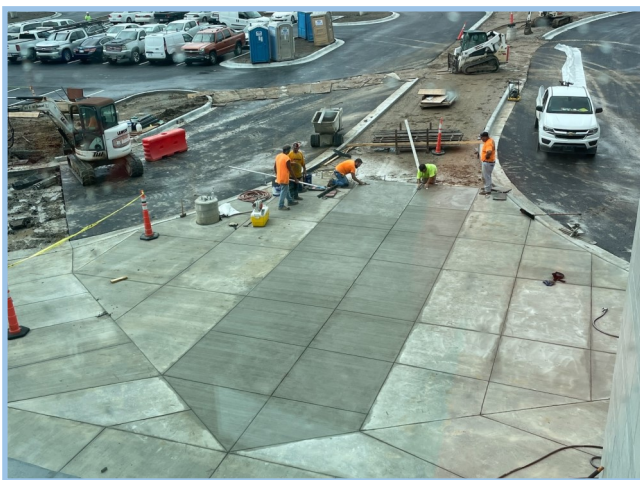

North Entrance Sidewalk

This Week: 07/17/23—07/21/23

- Completed Entrance Sidewalks
- Completed Ceilings in Area A
- Completed Pouring Asphalt
- Completed Striping Asphalt
- Completed Carpet Tile in Reception
- Completed Curb at 91st Street
- Completed Kitchen Equipment Connections
- Began Setting Light Poles
- Began East Retaining Wall Fence
- Began South Landscaping
- Began Trash Enclosure Foundations

Next Week: 07/24/23—07/28/23

- Complete Setting Light Poles
- Complete East Retaining Wall Fence
- Complete South Landscaping
- Complete Trash Enclosure Masonry
- Install Remaining Glass

Weather Days this week: (0) Days



Ceiling at Second Floor Tower



Reception

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Media Center



North Entrance Wall Tile



Basketball Lines at Hard Play



Panther Parkway

Pawnee Elementary School WEEKLY PROGRESS REPORT 07/14/2023



North Face of Building & Parking Lot



North Entrance Sidewalk

This Week: 07/10/23—07/14/23

- Began Testing Fire Alarm
- Began Pouring Asphalt
- Began Carpet Tile in Reception
- Began Striping Asphalt
- Continued Kitchen Equipment Connections
- Continued Pouring Sidewalks
- Continued Ceilings in Area A
- Continued Paint in Area A
- Continued MEP Trim Out
- Continued Installing Gym Floor

Next Week: 07/17/23—07/21/23

- Finish Pouring Front Entrance Sidewalks
- Finish Testing Fire Alarm
- Finish Ceilings in Area A
- Finish Pouring Asphalt
- Finish Striping Asphalt
- Finish Carpet Tile in Reception

Weather Days this week: (0) Days



Gym Floor Install



Reception

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Reception Flooring



North Parking Lot



North Parking Lot



Collaboration Space

Pawnee Elementary School WEEKLY PROGRESS REPORT 07/07/2023



North Parking Lot



North Entrance Sidewalk

This Week: 07/03/23—07/07/23

- Began Pouring North Entrance Sidewalks
- Continued Gym Floor Install
- Continued Paint in Area A
- Continued Ceilings in Area A
- Continued MEP Trim Out
- Continued Concrete Floor Polish and Stain
- Finished Pouring ADA Crossings on North

Next Week: 07/10/23—07/14/23

- Begin Testing for Fire Alarm
- Begin Pouring Asphalt
- Continue Pouring Sidewalks
- Continue Ceilings in Area A
- Continue Paint in Area A
- Continue MEP Trim Out
- Continue Installing Gym Floor

Weather Days this week: (2) Days



Gym Floor Install



Collaboration Space

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Ceiling of Second Floor Tower



Roof Patio



Polished Concrete Floor



Collaboration Space

Pawnee Elementary School WEEKLY PROGRESS REPORT 06/09/2023



Epoxy Restroom Floors Area B



Polish Concrete in Cafeteria

This Week: 06/05/23—06/09/23

- Continue Sitework
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue MEP Trim-out in Area A
- Continue Wall Tile in Area A
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area A
- Continue Polish Concrete in Area A

Next Week: 06/12/23—06/16/23

- Continue Sitework on North
- Continue Glazing in Area A
- Continue MEP Trim-Out in Area A
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring
- Continue Property Fence
- Continue Polish Concrete in Area B

Weather Days this week: (0) Days



Ceilings Continuing in Area B



Gym Finishes Touch-Up

Pawnee Elementary School WEEKLY PROGRESS REPORT


Page 2



Exterior Doors Installed



Outdoor Classroom Paver Install

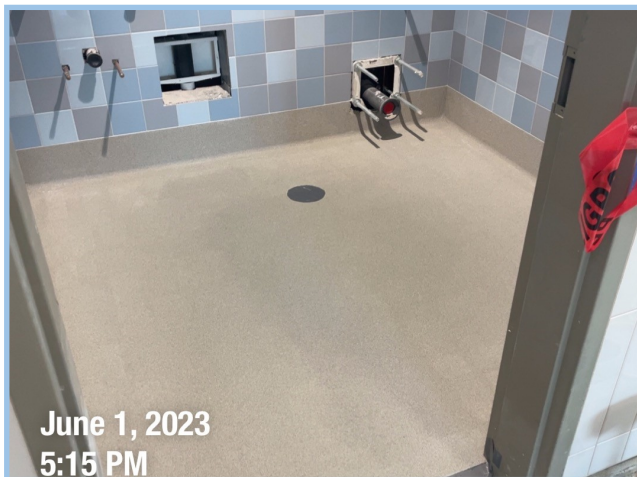

Single Restroom Epoxy Floor



Lighting Install

Pawnee Elementary School WEEKLY PROGRESS REPORT 06/02/2023



Metal Panel at Clerestory



Wall Prep for Tile

This Week: 05/29/23—06/02/23

- Continue Sitework
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue MEP Trim-out in Area A
- Continue Wall Tile in Area A
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area A
- Continue Polish Concrete in Area A

Next Week: 06/05/23—06/09/23

- Continue Sitework on North
- Continue Glazing in Area A
- Continue MEP Trim-Out in Area A
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring
- Continue Property Fence
- Continue Polish Concrete in Area B

Weather Days this week: (0) Days



Continue Grading for New Parking Lot



Polish Grinding in Corridor

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Grading Along NW Elevation



Soffit Venting at Front Entrance



Insulation at East Clerestory




Polish Grinding in Corridor

Pawnee Elementary School WEEKLY PROGRESS REPORT 05/26/2023



Grading at Front Playground

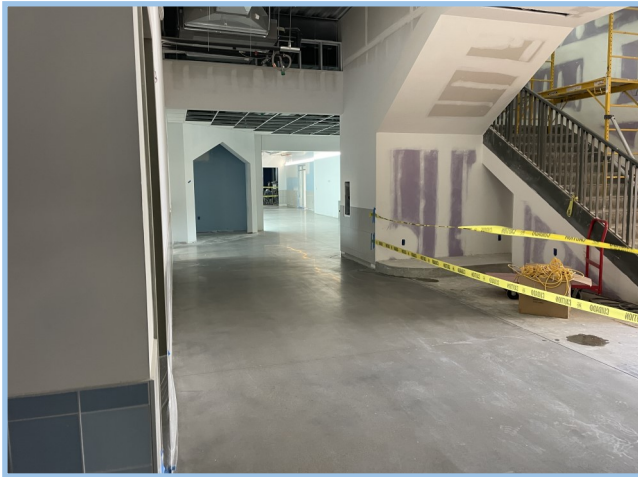

Polish Concrete Grinding

This Week: 05/22/23—05/26/23

- Continue Sitework
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue MEP Trim-out in Area A
- Continue Wall Tile in Area A
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area B
- Began Polish Concrete in Area B

Next Week: 05/22/23—05/26/23

- Continue Sitework on North
- Continue Glazing in Area A
- Continue MEP Trim-Out in Area A
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring
- Continue Property Fence
- Continue Polish Concrete in Area B

Weather Days this week: (0) Days




Metal Panel at South Elevation




West Side Retaining Wall



Area B Metal Panel at Clerestory

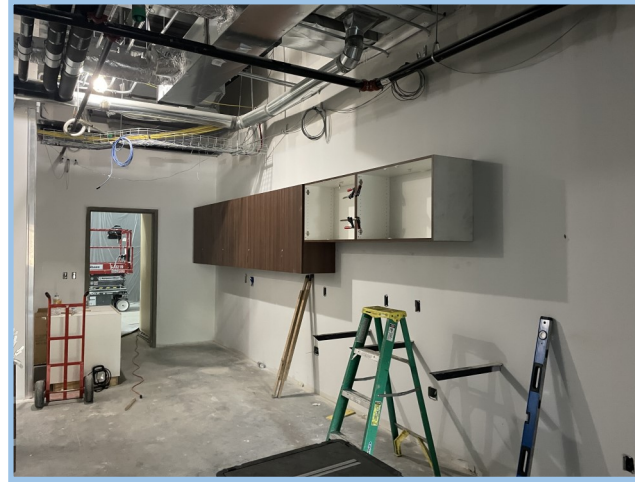

Casework at Reception

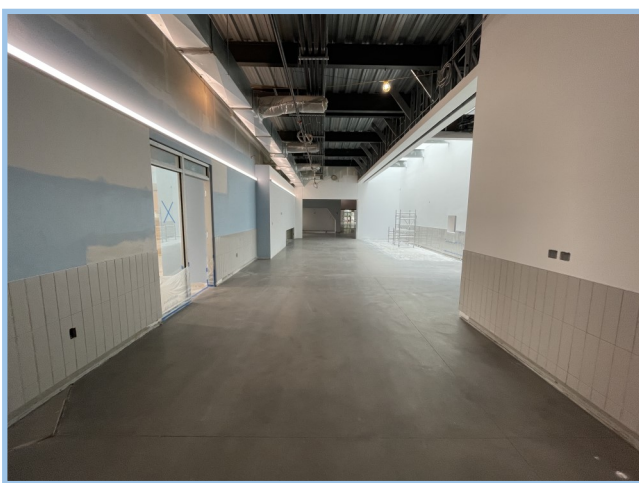

Polish Stain



South Playground Install

Pawnee Elementary School WEEKLY PROGRESS REPORT 05/19/2023



Classroom Flooring Prep



East Sidewalk Install

This Week: 05/15/23—05/19/23

- Continue Sitework
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue MEP Trim-out in Area A
- Continue Wall Tile in Area A
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area B

Next Week: 05/22/23—05/26/23

- Continue Sitework on North
- Continue Glazing in Area A
- Continue MEP Trim-Out in Area A
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring
- Complete Property Fence
- Begin Polish Concrete in Area B

Weather Days this week: (1) Days



Corridor Lighting & Grid



Level 2 Ceiling Grid Install

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Level 2 Area B Wall Tile Install



Mass Grading at North Side



Paint in Panther Parkway



Clerestory Area B Touch-Ups

Pawnee Elementary School WEEKLY PROGRESS REPORT 05/12/2023



South Metal Panel Install



East Curb Install

This Week: 05/08/23—05/12/23

- Continue Sitework
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue MEP Trim-out in Area B
- Continue Wall Tile in Area B
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area B
- Continue Property Fence

Next Week: 05/15/23—05/19/23

- Continue Sitework on North
- Continue Glazing in Area A
- Continue MEP Trim-Out in Area B
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring
- Complete Property Fence
- Begin Polish Concrete in Area B

Weather Days this week: (1) Days



Front Entrance Curtain Wall Install



Property Fence Install

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



East ADA Sidewalk Install



East Access Stair Prep



West Storm Install



Sun Feature Wall Prep

Pawnee Elementary School WEEKLY PROGRESS REPORT 05/05/2023



South Patio Slab Prep



Interior Aluminum Frame Install


This Week: 05/01/23—05/05/23

- Continue Sitework
- Complete Masonry on Area A
- Continue Glazing Area A
- Continue Metal Panel Install Area B
- Continue Ceiling Tile in Area A
- Continue Pulling Wire in Area A
- Continue MEP Trim-out in Area B
- Continue Wall Tile in Area B
- Continue Finishes & Paint in Area A
- Continue Alum Frames in Area B

Next Week: 05/08/23—05/12/23

- Continue Sitework on North
- Continue Exterior Area A
- Continue MEP Trim-Out in Area B
- Continue Metal Panel Install Area B
- Continue Paint in Area B
- Continue Paint in Area A
- Continue Resinous Flooring

Weather Days this week: (1) Days

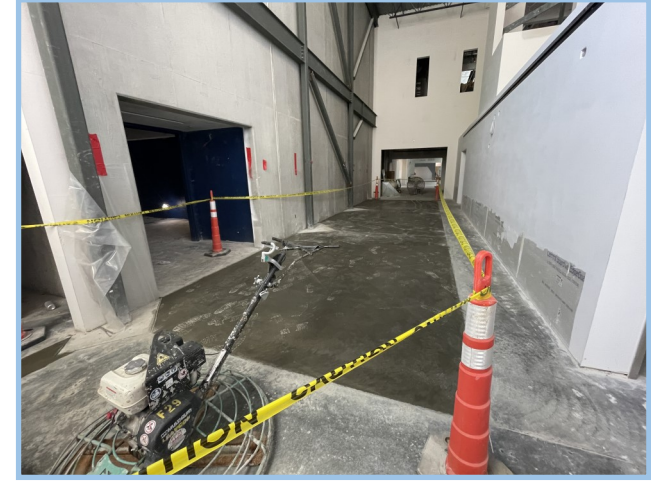

Slab Prep for Polish



Canopy Soffit Detailing

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Existing Building Demo Complete



Stone Complete



Ceiling work Area B



Fencing Demo at Property Line

Pawnee Elementary School WEEKLY PROGRESS REPORT 04/28/2023



South Playground Install



Ceiling Grid Install

This Week: 04/24/23—04/28/23

- Complete Existing Building Demo
- Continue Sitework
- Continue Masonry on Area A
- Continue Glazing Area A
- Continue Metal Panel Insulation
- Continue Ceiling Tile in Area A
- Continue Pulling Wire in Area A
- Continue MEP Trim-out in Area B
- Continue Wall Tile in Area B
- Continue Finishes & Paint in Area A
- Begin Aluminum Frames in Area B

Next Week: 05/01/23—05/05/23

- Continue Sitework on North
- Continue Exterior Area A
- Continue MEP Trim-Out in Area B
- Continue Metal Panel Insulation
- Continue Paint in Area B
- Continue Paint in Area A
- Begin Metal Panel System Install

Weather Days this week: (1) Days



Aluminum Door Frame Install



South Kitchen Brick Complete

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Second Playground Install



Kitchen Hood Install



Storm Inlets Poured



Front Canopy Build-Out

Pawnee Elementary School WEEKLY PROGRESS REPORT 04/21/2023



Exterior Stone Install



Demo of Existing School Foundations

This Week: 04/17/23—04/21/23

- Continue Existing Building Demo
- Continue Sitework
- Continue Masonry on Area A
- Continue Glazing Area A
- Continue Metal Panel Insulation
- Continue Ceiling Tile in Area B
- Continue Pulling Wire in Area A & B
- Continue MEP Trim-out in Area B
- Continue Wall Tile in Area B
- Continue Finishes & Paint in Area B

Next Week: 04/24/23—04/28/23

- Complete Existing Building Demo
- Continue Sitework
- Continue Exterior Area A
- Continue MEP Trim-Out in Area B
- Continue Metal Panel Insulation
- Continue Paint in Area B
- Begin Paint in Area A

Weather Days this week: (1) Days



Stainless Steel Panel Install



Exterior Patio Concrete

Pawnee Elementary School WEEKLY PROGRESS REPORT

Page 2



Install of Remaining Brick



Tile at Restrooms



Casework on Level 2 Area B



Stone Install on East Elevation
