




21st Century Classroom Improvements

August 24, 2023, Board Update



Sites In Progress & Completed

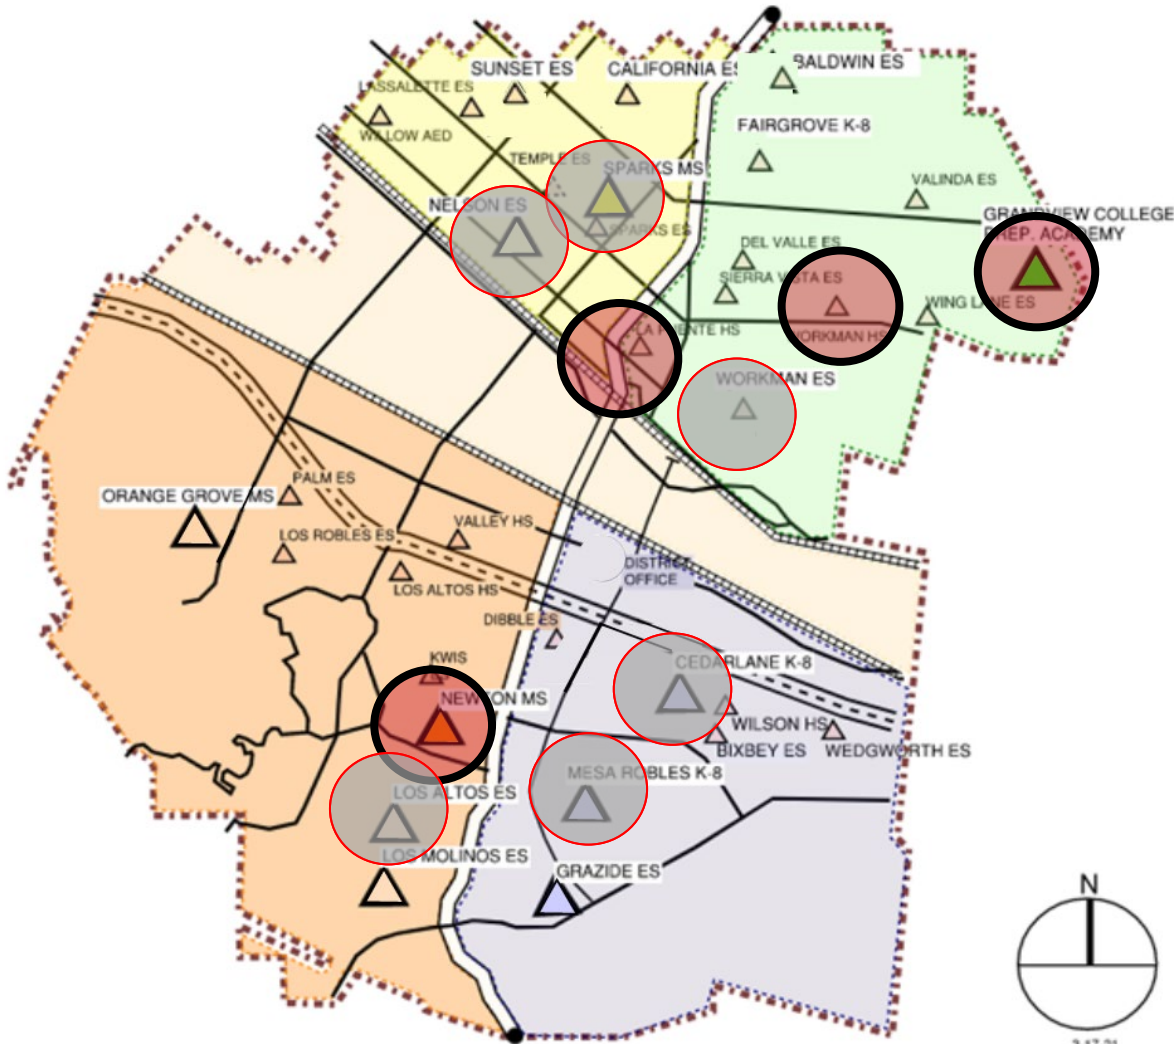

IN PROGRESS

Newton MS
Grandview K-8

HIGH SCHOOL REFRESH

La Puente HS
Workman HS


COMPLETED

Nelson ES
Los Altos ES
Workman ES
Mesa Robles K-8
Cedarlane K-8
Sparks MS

Newton Middle School

Phase 1: D-1 to D-4 Complete
 Phase 2: C-6 to C-8 Complete
 Phase 3: C-1 to C-4 Complete


Phase 4: B-4, B-6 to B-8 Complete
 Phase 5: Music Room Complete
 Phase 6: E-1, E-2, F-1, F-2 Next Phase

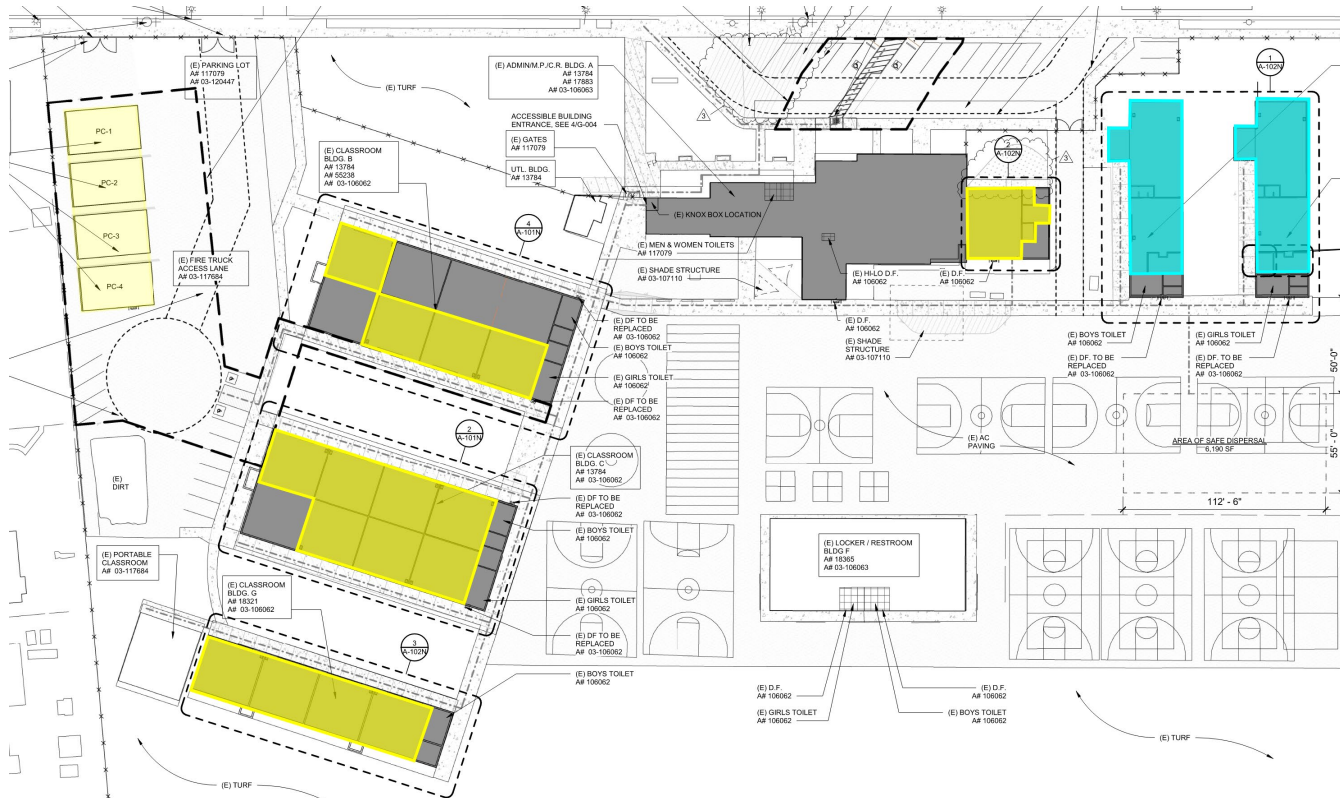

Site Plan & Status
 Construction

Newton Middle School

Band Room

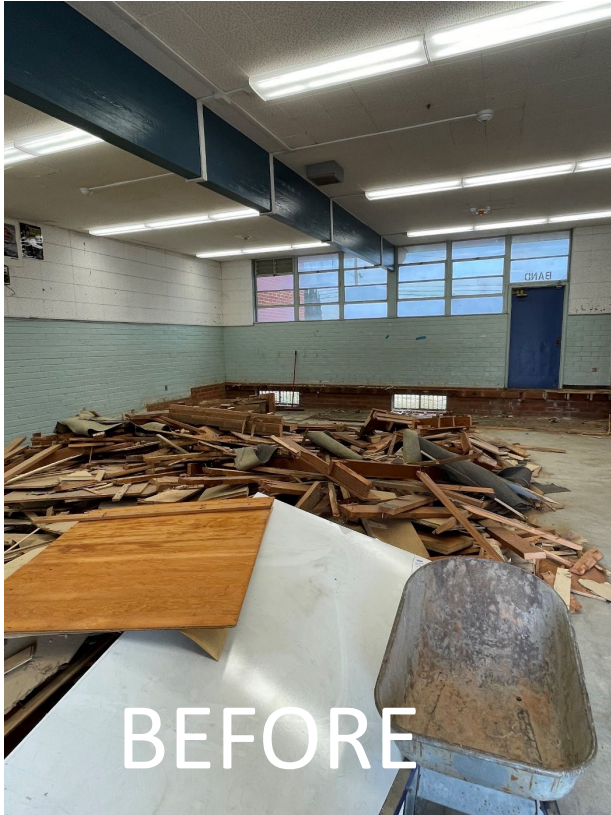

Project Status
Construction

Newton Middle School

Band Room






Project Status

Construction

Newton Middle School

KPI Overview NWMS 21 ST CENTURY CLASSROOM

Budget	Committed	Balance
\$ 4.71M	\$ 3.92M 83.1%	\$ 0.79M 16.9%

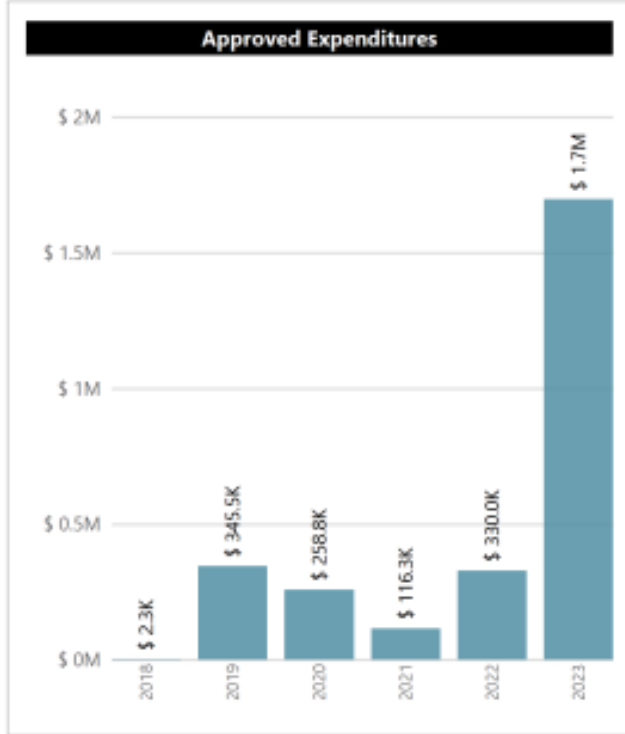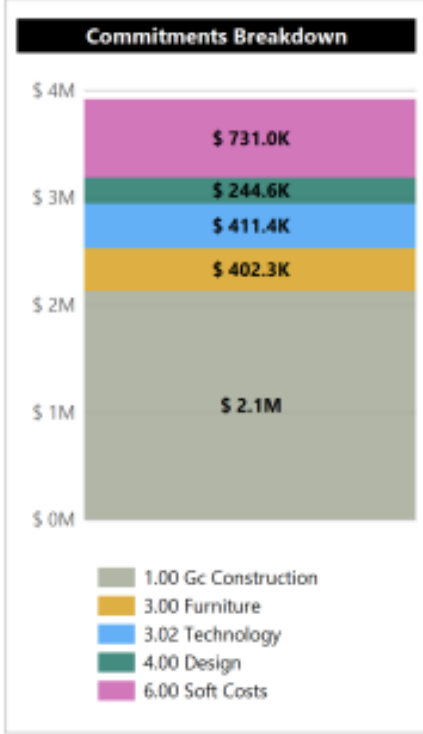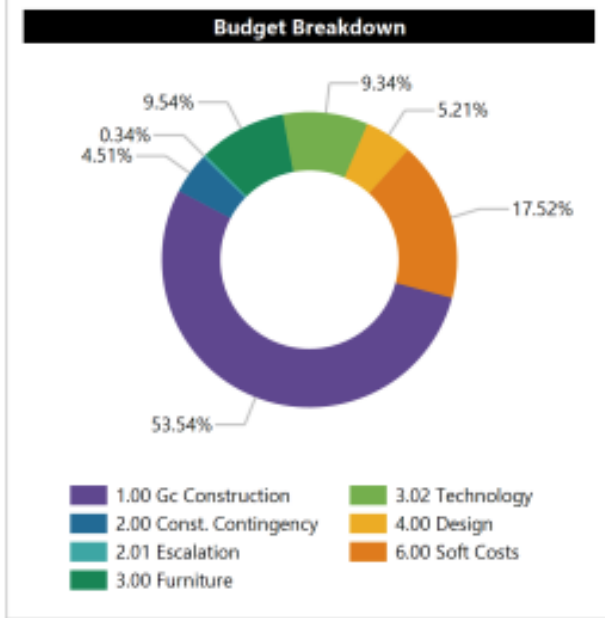

80% Complete

Modernization Plan

Classrooms: 19

Music Room: 1

Project Status

Construction

Grandview College Prep. Academy

Phase 1: 51-54 & 61-64
Complete

Phase 2: K-1, K-2, 32-33,
41, 43
Complete

Phase 3: B-4, Music/Band
Complete


Phase 4: 20-24
Next Phase



Site Plan & Status
Construction

Grandview College Prep. Academy

Construction Improvements

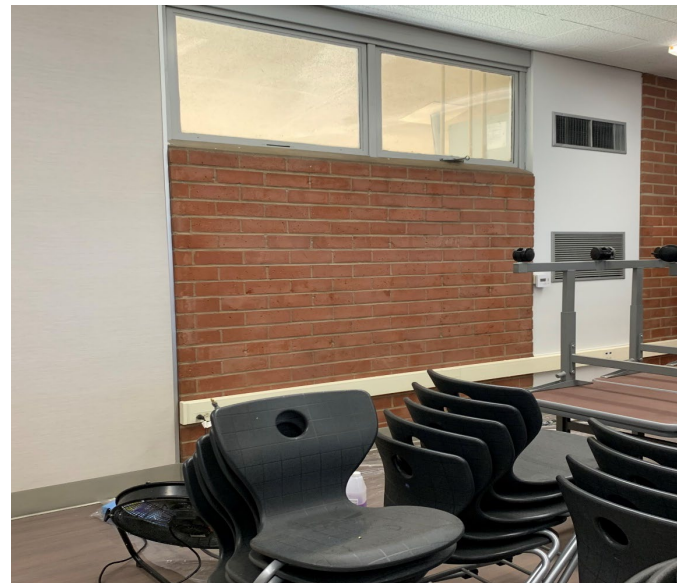

Project Status




Construction

Grandview College Prep. Academy

KPI Overview

GVCPA 21ST CENTURY CLASSROOM + 2 Other Projects

Budget	Committed	Balance
\$ 6.15M	\$ 4.47M 72.7%	\$ 1.68M 27.3%

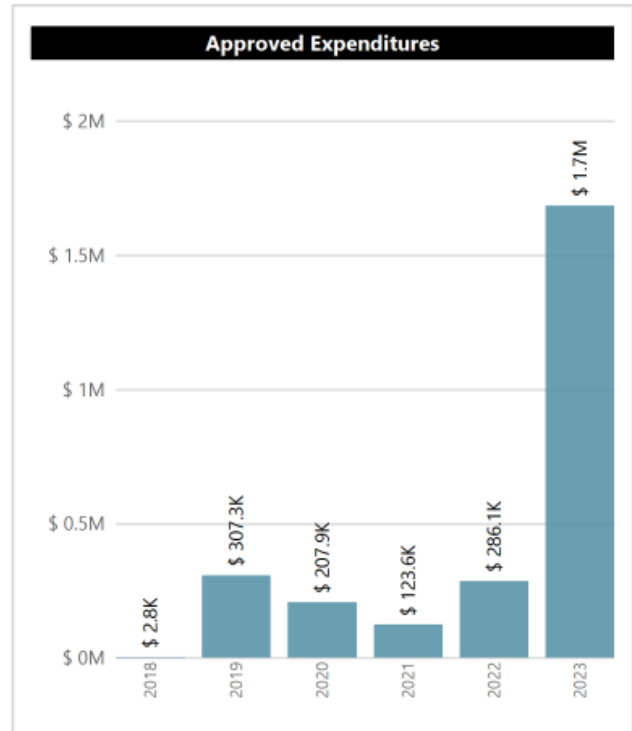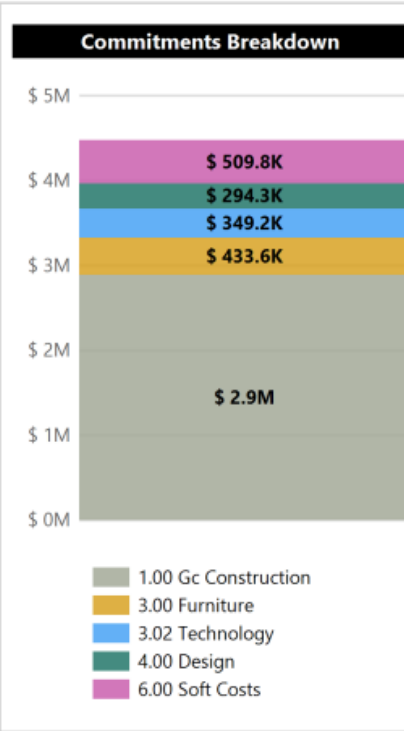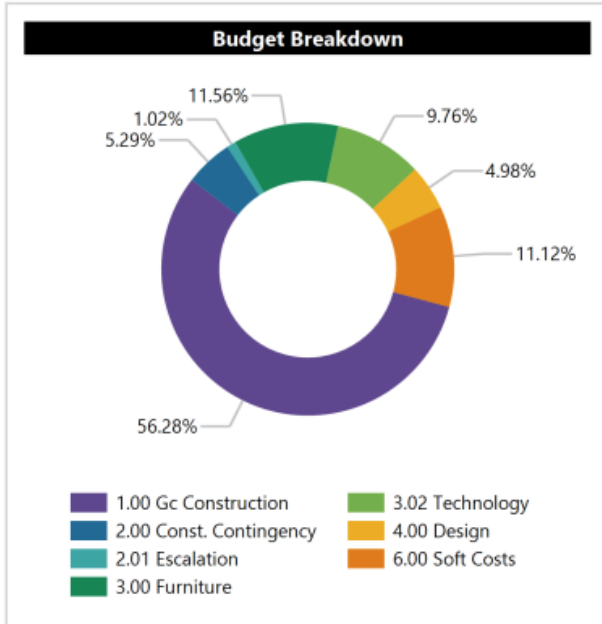

84% Complete

Project Status

Construction

Modernization Plan

Classrooms: 16

Music Room: 1

Kinder: 2

Sparks Middle School

Phase 1 : 9-16


Phase 2: 17-20

Music

Complete

Complete

Complete

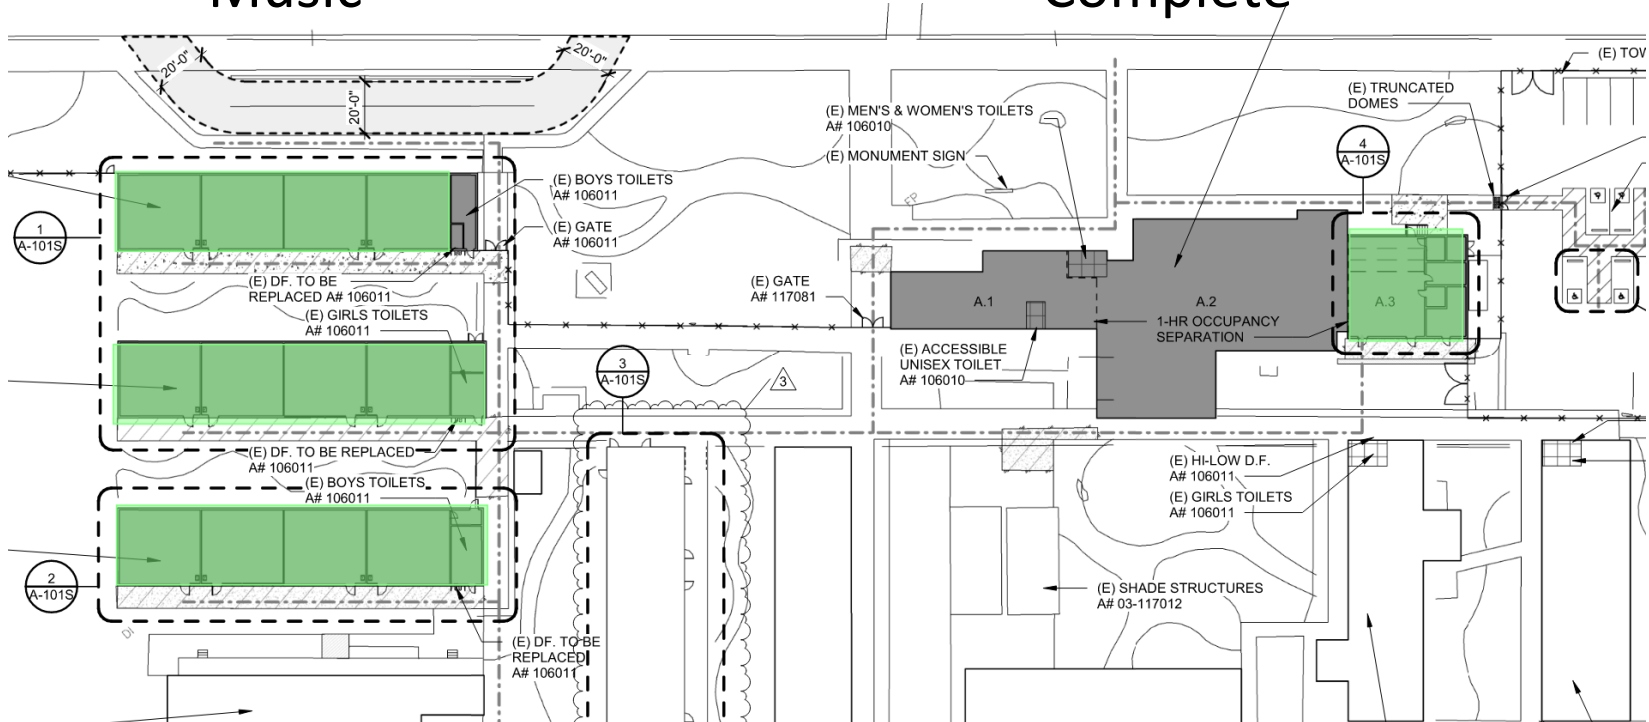

Site Plan & Status
Construction

Sparks Middle School



Project Status
Construction

Sparks Middle School



Project Status




Construction

Sparks Middle School

KPI Overview

SPKMS 21ST CENTURY CLASSROOM

Budget	Committed	Balance
\$ 3.59M	\$ 3.01M 83.9%	\$ 0.58M 16.1%

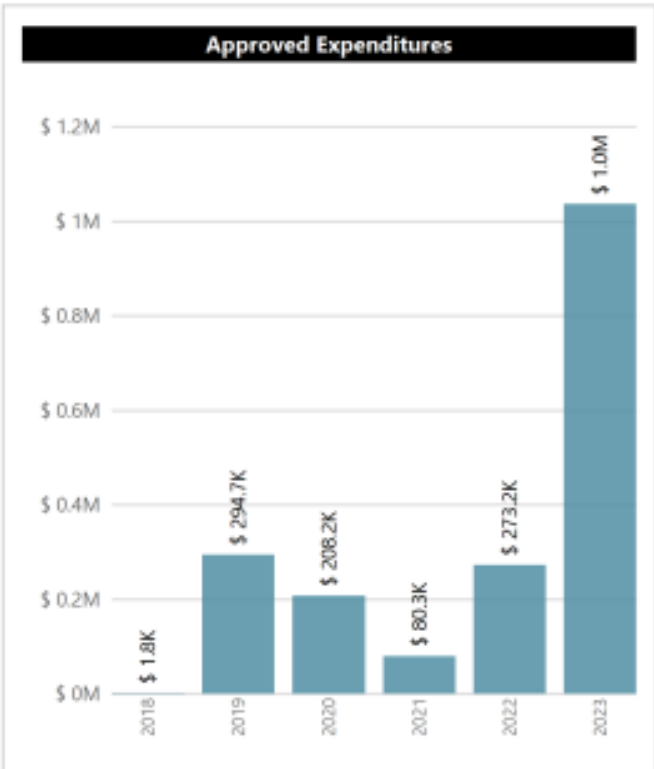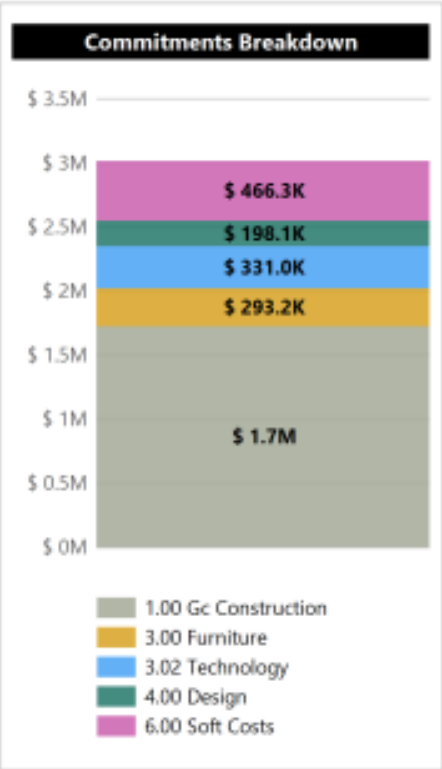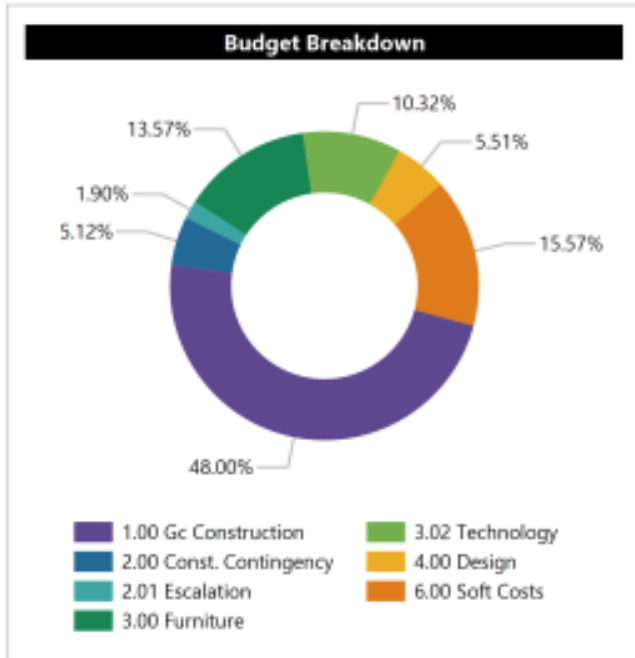

Complete

Modernization Plan

Classrooms: 12

Music Room: 1

Project Complete

94% billed and 11% Remaining

Project Status

Construction



Scheduled Completion

Sparks MS Complete


Grandview: September 2023

Newton MS: October 2023

HIGH SCHOOL REFRESH




● Rooms That Have Been Photographed and Cataloged

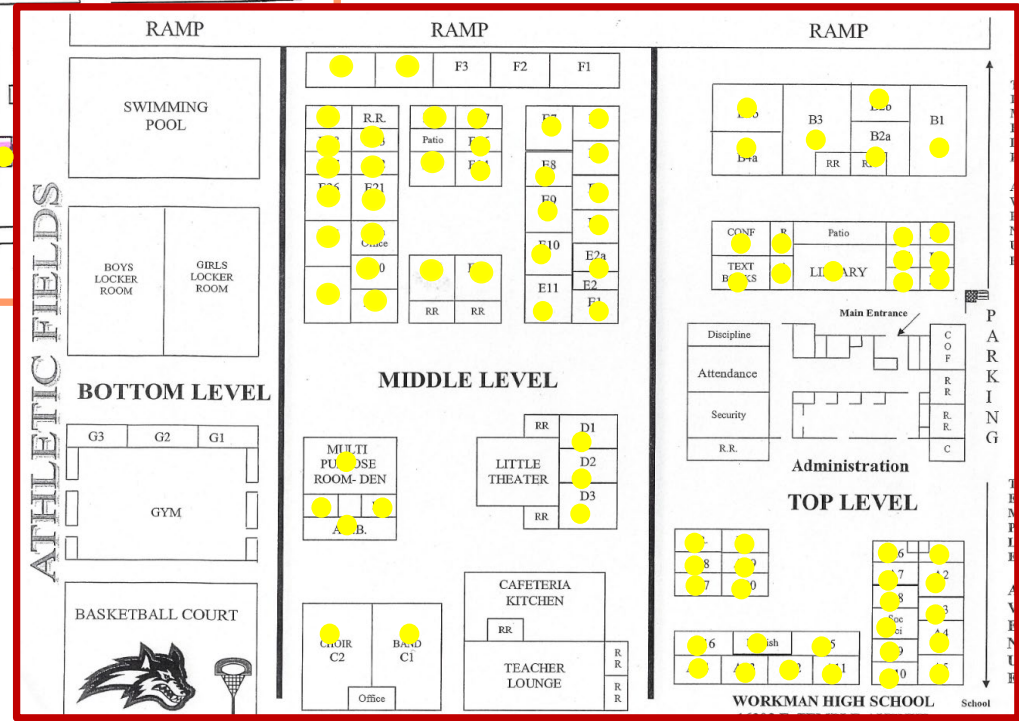

HIGH SCHOOL REFRESH

La Puente High School and Workman High School Option 1 and Option 2

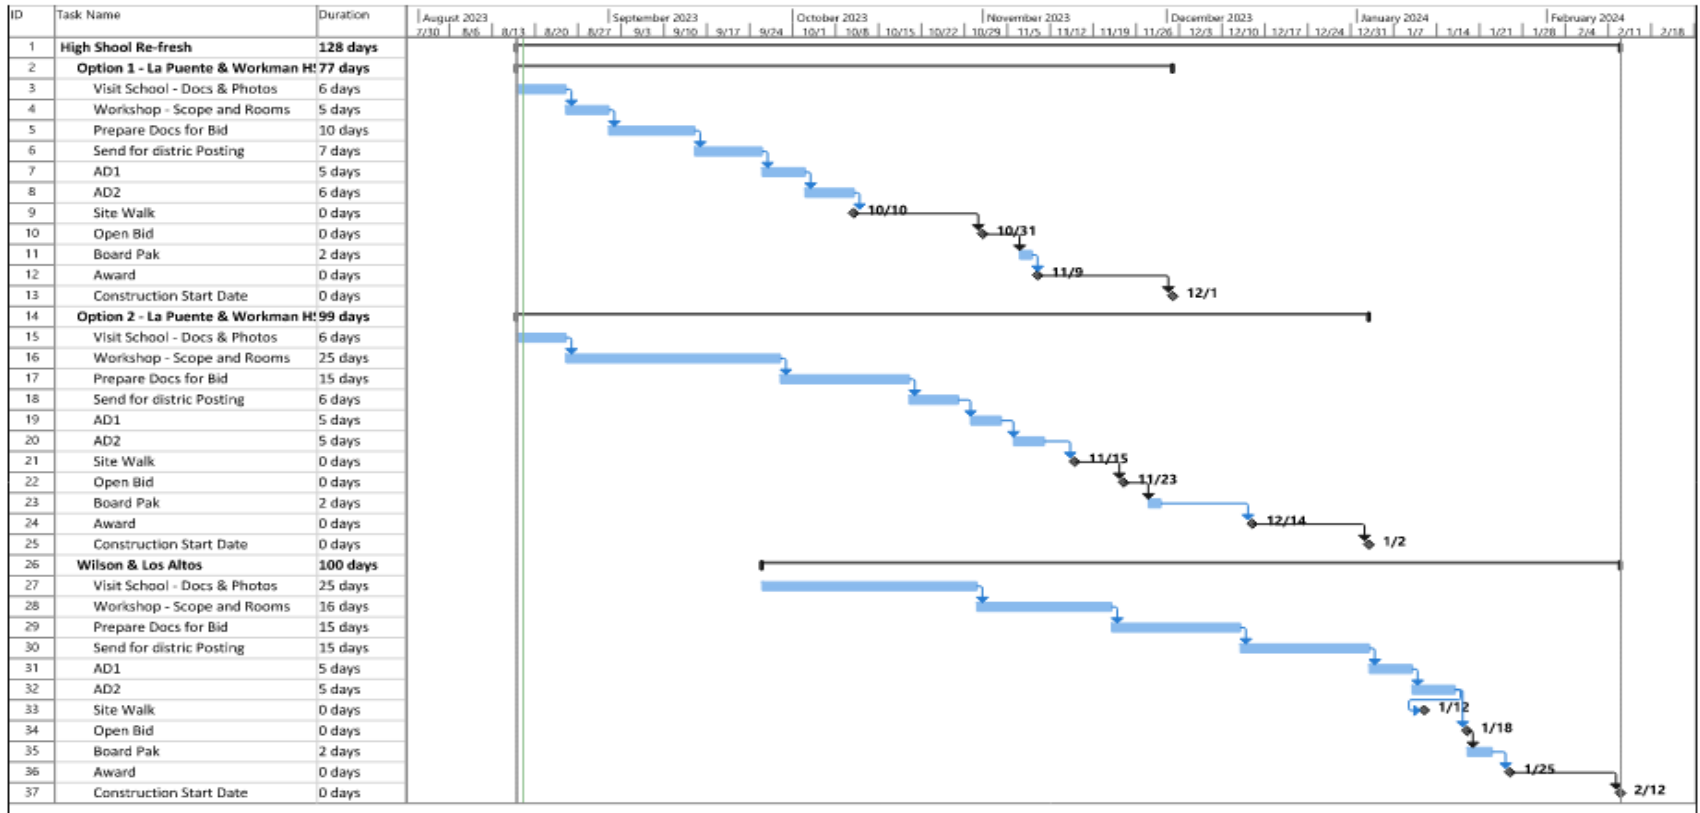


HIGH SCHOOL REFRESH

- La Puente High School
- Workman High School




Project Status

Measure BB Bond Phase B

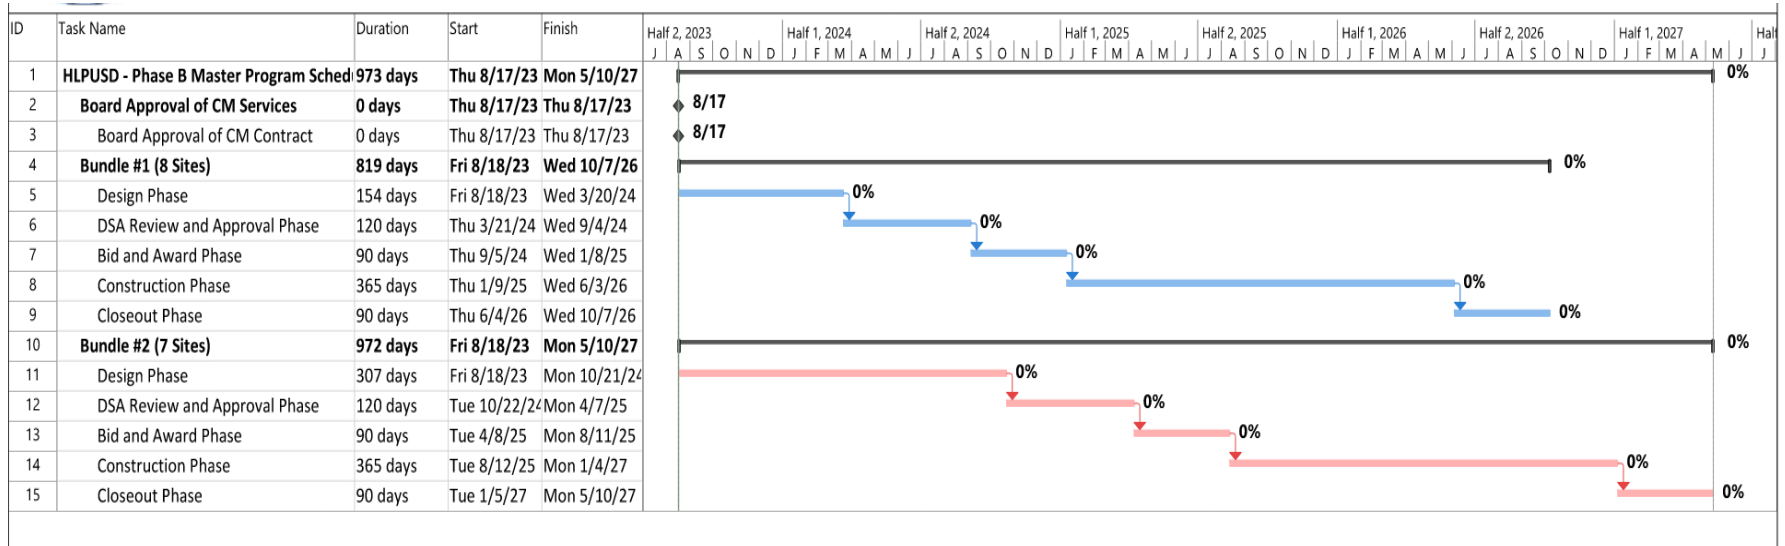

Contract Proposals Received From Studio + Architects
 Meeting and Site Visits Resumed
 Professional Fees negotiated

Request for Proposal Updates Out to PBK Architects
 Meeting and Site Visits In Planning



QUESTIONS + ANSWERS

CUMMING
Building Value Through Expertise
