

PHASE 1 - 05/25/17 - 08/11/17

PHASE 2 - 08/14/17 - 10/27/17

PHASE 3 - 10/30/17 - 01/05/18

PHASE 4 - 12/22/17 - 03/02/18

PHASE 5 - 03/05/18 - 05/11/18

PHASE 5.5 - 03/30/18 - 04/27/18


PHASE 6 - 05/14/18 - 09/07/18

PHASE X - Work within Phase in area or Holidays.

Weights to be relocated to New Cardio Room. Needs to go with Wrestling Room above. Spring Break abatement - March 30, 2018 thru April 6, 2018.

1ST FLOOR PHASING DRAFT

1/16" = 1'-0" U4.10.1 / 05-21-17

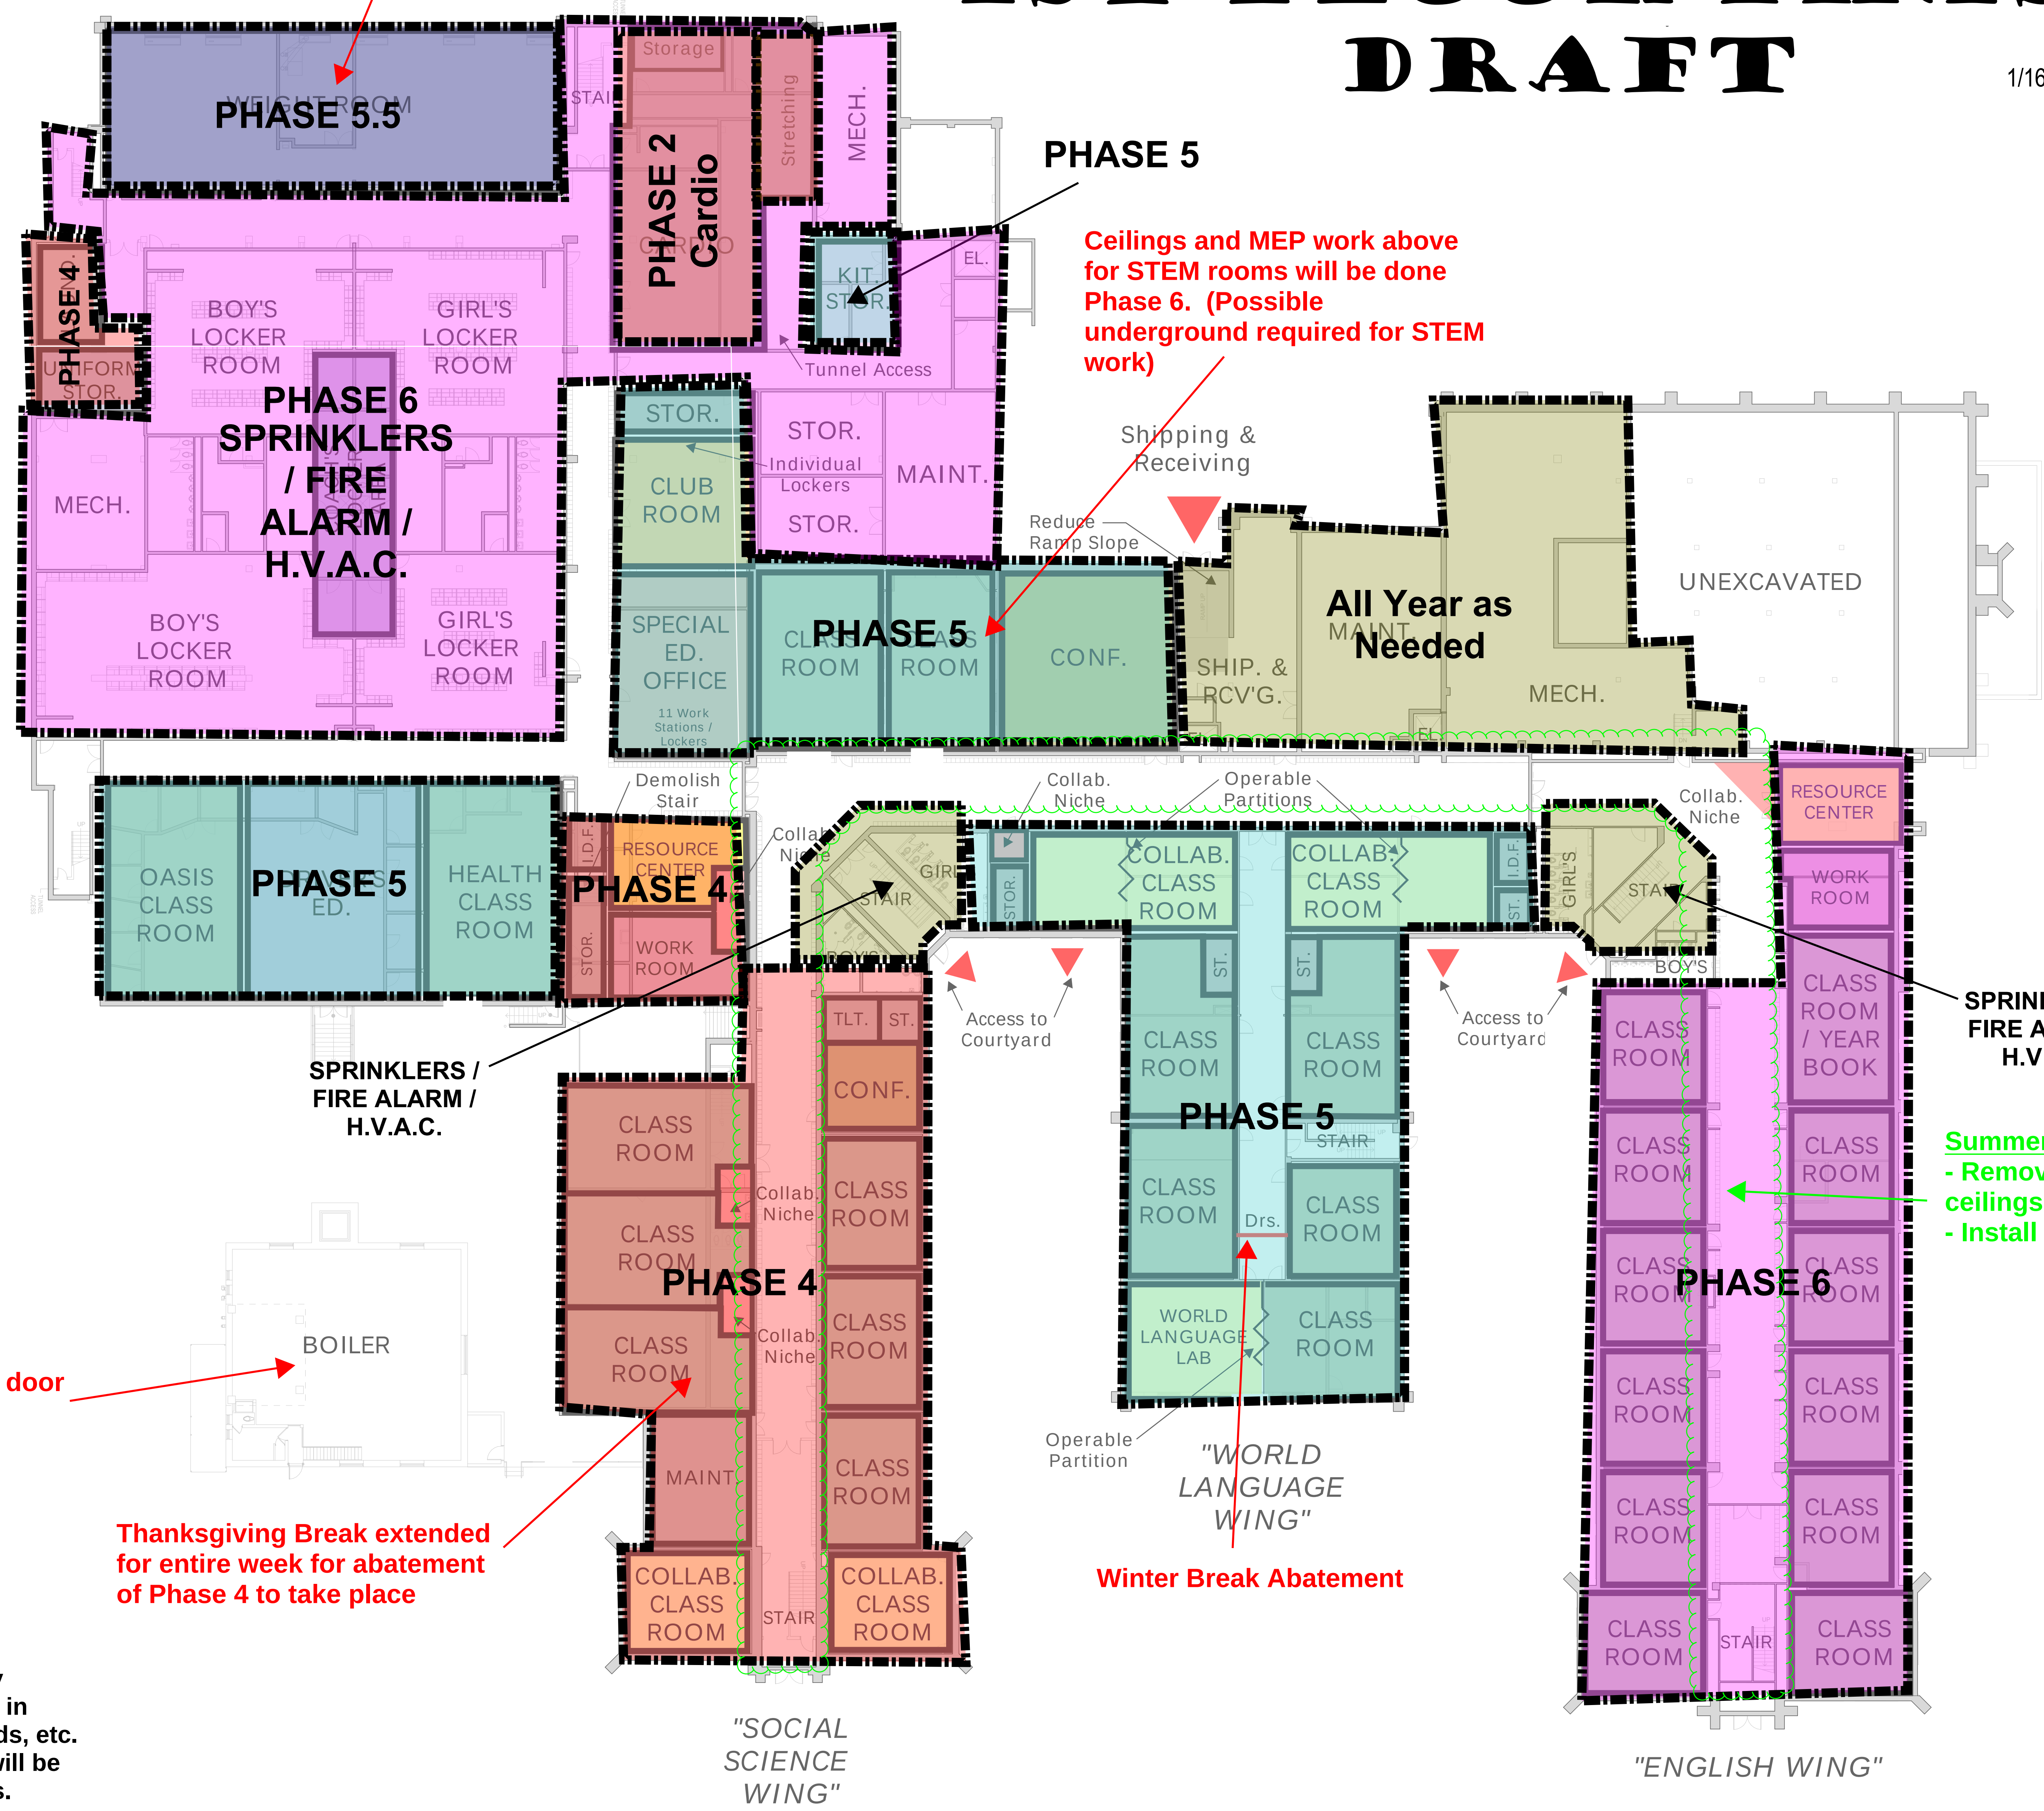

NOTE: Students with accessibility needs will be arranged/scheduled in classrooms to avoid elevator needs, etc. Injuries requiring crutches, etc. will be dealt with on a case by case basis.

Wrestling Room to go with Weight Room below. Spring Break abatement - March 30, 2018 thru April 6, 2018.

2ND FLOOR PHASING DRAFT

1/16" = 1'-0" 04.10.17

05-21-17

PHASE 5.5

COMMONS
SPRINKLERS
FIRE
ALARM /
H.V.A.C.

PHASE 6

***All site work would be Phase 6

All work MUST be completed no later than 09/29/17. HVAC work will be done later with access coordinated with LPSP

Summer 2017:
- Remove/Abate heating risers to 3rd floor (Work on 2nd Floor only)
- Remove Radiators above on floor also

SPRINKLERS /
FIRE ALARM /
H.V.A.C.

The Administration Wing will have **NO** heat as soon as Phase 6 construction begins in the English Wing below

***Mechanical Abatement and New Mechanical during Winter Break (HVAC work finished on 2nd Shift).

PHASE 1 - 5/25/17 - 8/11/17

PHASE 2 - 8/14/17 - 10/27/17

PHASE 3 - 10/30/17 - 1/5/18

PHASE 4 - 12/22/17 - 03/02/18

PHASE 5 - 03/05/18 - 05/11/18

PHASE 5.5 - 03/30/18 - 04/27/18

PHASE 6 - 05/14/18 - 09/07/18

PHASE X - Work within Phase in area and Holidays.

PHASE 5

SPRINKLERS /
FIRE ALARM /
H.V.A.C.

Phase 6
SUMMER
2018

Phase 4

Phase 1

Phase 1
& 6

Phase 6

PHASE 6

"ADMINISTRATION
WING"

"ARTS
WING"

"LIBRARY
WING"



LaSalle-Peru High School

Interior Renovations

KMETZARCHITECTS, INC.


LEGATARCHITECTS
SUSTAINABILITY | PERFORMANCE | DESIGN

Pepper
CONSTRUCTION

- PHASE 1 - 05/25/17 - 08/11/17
- PHASE 2 - 08/14/17 - 10/27/17
- PHASE 3 - 10/30/17 - 01/05/18
- PHASE 4 - 12/22/17 - 03/02/18
- PHASE 5 - 03/05/18 - 05/11/18
- PHASE 5.5 - 03/30/18 - 04/27/18
- PHASE 6 - 05/14/18 - 09/07/18
- PHASE X - Work within Phase in area and Holidays.

3RD FLOOR PHASING DRAFT

1/16" = 1'-0" 04.10.17
05-21-17

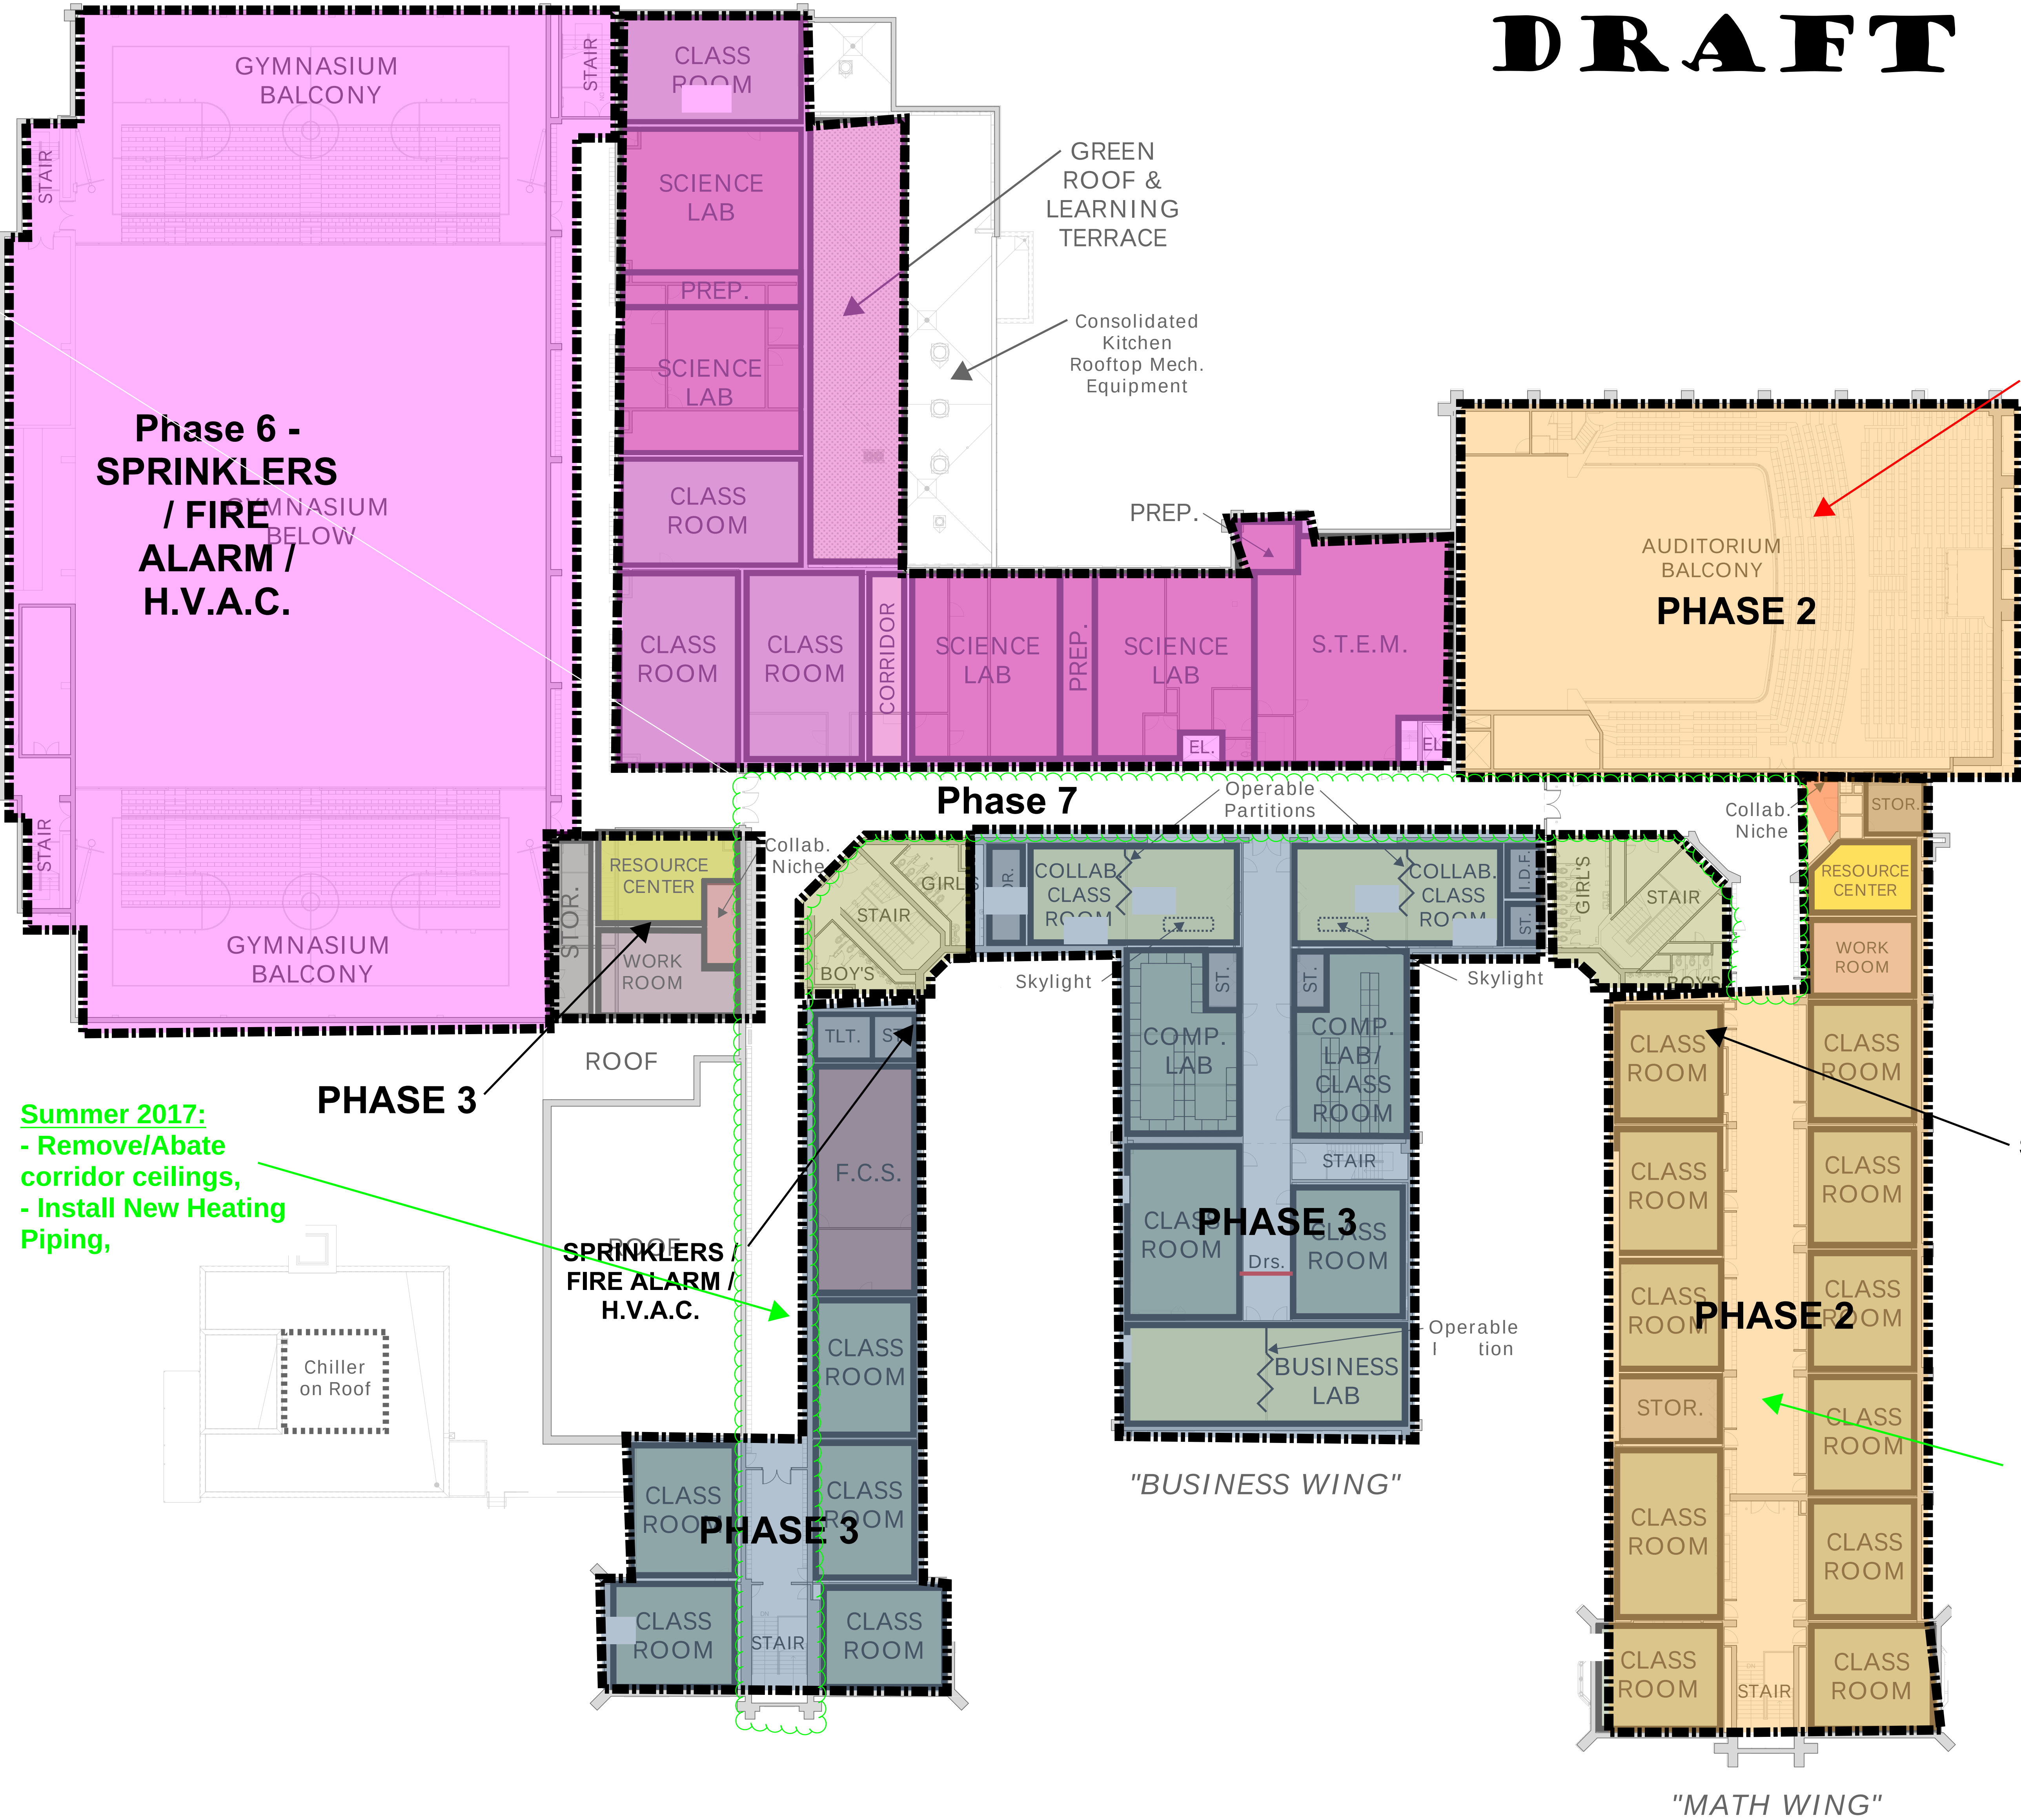

All work MUST be completed no later than 09/29/17. HVAC work will be done later with access coordinated with LPSD

SPRINKLER S / FIRE ALARM / H.V.A.C.

Summer 2017: Complete abatement of Math Wing



LaSalle-Peru High School

Interior Renovations

KMETZARCHITECTS, INC.

LEGATARCHITECTS
SUSTAINABILITY | PERFORMANCE | DESIGN

