




Mary E. Britton Middle School

➤ Completed Work:

- ICF to roof bearing elevation Area A and Area C – Pour 9.28.23
- ICF continuing at Area B and Area D
- Trusses installed at Gym
- CMU Topping out to mechanical platform Area A
- Continue CMU at Area C
- Topping Slab Area C to 95%
- Structural Steel At Area B and Area D continuing
- Continue to drill and grout geothermal wells (could be loud)
- Above Ceiling Sprinkler in Area A
- Above Ceiling Domestic and Chemical Piping Area A to 50%
- Above Ceiling Duct Area A – 85% of Main Trunk and Branch Duct installed
- Above Ceiling Duct Area C – 95% Complete Main Trunk and Branch Duct
- Started pulling wire at Area A
- Grease Trap Installed

➤ Upcoming Work/Look Ahead:

- Truss Complete at GYM
- Truss Complete at Kitchen Mechanical Room
- ICF to Mechanical Platform complete Area A and Area C
- Structural Steel at Area B and Area D complete
- Geothermal Wells complete.
- Continue Sprinkler and MEP Above Ceiling Rough In
- Site Sanitary Sewer Start
- Start Air Barrier at Gym
- Schedule Next ICF Pour – Tie together A and C to B and D

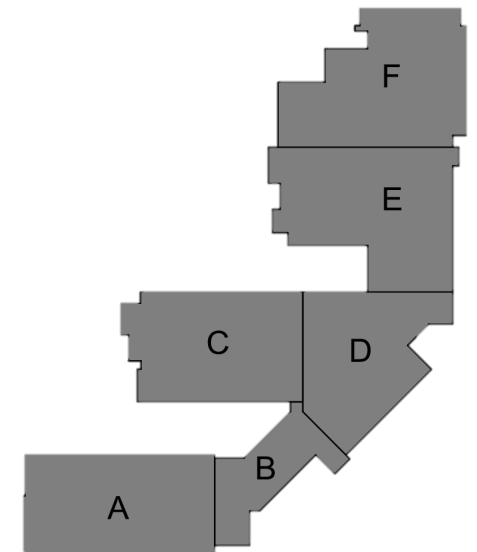

Mary E. Britton Middle School



Area A - Topping Pour on 2nd Floor



Week Ending September 29, 2023

Mary E. Britton Middle School



Area A - ICF Stacked up to Finish Height



Week Ending September 29, 2023

Mary E. Britton Middle School



Area B - Media Center 2nd Floor in Place



Week Ending September 29, 2023

Mary E. Britton Middle School



Area C - CMU Continues on the 2nd Floor



Week Ending September 29, 2023

Mary E. Britton Middle School

Area D - Hollow Core Plank Install Continues



Week Ending September 29, 2023

Mary E. Britton Middle School



Area E - Steel Set at Stage



Week Ending September 29, 2023

Mary E. Britton Middle School



Area F - Setting Trusses in the Gym



Week Ending September 29, 2023

Mary E. Britton Middle School



Site - Geothermal Well Field Drilling Continues



Week Ending September 29, 2023
