




Mary E. Britton Middle School

➤ Completed Work:

- Continue ICF at Cafeteria
- ICF at Gym, Kitchen Mechanical Room Topped out (11/19 Pour)
- Start Decking at Gym Area
- Complete Roof Joist at Kitchen & Mechanical Space
- Complete CMU at Area A
- Continue MEP Rough in overhead and wall multiple areas
- Air Barrier Application at Gym Area
- All geothermal wells complete and continue header piping
- Continue Site Sanitary
- Steel Erection in Multiple Areas
- Exterior Air Barrier Continuing
- KAW subcontractor delivered ductile iron pipe for water line install

➤ Upcoming Work/Look Ahead:

- Set Hollow Core at C platform to CJ line
- Set Hollow Core at B Platform
- Set Hollow Core at D Platform
- Continue ICF at Cafeteria, B and D Areas
- ICF South Wall of Area C
- Start water line service
- Continue Air Barrier
- Continue MEP and Sprinklers various areas
- Continue erecting steel Area F, B and D
- Finish CMU to platform level Area A
- Hollow Core Area A set for Nov 1.

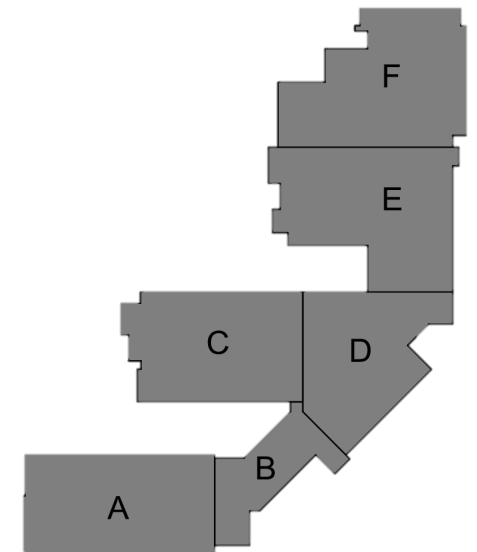

Mary E. Britton Middle School



Area A – MEP Above Ceiling Continues



Week Ending October 20, 2023

Mary E. Britton Middle School



Area C – 2nd Floor CMU Continues in the Corridor



Week Ending October 20, 2023

Mary E. Britton Middle School



Area D – 2nd Floor CMU Continues in Restrooms



Week Ending October 20, 2023

Mary E. Britton Middle School



Area D -2nd Floor Slab Poured over Hollow Core Planks



Week Ending October 20, 2023

Mary E. Britton Middle School



Area D 2nd Floor Steel Installed for Landings



Week Ending October 20, 2023

Mary E. Britton Middle School



Area E – Steel Joists Installed in Kitchen



Week Ending October 20, 2023

Mary E. Britton Middle School



Area F – Air Barrier Started at the Gym Locker Room



Week Ending October 20, 2023

Mary E. Britton Middle School



Area F – Decking has begun in Gym



Week Ending October 20, 2023
