




Mary E. Britton Middle School

➤ Completed Work:

- Set Hollow Core at Area C platform to CJ line
- Set Hollow Core at Area B Platform
- Set Hollow Core at Area D Platform
- Continue ICF at Cafeteria, Areas B and D
- ICF South Wall of Area C
- Continue Air Barrier around the building on ICF
- Continue MEP and Sprinklers various Areas
- Continue erecting steel in Area F, B and D
- Finish CMU to platform level in Area A
- Hollow Core Area A set for Nov 1.

➤ Upcoming Work/Look Ahead:

- Set Hollow Core at Area A Platform
- Complete Hollow Core at Area B and D
- Complete Gym Roof Structure
- Complete Kitchen/Mechanical Roof Structure
- Finish topping slab at Area D
- Prep Topping Slab at Area C platform
- Continue ICF at Area E Cafeteria
- Start ICF at Storm Structure above 15'
- Continue MEP and Sprinkler various Areas
- CMU at Stage Area and Cafeteria
- Roof systems Mobilization and materials delivery

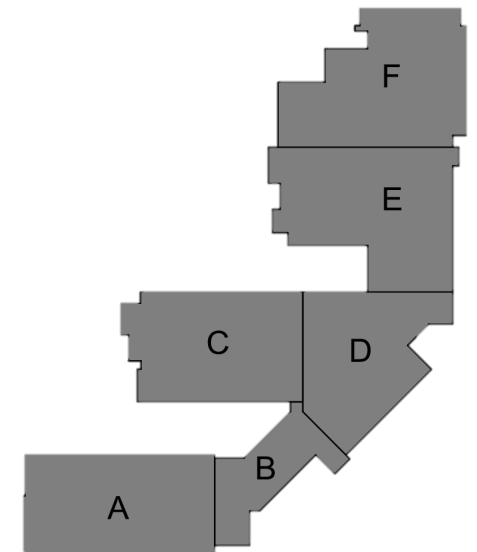

Mary E. Britton Middle School



Area A – Platform CMU Topped Out



Week Ending October 27, 2023

Mary E. Britton Middle School



Area B – 2nd Floor Steel Structure Setting



Week Ending October 27, 2023

Mary E. Britton Middle School



Area B – Flex Window and Sliding Door Opening at 2nd Floor



Week Ending October 27, 2023

Mary E. Britton Middle School



Area D – Continuing Walls to Roof



Week Ending October 27, 2023

Mary E. Britton Middle School

Area E – Continuing ICF Walls at Cafeteria



Week Ending October 27, 2023

Mary E. Britton Middle School



Area E – Platform Planks Set and Ready for Topping



Week Ending October 27, 2023

Mary E. Britton Middle School



Area F – Acoustical Decking Installed at Gym



Week Ending October 27, 2023

Mary E. Britton Middle School



Area F – Gym Locker Room Parapet Blocking Installed



Week Ending October 27, 2023
