



Saint Paul
PUBLIC SCHOOLS

Major Capital Projects:

Board of Education monthly progress update

FACILITIES DEPARTMENT

October 2023



Project Timeline

1. Gate Check 1: Five-Year Capital Improvement and Deferred Maintenance Implementation Plan

Work identified in the five-year plan has been prioritized over the represented five-year horizon. Specificity of scope, schedule and budget vary for projects contained in the plan.

Board action requested: Approval of prioritization of work as represented in the plan.

2. Gate Check 2: Project Charter

The project charter is a product of internal pre-design work for projects estimated to be over two million dollars. The project charter contains the defined scope based on the evaluation of building condition, programmatic need, and initial stakeholder engagement. The preliminary schedule and project estimate are included.

Board action requested: Approval of the project charter indicating acceptance of the identified scope and understanding of the project schedule and rough order of magnitude of cost. Approval indicates the Board's direction to issue a request for proposal to secure design services.

3. Gate Check 3: Project Budget

Once a project has moved through schematic design, solutions have been identified and developed with sufficient detail to estimate a construction cost and set a final project budget. Finalization of the design and construction drawings will be informed by this budget.

Board action requested: Approval of final project budget. Approval indicates the Board's direction to proceed with construction bidding so long as the project remains within the allotted budget.

4. Gate Check 4: Construction Award

Per public procurement practices, work will be advertised for bid and bids will be received by the Purchasing Office and vetted for response compliance. Project consultants will vet the value of bids against anticipated costs and provide the District with a formal recommendation to award based on the lowest responsible bid.

Board action requested: Approval of vetted and recommended vendors to award work and enter into contractual agreement for construction.

5. Gate Check 5: Project Closeout

This gate check will be presented at the beginning of the project closeout phase and again upon final fiscal closeout of the project. The project closeout period begins at substantial completion of construction. The Substantial Completion certificates indicate beneficial occupancy and shift of focus to completion and inspection of punchlist items and entry into warranty period. There are still outstanding financial obligations during the closeout phase of the project, but an initial evaluation of the overall use of budget can be conducted. The second presentation of this gate check will occur when all contractual obligations are complete and all final payments have been issued. This can occur twelve to eighteen months after completion of construction. Except in the rare circumstance in which Substantial Completion and final closeout occur simultaneously, the Board will see the following two reports during this gate check:

- Gate Check 5.1: Initial Project Closeout (Substantial Completion)
- Gate Check 5.2: Final Project Closeout

Board action requested: Acceptance of report(s).

Project Financial Information

- A. Rough Order of Magnitude Cost Estimate:** In the initial planning phase, the cost of a project gets refined along the way as the scope of work is fine tuned and more in-depth information is gathered on the condition of the building and overall site. Through this process, the initial costing evolves from a rough estimate referred to as a "Rough Order of Magnitude" to a final budget. (Presented to the Board at Gate Check 1 and 2.)
- B. Original Budget:** Final project budget approved by the Board at Gate Check 3.
- C. Committed Costs:** Contractual obligation of funds for project work.
- D. Invoiced to Date:** Invoices are submitted and approved through Procore, the project management environment used by the District. The value represented indicates all invoices submitted and approved by the project team.
- E. Construction Award:** Total of all construction contracts.
- F. Construction Cost Changes:** Value of all change orders issued to construction contracts.
- G. Percent Change:** Calculation of construction change orders against total construction award.
- H. Total Forecasted Cost:** Anticipated cost of the fully delivered project at the time of the report including known committed, pending, and potential costs as identified by the project team.
- I. Construction Percent Complete (as invoiced):** Percent of completion is calculated based on the value of work in place as indicated on the vetted and approved pay applications submitted by contractors against the total value of construction commitments. As this is based on billed amounts, there is frequently a 30-60 day lag to represent the work in full.



American Indian Magnet: October 2023 Project Update



Location: 1075 Third St. E., Saint Paul, MN 55106

Grades: PreK-8

Enrollment (SY20-21): 611

Project website: spps.org/aimsfmp

School website: spps.org/aims

Project summary

Project number: 1160-19-01

Funding: Certificates of Participation (COP)

Project type: Addition and renovation

Square footage:

- Existing: 103,000 sf
- Proposed: 131,626 sf

SPPS project team:

- Michelle Bergman Aho, Project Manager
- Kenny Ekblad, Project Coordinator

Design team: Cuningham Group

Construction management: H+U Construction

Project scope

- Additions with new PreK-8th grade classrooms, administration area, media center (Long House), kitchen, and cafeteria.
- New playground and site improvements.
- Renovation of existing building including learning spaces, academic support spaces and restrooms.
- Replacement of all finishes, HVAC and controls, plumbing, lighting, required upgrades to fire suppression and fire alarm systems.

New this month

- The second-floor renovations will be completed by the end of October with final electrical, classroom AV, and flooring.
- In November, work will shift to first-floor renovations for the remainder of the project.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$53,300,000	\$47,089,651	\$40,510,277	\$33,756,040	\$2,912,439	8.63%	\$47,398,208	88.21%

Project Timeline

Phase: Planning → Design → Construction →					
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout
Key dates:	✓ Oct. 2018	☐ N/A	✓ Feb. 2020	✓ May 2020	☐ Fall 2024

American Indian Magnet



From top: New carpeting installed in second-floor medium group room; flooring prepped for rubber tile installation (September 2023)



Saint Paul
PUBLIC SCHOOLS

Barack and Michelle Obama: October 2023 Project Update

Location: 707 Holly Ave., Saint Paul, MN 55104

Grades: PreK-8

Proposed enrollment: PK-5: 450; Middle school: 450

Project website: spps.org/obama-builds

Project summary

Project number: 3210-23-01

Funding: Certificates of Participation, Long Term Facilities Maintenance

Project type: Renovations and remodel

Square footage:

- Existing: 141,662 sf
- Proposed: 146,496 sf

SPPS project team:

- Michelle Bergman Aho, Project Manager
- Jhalil Payne, Project Coordinator

Design team: Snow Kreilich Architects

Construction management: H+U

Project scope

- Construction project is an outcome of [Envision SPPS](#); will house both the Montessori PreK-5 program currently located at JJ Hill along with a new, independent middle school
- Renovation of general learning space, gym, cafeteria, media center, art room, administration office
- New identifiable and secure entry, parent room, kitchen addition, [inclusive restrooms](#)
- New electrical and mechanical systems

New this month

- Asbestos flooring tile has been removed in all hallways and identified classrooms.
- Bid package 1 with the demolition scope is out for bid and are due on October 10.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$72,300,000	\$6,157,116	\$1,930,258	Pending	\$0	0%	\$72,300,000	0%

Project Timeline

Phase: Planning → Design → Construction →					
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout
Key dates:	✓ March 2021	✓ Aug. 2022	✓ Jan. 2023	☐ TBD	☐ Fall 2025

Barack and Michelle Obama



Hallway after asbestos abatement (September 2023)



Saint Paul
PUBLIC SCHOOLS

Bruce Vento Elementary: October 2023 Project Update



Location: 409 Case Avenue, Saint Paul, MN 55130

Grades: PreK-5

Enrollment (SY22-23): 540

Project website: spps.org/vento-builds

School website: spps.org/vento

Project summary

Project number: 1020-22-01

Funding: Certificates of Participation

Project type: New construction

Square footage:

- Existing: 101,231 sf
- Proposed: 164,000 sf

SPPS project team:

- Pam Bookhout, Project Manager
- Maria Wollensak, Project Coordinator

Design team: Cuningham Group

Construction management: RJM Construction

Project scope

- New building constructed on east side of property
- Sustainability features include high-performance building envelope, geoexchange system, and preparation for photovoltaic panels
- Playground for elementary and early childhood programs, and general play area
- Separate parent and bus drop-offs
- Staff and visitor parking (limited)
- Stormwater management addressing site elevation

New this month

- The second of two bid packages was published and contracts will likely be presented to the Board of Education in October.
- Soil work began and additional soil evaluation is complete.
- Design drawings for building piers (rammed aggregate piers) have begun and installation of the building piers will begin in October.
- New egress path from the school has been completed.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete* (as invoiced)
\$89,900,000	\$26,330,984	\$2,919,037	Pending	\$0	0%	\$89,900,000	0%

Project Timeline

Phase: Planning → Design →					Construction →
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout*
Key dates:	✓ March 2021	✓ Aug. 2022	✓ Feb. 2023	☐ TBD	☐ Fall 2025

*The stated closeout date represents substantial completion and occupation of the new construction; additional site work will continue through summer 2026.

Saint Paul Public Schools ▪ Facilities Department ▪ 1930 Como Avenue ▪ Saint Paul, MN 55108

Ph: 651-744-1800 ▪ Fax: 651-290-8362 ▪ facilities@spps.org ▪ spps.org/builds

Bruce Vento Elementary



From top left: Groundbreaking event on September 28; grading for new egress path; finished egress path (September 2023)



Saint Paul
PUBLIC SCHOOLS

Education and Operations Services: October 2023 Project Update

Location: 1930 Como Ave., Saint Paul, MN 55108

Number of employees: Approximately 230 staff

Project summary

Project number: 4000-22-01

Funding: American Rescue Plan

Project type: HVAC upgrades

Square footage:

- Existing: 228,836 SF
- Proposed: N/A

SPPS project team:

Jason Jones, Project Manager

Design team: TKDA

Construction team: Morcon

Project scope

- Replace existing air handling units with new one
- Add A/C condensing units on roof
- Improve ventilation in maintenance office area

New this month

- Mechanical unit delivery is still on schedule for delivery at then end of November/early December for a winter break switchover.
- Existing utility relocation has been completed.
- Asbestos was abated over the new mezzanine platform to prepare for utility relocations.
- Electrical panel upgrades occurred in October as the EOS kitchen will not be in use after mid-October.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$3,052,402	\$2,031,305	\$667,626	\$1,426,314	\$287,662	20.17%	\$2,048,305	30.22%

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i> →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout		
Key dates:	<input type="checkbox"/> N/A	<input type="checkbox"/> N/A	<input checked="" type="checkbox"/> Dec. 2021	<input checked="" type="checkbox"/> Aug. 2022	<input type="checkbox"/> Winter 2024		

Saint Paul Public Schools ▪ Facilities Department ▪ 1930 Como Avenue ▪ Saint Paul, MN 55108

Ph: 651-744-1800 ▪ Fax: 651-290-8362 ▪ facilities@spps.org ▪ spps.org/builds



Hidden River Middle School: October 2023 Project Update



Location: 1700 Summit Ave., Saint Paul, MN 55105

Grades: 6-8

Enrollment (SY22-23): 568

Project website: spps.org/hiddenriver-builds

School website: spps.org/hiddenriver

Project summary

Project number: 3140-20-02

Funding: Certificates of Participation (COP) and Capital Bonds

Project type: Remodel and addition

Square footage:

- Existing: 82,322 SF
- Proposed: Renovation: 89,621 SF; Addition: 9,613 SF

SPPS project team:

- Angela Otteson, Project Manager
- Josie Geiger, Project Coordinator

Design team: DLR Group

Construction management: Kraus-Anderson

Project scope

- New administrative offices in two-story addition
- Clearly marked main entrance with new secure entry
- Renovated and reconfigured classrooms
- Kitchen renovation, inclusive restrooms
- New instructional audio/visual equipment
- HVAC and controls replacement, electrical replacement, and other systems improvements
- Partial roof replacement, window replacements, parking lot pavement

New this month

- Bid package 2 construction bids were received September 19; recommended bids will be presented for approval by the Board of Education in October.
- Construction meetings will soon begin for the Wilson renovations to right-size classrooms and expand the cafeteria before students temporarily move in for SY2024-25.


October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$54,200,000	\$7,463,656	\$2,424,207	Pending	\$0	0%	\$54,200,000	0%

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i>							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout		
Key dates:	✓ March 2021	✓ March 2021	✓ Sept. 2022	☐ TBD	☐ Fall 2025		

Hidden River Middle School

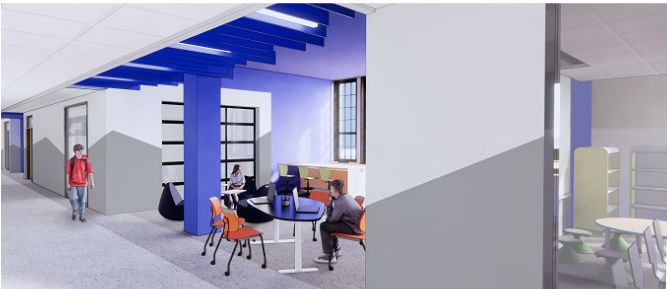

From top, then left to right: Cafeteria looking toward media center doors; new main entry with stairs to second floor; learning commons in building's classroom area; view down hallway looking towards flex classroom, image also shows color wayfinding; media center learning stair connected to cafeteria (April 2023)



Highland Park Middle School - HVAC: October 2023 Project Update



Location: 975 S Snelling Ave., Saint Paul, MN 55116

Grades: 6-8

Enrollment (SY21-22): 721

Project website: spps.org/Page/41781

School website: spps.org/highlandms

Project summary

Project number: 3081-22-02

Funding: American Rescue Plan

Project type: HVAC upgrades

Square footage:

- Existing: 135,431 SF
- Proposed: N/A

SPPS project team: Jason Jones, Project Manager

Design team: ATS&R

Construction team: Knutson Construction

Project scope

- Remove existing uni-vents in rooms
- Provide classrooms with cooling by installing a new dedicated outdoor air system unit on roof
- Replace existing fin tube radiation with new ones
- New LED lighting and ceiling in classrooms and hallways

New this month

- Phase 1 of the HVAC project is now complete; finalizing and closing out a few punch list items and faculty requests.
- Phase 2 will begin at the end of this school year in June and will be completed over summer 2024.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$6,484,217	\$5,485,296	\$2,769,284	\$4,315,320	\$163	- 1%	\$5,505,960	54.32%

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i> →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award			Closeout
Key dates:	<input type="checkbox"/> N/A	<input type="checkbox"/> N/A	<input checked="" type="checkbox"/> Dec. 2021	<input checked="" type="checkbox"/> Aug. 2022			<input type="checkbox"/> Fall 2023



Highland Park Middle School - Renovation: October 2023 Project Update



Location: 975 S Snelling Ave., Saint Paul, MN 55116

Grades: 6-8

Enrollment (SY22-23): 805

Project website: spps.org/Page/46814

School website: spps.org/highlandms

Project summary

Project number: 3081-23-01

Funding: Certificates of Participation, Long Term Facilities Maintenance

Project type: Addition and renovation

Square footage:

- Existing: 168,968 SF
- Proposed: 19,560 SF

SPPS project team:

- Mike Christen, Project Manager
- Jhalil Payne, Project Coordinator

Design team: ATS&R

Construction team: Kraus-Anderson Construction

Project scope

- New identifiable front entrance and main office
- Two-story link addition
- Fully-remodeled kitchen and cafeteria
- Renovated special education suite
- Updated classroom technology
- Gym floor replacement; substantial renovations of existing spaces
- Inclusive restrooms
- Replacement of sidewalks, ramps and landings; updates to parking lot with new parent drop-off lane
- Stormwater management and landscaping

New this month

- Project team is preparing construction documents with plans to publish bids in November.
- Project is still on target to begin April 2024 with phase 1 work on the new front entry and administration addition.
- SPPS Trades team has reviewed the design and plans specifications.


October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$49,500,000	\$2,166,747	\$499,289	TBD	\$0	0%	\$49,500,000	0%

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i> →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout		
Key dates:	✓ March 2021	✓ Sept. 2022	✓ July 2023	☐ TBD	☐ Fall 2025		

Highland Park Middle School

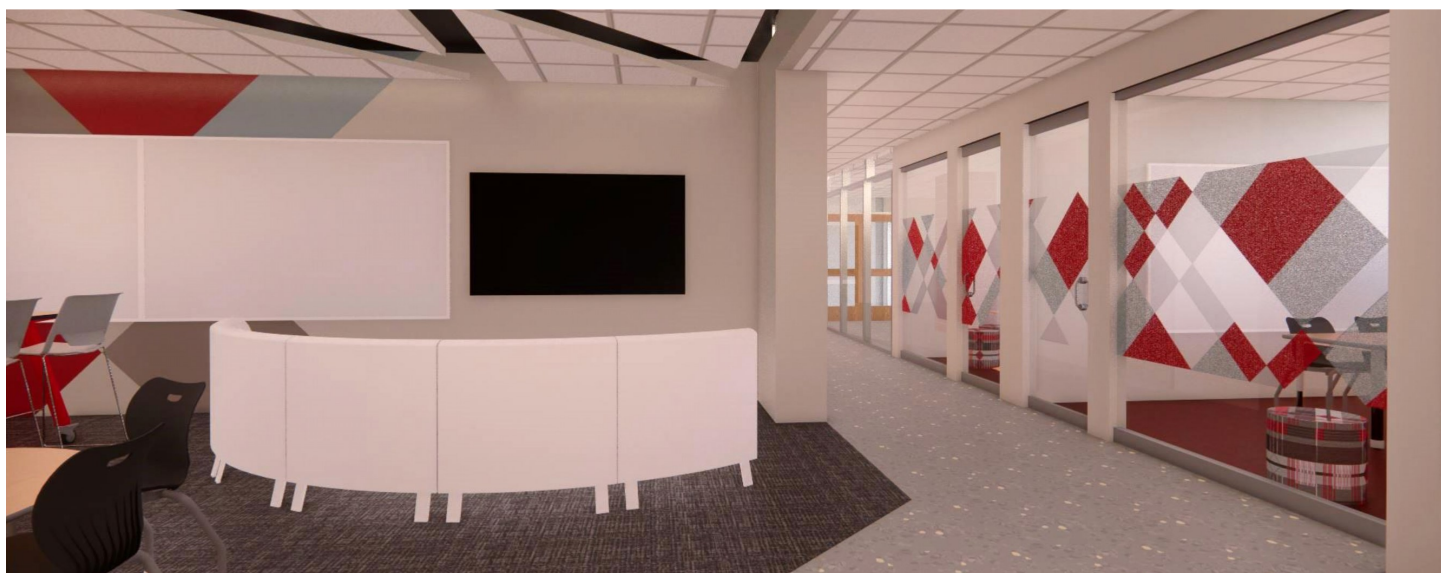

From top: Renderings of reception area, breakout and small-group rooms, and cafeteria



Jie Ming Mandarin Immersion: October 2023 Project



Location: 1845 Sheridan Ave. W., Saint Paul, MN 55116

Grades: K-5

Enrollment (SY21-22): 380

Project website: spps.org/jieming-builds

School website: spps.org/jieming

Project summary

Project number: 3090-21-01

Funding: Certificates of Participation (COP)

Project type: Addition and renovation

Square footage:

- **Existing:** 55,160 SF
- **Proposed:** 70,725 SF

SPPS project team:

- Rosemary Dolata, Project Manager
- Kenny Ekblad, Project Coordinator

Design team: Cuningham

Construction management: Knutson Construction

Project scope

- Kitchen and cafeteria addition
- New classrooms (5), inclusive restrooms, and gym floor
- New HVAC in existing west wing; one new boiler in original school building
- Improved traffic flow for cars, buses, and deliveries

New this month

- Contractors continue to work through punchlist items.
- Work supporting the newly installed boiler is nearing completion.
- The school's Autumn Festival on September 29 included a ribbon-cutting to celebrate the new building addition.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$26,840,000	\$20,057,752	\$12,342,055	\$14,001,438	\$947,698	6.77%	\$20,228,878	59.25%

Project Timeline

Phase: Planning → Design → Construction →					
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout
Key dates:	✓ March 2021	✓ March 2021	✓ Feb. 2022	✓ Spring/Summer 2022	☐ Fall 2023

Jie Ming Mandarin Immersion



From top left: Ribbon cutting on September 29; cafeteria and food service area; school entrance with Moon Gate at right; "Tiger's Lair" serves as student informal learning and gathering space; inclusive restroom (September 2023)



Saint Paul
PUBLIC SCHOOLS

Johnson Senior High School: October 2023 Project Update



Location: 1349 Arcade S., Saint Paul, MN 55106

Grades: 9-12

Enrollment (SY20-21): 1,243

Project website: spps.org/Page/39804

Schools website: spps.org/johnsonsr

Project summary

Project number: 1150-19-01

Funding: Long-Term Facilities Maintenance (LTFM) ;
American Rescue Plan (ARP)

Project type: Building systems upgrades

Square footage: Existing: 281,369 SF; Proposed: N/A

SPPS project team:

- Jason Jones, Project Manager
- Josie Geiger, Project Coordinator

Design team:

- TKDA
- Tim Hoseck, Engineer
- Ursula Larson, Architect

Construction team: Market & Johnson

Project scope

- Installation of geo-thermal heating and cooling system
- Significant replacements to the HVAC system
- Lighting replacement
- Significant additional indoor-air quality scope added mid-project with American Rescue Plan (ARP) funding

New this month

- The building now has all new mechanical systems to serve students, staff, and community for decades to come.
- This project is now complete and will no longer appear in monthly reports.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$18,843,758*	\$17,994,421	\$16,998,470	\$12,865,000	\$2,907,769*	22.60%*	\$17,957,545	95.06%

*American Rescue Plan funds approved for indoor-air quality work and added to the project; this will result in efficiencies in cost and schedule.

Project Timeline

Phase: <i>Planning</i> → <i>Design</i> → <i>Construction</i> →						
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout	
Key dates:	✓ Oct. 2018	☐ N/A	✓ Oct. 2020	✓ Feb. 2021	✓ Fall 2023	

Saint Paul Public Schools ▪ Facilities Department ▪ 1930 Como Avenue ▪ Saint Paul, MN 55108

Ph: 651-744-1800 ▪ Fax: 651-290-8362 ▪ facilities@spps.org ▪ spps.org/builds



Saint Paul
PUBLIC SCHOOLS

Maxfield Elementary School: October 2023 Project Update



Location: 380 Victoria St N., Saint Paul, MN 55104

Grades: PreK-5

Enrollment (SY21-22): 172

Project website: spps.org/Page/41781

School website: spps.org/maxfield

Project summary

Project number: 4180-22-01

Funding: American Rescue Plan

Project type: HVAC upgrades

Square footage:

- Existing: 71,334 SF
- Proposed: N/A

SPPS project team: Jason Jones, Project Manager

Design team: KOMA & E-P

Construction team: Market & Johnson

Project scope

- Provide classrooms with improved ventilation and cooling by installing new dedicated outdoor air system units on roof
- Replace existing fin tube radiation with new
- New LED lighting and ceiling in hallways
- Replace existing boiler with two new boilers
- Update and replace building's main electrical service
- Remove existing uni-vents in rooms; minor modifications to existing casework where uni-vents will be removed from the window wall

New this month

- Punchlist items are being completed.
- Waiting on roof guardrails to be installed before the building inspector signs off on the project.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$3,106,744	\$2,105,466	\$1,195,230	\$1,727,223	\$8,703	0.50%	\$2,141,565	52.46%

Project Timeline

Phase: Planning → Design → Construction →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout		
Key dates:	<input type="checkbox"/> N/A	<input type="checkbox"/> N/A	<input checked="" type="checkbox"/> Dec. 2021	<input checked="" type="checkbox"/> Aug. 2022	<input type="checkbox"/> Fall 2023		



Saint Paul
PUBLIC SCHOOLS

Mississippi Creative Arts: October 2023 Project Update



Location: 1575 L'Orient St., Saint Paul, MN 55117

Grades: PreK-5

Enrollment (SY21-22): 411

Project website: spps.org/Page/41781

Project summary

Project number: 4190-22-01

Funding: American Rescue Plan

Project type: HVAC upgrades

Square footage:

- Existing: 66,052 SF
- Proposed: N/A

SPPS project team:

- Jason Jones, Project Manager
- Josie Geiger, Project Coordinator

Design team: ATS&R

Construction team: RJM Construction

Project scope

- Provide classrooms with improved ventilation and cooling by installing new dedicated outdoor air system units on roof
- Replace existing fin tube radiation with new
- New LED lighting and ceiling in hallways
- Replace existing boiler with two new boilers
- Update and replace building's main electrical service
- Remove existing uni-vents in rooms; minor modifications to existing casework where uni-vents will be removed from the window wall

New this month

- The first phase of the project is now complete.
- The second phase will begin at the end of this school year in June and will be completed during summer 2024.

October 2023 - Project Financial Information

Original Budget	Committed Costs	Invoiced to Date	Construction Award	Construction Cost Changes	% Change	Total Forecasted Cost	Construction % Complete (as invoiced)
\$7,843,111	\$6,291,748	\$2,697,182	\$4,976,736	\$176,433	3.55%	\$6,325,390	42.83%

Project Timeline

Phase: Planning → Design → Construction →							
BOE Gate Check:	Five Year Plan	Project Charter	Budget Approval	Contract Award	Closeout		
Key dates:	<input type="checkbox"/> N/A	<input type="checkbox"/> N/A	<input checked="" type="checkbox"/> Dec. 2021	<input checked="" type="checkbox"/> Aug. 2022	<input type="checkbox"/> Fall 2024		



Summary of All Active Projects: October 2023

While the intent of this monthly report is to provide detailed information about large-scale projects, there are a myriad of important smaller projects underway as part of SPPS Builds, the District's deferred maintenance and capital improvement program. Below is a financial summary of all the active projects of all sizes currently underway across the District, which is also referenced on the [SPPS Builds website](#) where more information is available and updated regularly.

Project	Budget	Committed Costs	Invoiced to Date	Total Forecasted Cost
American Indian Magnet: Building Addition & Remodel	\$53,300,000	\$47,089,651	\$40,510,277	\$47,398,208
Barack and Michelle Obama Elementary School: Building Addition & Renovation	\$72,300,000	\$6,157,116	\$1,930,258	\$72,300,000
Battle Creek Middle School: Site Restoration Project	\$304,214	\$34,179	\$0	\$304,214
Bruce Vento: New Construction	\$89,900,000	\$26,330,984	\$2,919,037	\$89,900,000
Carpentry Plus: Harding, Phalen, Chelsea, Murray	\$1,238,000	\$1,180,251	\$983,781	\$1,180,251
Cherokee Heights ES: System Replacements	\$17,533,000	\$4,830	\$4,830	\$17,533,000
Como Park Senior High: Athletics	\$970,000	\$68,690	\$63,649	\$970,000
Creative Arts High School: ARP HVAC Upgrades	\$3,401,488	\$382,575	\$183,631	\$3,401,488
Crossroads: I Zone Space Reimagined	\$454,716	\$412,810	\$47,526	\$413,455
Early Childhood Hubs: Age Appropriate Play (East/West)	\$480,000	\$0	\$0	\$480,000
Eastern Heights: Playground Replacement	\$484,000	\$390,060	\$291,320	\$484,000
Education and Operations Services: ARP Kitchen HVAC Upgrades	\$3,052,402	\$2,031,305	\$667,626	\$2,048,305
Education and Operations Services: Dock Doors Lintels and Brick Replacement	\$2,504,000	\$0	\$0	\$2,504,000
Education and Operations Services: Print Copy Mail Center AHU Replacement	\$1,139,000	\$75,896	\$20,346	\$1,139,000
Education and Operations Services: Security Enhancements - Nutrition Services	\$30,000	\$0	\$0	\$30,000
Electrical System Replacement: Harding & Central HS	\$5,005,000	\$0	\$0	\$5,005,000
E-STEM: Boiler Replacement	\$160,000	\$0	\$0	\$160,000
E-STEM: Monument Sign	\$107,250	\$3,000	\$3,000	\$107,250
Farnsworth Upper: HVAC Replacement	\$11,162,000	\$450,524	\$1,149	\$11,162,000
Farnsworth Upper: Locker Replacement	\$111,000	\$73,713	\$64,129	\$73,713
FY23 Fire Safety Systems: Battle Creek ES, Groveland, Mississippi, Wash Tech, Wheelock, Harding	\$4,490,000	\$2,891,128	\$1,291,222	\$2,891,128
FY23 Flooring and Replacement Program: Highland Park Sr., JAJ Achievement Plus, Murray MS, Phalen Lake, Wellstone ES	\$1,113,000	\$352,066	\$2,888	\$1,113,000
FY22 Flooring Replacements: Focus Beyond, Hubbs, Rondo, LEAP, Harding	\$989,000	\$946,383	\$901,223	\$946,383
Focus Beyond: Playground Replacement	\$554,000	\$553,106	\$543,701	\$553,106
Griffin Stadium (Central HS): Electrical System Replacement	\$504,000	\$289,861	\$34,661	\$289,861
Hidden River Middle School: Renovation	\$54,200,000	\$7,463,656	\$2,424,207	\$54,200,000
Highland Park Middle School: Entry Addition and Renovation	\$49,500,000	\$2,166,747	\$499,289	\$49,500,000
Highland Park Middle School: ARP HVAC Upgrades	\$6,484,217	\$5,485,296	\$2,769,284	\$5,505,960
Highland Park Middle School: Stage Flooring Replacement	\$58,300	\$69,415	\$3,671	\$69,415

Project	Budget	Committed Costs	Invoiced to Date	Total Forecasted Cost
Highland Park Senior High: Athletics	\$2,795,000	\$102,150	\$12,882	\$2,795,000
FY22 Instructional A/V Replacement: Harding, Murray	\$2,670,000	\$1,389,688	\$899,632	\$1,389,688
FY23 Instructional A/V Replacement: Central HS, LEAP @ JAJ	\$2,500,000	\$1,194,474	\$1,044,614	\$1,203,274
Jie Ming Mandarin Immersion Academy: Building Addition & Renovation	\$26,840,000	\$20,057,752	\$12,342,055	\$20,228,878
John A Johnson: Renovations for LEAP	\$981,000	\$1,029,346	\$220,837	\$1,029,346
Johnson High School: HVAC Replacement	\$18,843,758	\$17,994,421	\$16,998,470	\$17,957,545
L'Etoile du Nord Upper: Boiler Replacement	\$123,500	\$0	\$0	\$123,500
LEAP (Wilson): Concrete Replacement	\$179,000	\$48,139	\$42,804	\$179,000
Maxfield Elementary: ARP HVAC Upgrades	\$3,106,744	\$2,105,466	\$1,195,230	\$2,141,565
FY22 Mechanical Replacements - HVAC: OWL, St Paul, Music Academy	\$1,639,185	\$1,514,825	\$362,254	\$1,514,825
Mississippi Creative Arts: ARP HVAC Upgrades	\$7,843,111	\$6,291,748	\$2,697,182	\$6,325,390
FY23 Nutrition Services: Equipment Installation	\$155,000	\$154,956	\$116,217	\$154,956
FY23 Paving Program: Galtier, Wash Tech, Phalen Lake, Wheelock, Focus Beyond	\$1,224,000	\$1,058,102	\$659,425	\$1,058,102
FY24 Paving Program: Groveland, JAJ	\$1,079,000	\$115,336	\$30,212	\$1,079,000
Plumbing Plus: Wheelock, Eastern Heights, LNFI Upper, Groveland, Hubbs, Focus Beyond, JAJ, Griffing Stadium	\$2,393,000	\$100,930	\$0	\$2,393,000
Randolph Heights Elementary School: Boiler Replacement	\$1,332,000	\$76,000	\$24,320	\$1,332,000
Riverview: Retaining Wall and UST Removal	\$185,350	\$39,366	\$21,452	\$185,350
Rondo Complex: ARP HVAC RTU Replacement	\$1,958,424	\$381,173	\$15,129	\$1,958,424
FY22 Roofing Replacement Program: EXPO, Groveland Park, Johnson Sr., Wellstone	\$4,400,000	\$4,000,762	\$955,500	\$4,007,940
Theater and Stage Equipment Upgrades: Harding, Highland Park HS, OWL, Wash Tech	\$2,354,000	\$2,095,529	\$1,485,303	\$2,135,278
Washington Technology: Foundation Repair	\$154,000	\$53,308	\$28,336	\$154,000
Wellstone: Plumbing, Piping and HVAC Replacement	\$10,654,000	\$0	\$0	\$10,654,000
