

Presented by: CJ Knowland, Director, Facilities, Maintenance, Operations, and Transportation Elvia Galicia, Assistant Superintendent, Business Services






New Gymnasium

30,297 SF

- 3-Court Gymnasium
- Lobby and Interior Corridors
- (5) Team Rooms
- (2) Sets of Gendered Restrooms
- (4) Gender Neutral Restrooms
- Concessions
- Storage

Add Alternate Weight Room 3,065 SF

Total 33,362 SF

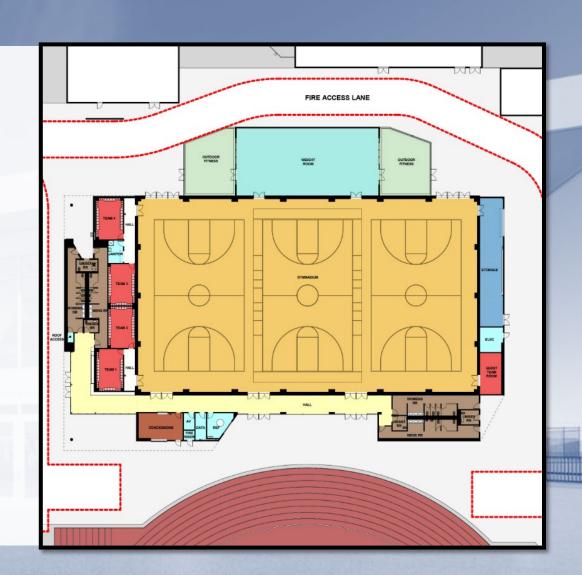



New Gymnasium Weight Room – Sample Renderings





Weight Room - 3,065 SF

- (2) Overhead Roll Up Doors
- Indoor/Outdoor Synthetic Turf






New Gymnasium Location and Logistics Plan





Portable Relocation Site Plan and Schedule




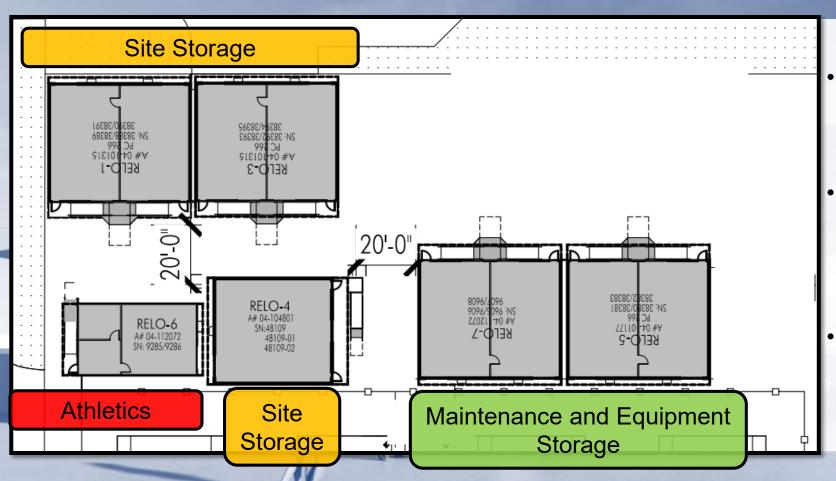

- An over-the-counter review with DSA is scheduled for November 30th
- Relocation of portable classrooms and containers scheduled to take place over Winter Break
- Utility infrastructure and setting of portable classrooms scheduled for January 2024



New Gymnasium Schedule

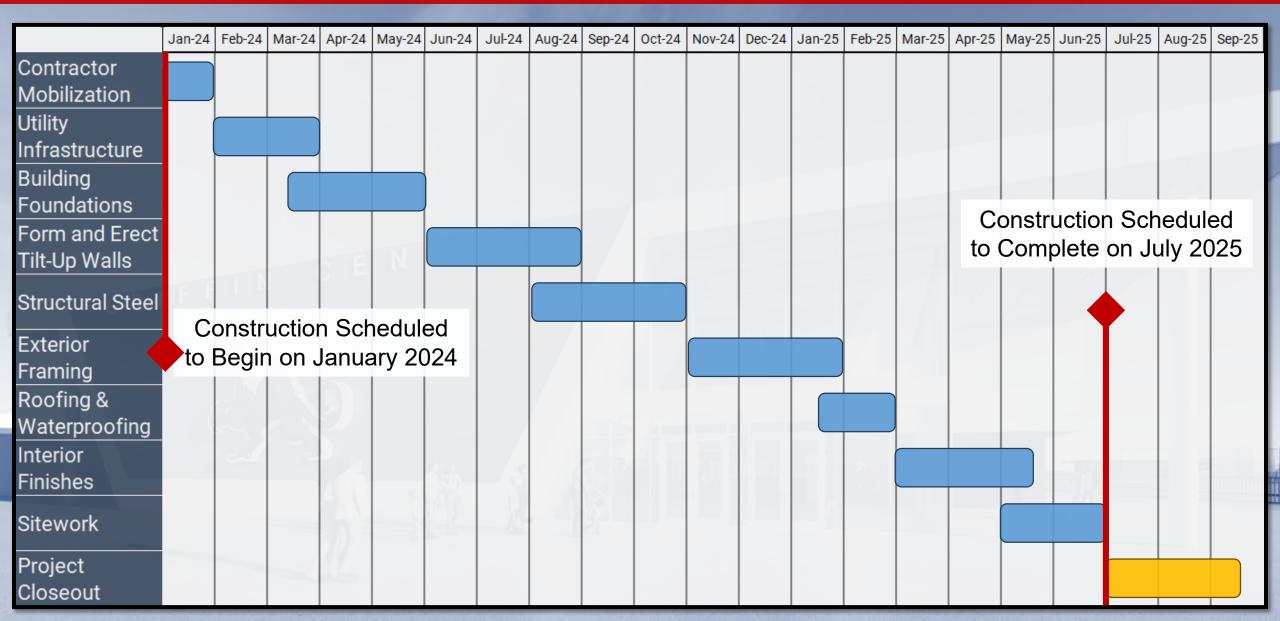





Previous Project Estimate – Board Workshop 9/20/2022

Second Gymnasium Comprehensive **Estimate** Estimated Cost and Estimated Cost Design Contingency Contingency Soft Costs & 3,586,774 2.739.278 \$ Planning 847,496 22,229,166 Construction Costs \$ 20.208.333 2.020.833 TOTAL PROJECT 22,947,611 \$ 847.496 \$ 2.020.833 25,815,940 PHASE 2 - Weight 2.469.907 2,716,898 246.991 TOTAL PROJECT COST with PHASE 2 25,417,518 \$ 847,496 \$ 2,267,824 \$ 28,532,838

- Bids from General Contractors were received on November 9th ranging from \$23.6M to \$27.5M in construction costs with a10% contingency included.
- The General Contractor bids forecast a total project cost (construction costs and soft costs), including the weight room, ranging from \$27M to \$31M.
- Soft Costs for the project account for approximately \$3.5M
 - Soft Costs include design consultants, inspection services, and regulating agency permits.
 - Soft Costs do <u>not</u> include weight room equipment or furniture.
- The General Contractors have provided costs for the weight room ranging from \$450K to \$825K.
 - This is likely considerably less than the actual construction cost of the weight room due to the General Contractors strategically weighting their bid amounts.

Facilities Revenue Projections



Estimated Facilities Funds Remaining		Funds Remaining
Bonds Funds		\$25,292,443
Capital Improvement Fund		\$11,488,381
State Matching Funds Received		\$1,200,090
Developer Fee Funds		\$1,652,293
EDCC Reserve Funds		\$6,500,000
Arts, Music, Discretionary Block Grant		\$5,200,000
	TOTAL	\$51,333,207

Total Projected Revenues \$51,333,207

Current Facilities Projects Budgets



Facilities Project		Budget
Scoreboard Replacement		\$200,000
Program & Construction Management		\$815,524
LAHS New Gymnasium & Weight Room		\$29,000,000
LAHS Classroom Renovations		\$12,000,000
LAHS Performing Arts Center Renovations		\$8,000,000
LAHS Restroom Renovations		\$4,000,000
	TOTAL	\$54,015,524

Potential Additional Funds:

Seismic Mitigation Grant \$3M State Matching Grants \$4M

Current Project Budgets	<u>\$54,015,524</u>
Projected Balance	(\$2,682,317)

New Gymnasium Contract Procurement Next Steps

- The contract is to be awarded based on a determination of 'Best Value'.
- Interviews are currently being scheduled with the General Contractors to take place over the next week.
- We anticipate bringing the General Contractor agreement for approval at the December 12th Board Meeting.







