


#### Completed Work:

- Roofing over gym complete. Working over Mechanical platform
- ➤ ICF At Cafeteria will be complete on 12/6
- Completed CMU in Areas C/D to elevator and lobby stairs
- Set Roof Steel Area A and Area C with additional erection crew. Both Roofs Structure to 90%
- Continue Site, Sanitary, Domestic/Fire Lines, MEP and Sprinkler
- Continue Metal Stud Framing
- Geothermal Underground to building Continuing
- > KAW installed 500' of domestic DIP line
- Continue Air Barrier Prep
- Continue Masonry at Stage and Area A-B end walls
- Ceiling and Soffit Work Complete Area A and Area C

### Upcoming Work/Look Ahead:

- Complete ICF at Cafeteria and Building C
- Start ICF area D and End Wall Area A
- Continue Steel Erection at Area E (Cafeteria)
- Complete CMU at Stage Area for Hollow Core Planks Set-out
- Set Stala Frames at Area D
- Start ICF and CMU at Storm Shelter
- Domestic Water to vault
- Install Temporary Heating at Area A
- Pour Topping Slab at Platform Area A and Area C
- Continue Zone Piping at Geothermal Field
- Continue rough-in of Sprinkler and MEP scopes
- Install Roofing system and curbs at Kitchen/Mechanical room






### Area A – CMU at Fire Wall almost complete






### Area A – Steel Roof Framing Set

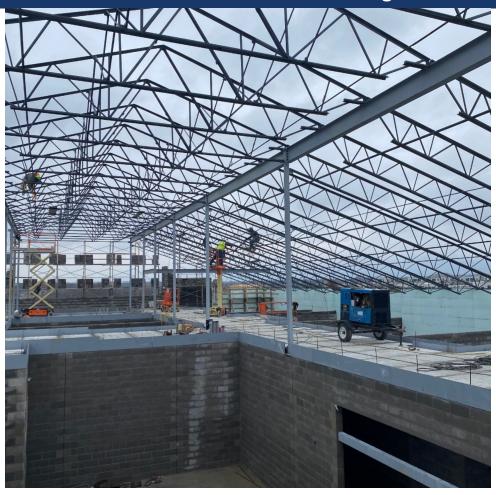



### Area B – ICF at 2<sup>nd</sup> Floor Continues

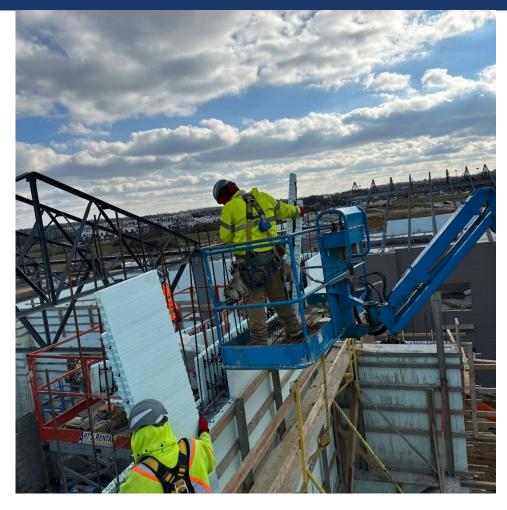




### Area B – Mechanical Platform Metal Deck Installed





### Area C – Steel Roof Framing Continues

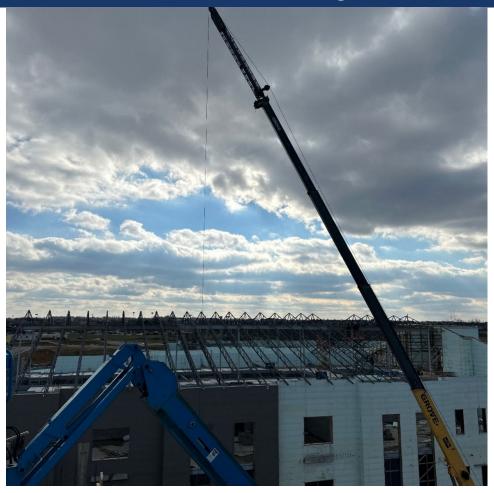



### Area E – Cafeteria End Wall Concrete Pour





### Area E – Cafeteria ICF End Wall Complete





### Area E – Cafeteria Roof Framing Set

