

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 11/17/2023



**Canopy at Addition Courtyard**



**Acoustical Wall Panels in Auxiliary Classroom**

## **This Week: 10/30/23—11/03/23**

- Completed Painting the Metal Panels and Steel at the Addition Courtyard Canopy
- Completed Installing the Outdoor Heaters at the Addition Courtyard
- Completed Installing the Flooring at the Auxiliary Classroom
- Completed Installing the Acoustical Wall Panels at the Auxiliary Classroom
- Completed Installing the Doors at the Entrance to Auxiliary Classroom
- Completed the Steel Handrail at Courtyard Ramp

## **Next Week: 11/06/23—11/10/23**

- Complete Storefront Window Install at Addition
- Complete Sod at Addition Courtyard



**Flooring in Auxiliary Classroom**



**Whiteboards at Addition Courtyard**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 11/03/2023



**Outdoor Heaters at Addition Courtyard**



**Markerboards in Auxiliary Classroom**

## **This Week: 10/30/23—11/03/23**

- Continued Storefront Window Install at Addition
- Continued Installing Outdoor Heaters at Addition
- Installed landscaping at Bus Loop Entrance
- Began Installing Doors at Entrance to Auxiliary Classroom

## **Next Week: 11/06/23—11/10/23**

- Complete Storefront Window Install at Addition
- Complete Sod at Addition Courtyard
- Complete Outdoor Heaters Installation at Addition
- Begin Painting Metal Panels and Steel at Addition
- Begin Painting Drywall in Auxiliary Classroom
- Begin Flooring at Addition



**Outdoor Heaters at Addition Courtyard**



**Window & Windowsill in Auxiliary Class-**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 10/27/2023



Outdoor Heaters at Addition Courtyard



Exterior of Auxiliary Classroom

## **This Week: 10/23/23—10/27/23**

- Installed Markerboards in Auxiliary Classroom
- Continued Storefront Window Install at Addition
- Began Installing Outdoor Heaters at Addition
- Began Sod at Addition Courtyard

## **Next Week: 10/30/23—11/03/23**

- Complete Storefront Window Install at Addition
- Complete Sod at Addition Courtyard
- Continue Installing Outdoor Heaters at Addition
- Begin Painting Metal Panels and Steel at Addition
- Begin Painting Drywall in Auxiliary Classroom
- Begin Flooring at Addition



Outdoor Heaters at Addition Courtyard




Exterior of Auxiliary Classroom & Courtyard

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 10/20/2023



**Metal Panels at Addition Canopy**

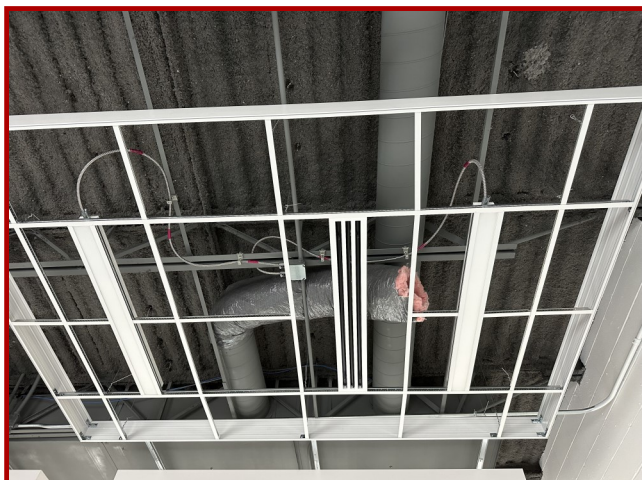

**Light Fixture Install in Auxiliary Classroom**

## **This Week: 10/16/23—10/20/23**

- Completed Metal Panel Install at Addition
- Continued Storefront Window Install at Addition
- Completed Installing Light Fixtures in the Acoustical Panel Ceiling Clouds

## **Next Week: 10/23/23—10/27/23**

- Complete Storefront Window Install at Addition
- Begin Painting Metal Panels and Steel at Addition
- Begin Painting Drywall in Auxiliary Classroom
- Begin Flooring at Addition
- Begin Installing Outdoor Heaters at Addition



**Courtyard Turf and Addition Canopy**



**Metal Panels at Addition Canopy**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 10/13/2023



**Metal Panels at Addition Canopy**



**Turf at Addition**

## **This Week: 10/09/23—10/13/23**

- Completed Waterproofing at Addition Canopy
- Completed Metal Panel Install at Front Entrance
- Continued Storefront Window Install at Addition
- Completed Turf Install at Addition Courtyard
- Completed Hanging the Acoustical Panel Ceiling Clouds
- Began Metal Panel Install at Addition

## **Next Week: 10/16/23—10/20/23**

- Complete Storefront Window Install at Addition
- Complete Metal Panel Install at Addition
- Begin Painting Metal Panels and Steel at Addition
- Begin Flooring at Addition



**Front Canopies**



**Metal Panels at Addition Canopy**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 10/06/2023



**Turf at Addition Courtyard**



**Prep for Turf at Addition**

## **This Week: 10/02/23—10/06/23**

- Completed Drywall Install in Auxiliary Classroom
- Continued Waterproofing at Addition Canopy
- Continued Metal Panel Install at Front Entrance
- Continued Storefront Window Install at Addition
- Began Turf Install at Addition Courtyard
- Began Hanging the Acoustical Panel Ceiling Clouds

## **Next Week: 10/09/23—10/13/23**

- Complete Waterproofing at Addition Canopy
- Complete Metal Panel Install at Front Entrance
- Complete Turf Install at Addition
- Begin Metal Panel Install at Addition Canopy



**Acoustical Panel Ceiling Clouds**




**Waterproofing at Addition Canopy**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 09/29/2023



Front Canopy

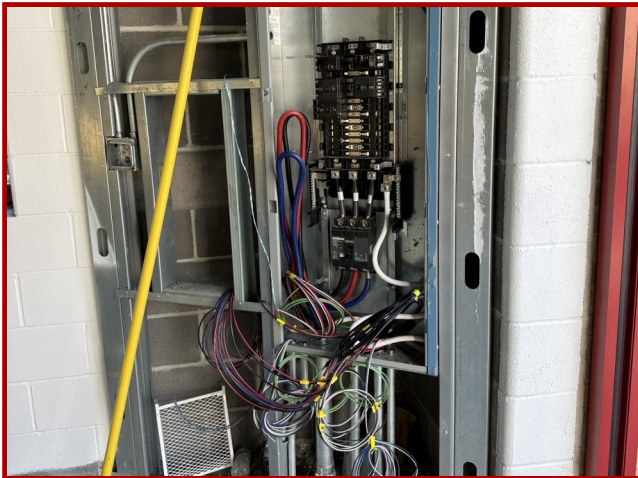

Panelboard in Auxiliary Classroom

## This Week: 09/25/23—09/29/23

- Completed Courtyard Concrete & Flatwork
- Completed Plywood Sheathing at Addition Canopy
- Continued Metal Panel Install at Front Entrance
- Continued Storefront Window Install at Addition
- Began Waterproofing at Addition Canopy

## Next Week: 10/02/23—10/06/23

- Complete Storefront Window Install at Addition
- Complete Metal Panel Install at Front Entrance
- Final Grade Courtyard
- Begin Metal Panel Install at Addition Canopy
- Begin Drywall in Auxiliary Classroom



Concrete Sidewalk at Addition



Concrete Curb in Courtyard

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 09/22/2023



Canopy Sign



Auxiliary Classroom Interior Paint

## **This Week: 09/18/23—09/22/23**

- Installed the Hocker Grove Sign at Front Canopy
- Completed Courtyard Concrete & Flatwork
- Completed Painting at Auxiliary Classroom Interior
- Continued Metal Panel Install at Front Entrance
- Began Plywood Sheathing at Addition Canopy

## **Next Week: 09/25/23—09/29/23**

- Complete Construction in Front Office
- Complete Storefront Window Install at Addition
- Continue Metal Panel Install at Front Entrance
- Final Grade Courtyard



Metal Paneling & Front Office Entrance Sign



Plywood Sheathing at Addition Canopy

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 09/15/2023



**Concrete Bench**



**Courtyard Sidewalk**

## **This Week: 09/11/23—09/15/23**

- Completed Courtyard Concrete & Flatwork
- Completed Storefront Install in Front Office
- Continued MEP Rough-In at Auxiliary Classroom
- Continued Metal Panel Install at Front Entrance
- Continued Storefront Install at Addition

## **Next Week: 09/18/23—09/22/23**

- Complete Storefront Window Install at Addition
- Continue MEP Rough-In at Addition
- Continue Metal Panel Install at Front Entrance
- Begin Painting Steel at Addition



**MEP Rough-In at Addition**



**Addition Storefront Framing**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 09/08/2023



**Concrete Bench**



**Courtyard Storefront Window Framing**

## **This Week: 09/04/23—09/08/23**

- Completed Courtyard Concrete & Flatwork
- Continued MEP Rough-In at Auxiliary Classroom
- Continued Metal Panel Install at Front Entrance
- Began Storefront Window Install at Addition

## **Next Week: 09/11/23—09/15/23**

- Continue MEP Rough-In at Auxiliary Classroom
- Continue Metal Panel Install at Front Entrance
- Continue Storefront Window Install at Addition
- Begin Storefront Install in Front Office



**MEP Rough-In at Addition Ceiling**



**Addition Storefront Window Framing**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 09/01/2023



Ramp to Courtyard



Front Landscaping

## This Week: 08/28/23—09/01/23

- Continued Courtyard Concrete & Flatwork
- Continued Landscaping & Sod at Front of School
- Continued MEP Rough-In at Auxiliary Classroom
- Began Metal Panel Install at Front Entrance

## Next Week: 09/04/23—09/08/23

- Complete Courtyard Concrete & Flatwork
- Continue Landscaping & Sod at Front of School
- Continue MEP Rough-In
- Continue Metal Panel Install at Front Entrance
- Begin Glazing at Addition



MEP Rough-In at Addition Ceiling



Courtyard Sidewalk

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 08/25/2023



Auxiliary Classroom Patio



Auxiliary Classroom Roof

## This Week: 08/21/23—08/25/23

- Completed Roofing at Auxiliary Classroom
- Completed Courtyard Concrete & Flatwork
- Completed Spray Insulation at Auxiliary Classroom Ceiling
- Continued Landscaping & Sod at Front of School
- Continued Metal Panel Prep at Front Entrance
- Began MEP Rough-In at Auxiliary Classroom

## Next Week: 08/28/23—09/01/23

- Continue Landscaping & Sod at Front of School
- Continue MEP Rough-In
- Begin Courtyard Turf
- Begin Glazing at Addition
- Begin Installing Metal Panels at Front Entrance



Spray Insulation at Addition Ceiling



Addition Canopy Roof

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 08/18/2023



**Masonry at Courtyard Walls**



**Auxiliary Classroom Entrance**

## **This Week: 08/14/23—08/18/23**

- Completed Renovation Final Clean
- Completed Masonry at Addition
- Completed Final Storm Tie-Ins at Addition
- Began Landscaping & Sod at Front of School
- Began Roofing at Auxiliary Classroom
- Began Courtyard Concrete & Flatwork

## **Next Week: 08/21/23—08/25/23**

- Continue Landscaping & Sod at Front of School
- Continue Roofing at Auxiliary Classroom
- Continue Courtyard Concrete & Flatwork
- Begin MEP Rough-In at Addition



**Front of Auxiliary Classroom**



**Auxiliary Classroom Roof**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 08/11/2023



Restroom



Addition Canopy

## **This Week: 08/07/23—08/11/23**

- Completed Plumbing Fixture Install
- Completed Ceiling Install
- Continued Masonry at Addition
- Continued Reception Desk
- Continued Addition Blocking
- Began Metal Panel Prep
- Began Final Clean

## **Next Week: 08/14/23—08/18/23**

- Begin Landscaping & Sod
- Continue Metal Panel Install at Front Entrance
- Continue Masonry at Addition
- Set Roof Curb
- Continue Final Clean




Reception Desk



Reception Carpet

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 08/04/2023

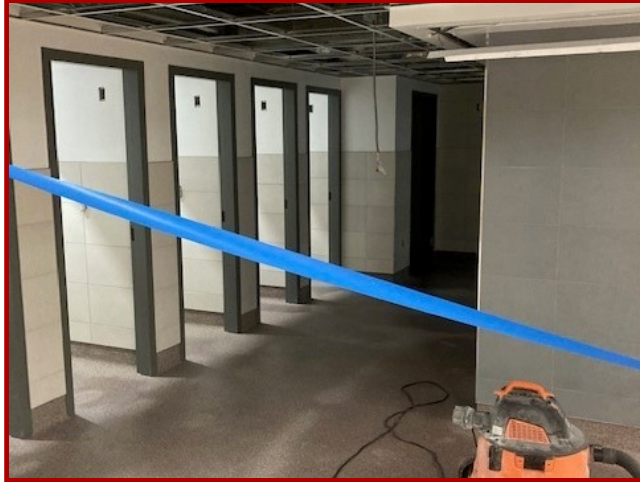

Restroom



Restroom

## This Week: 07/31/23—08/04/23

- Completed the Mill & Overlay of Asphalt
- Completed Asphalt Striping
- Completed Painting in Reception
- Continued Masonry at Addition
- Completed Office Storefront
- Completed Sidewalk Install at Bus Loop Entrance
- Continued Reception Desk

## Next Week: 08/07/23—08/11/23

- Complete Plumbing Fixture Install
- Complete Ceiling Install
- Continue Masonry at Addition
- Continue Addition Blocking
- Begin Metal Panel Install at Front Entrance
- Begin Final Clean



West Parking Lot Asphalt



Parent Drop Off Asphalt

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 07/14/2023



Masonry on Courtyard Walls



Restroom

## This Week: 07/10/23—07/14/23

- Began Erecting Structural Steel Outside Addition
- Began Base Layer of Asphalt at Bus Loop
- Continued Masonry on Courtyard Walls
- Finished Framing in RR
- Finished MEP Rough-In in RR
- Finished Sheathing at Front Entrance

## Next Week: 07/17/23—07/21/23

- Begin Sheet Rock in RR
- Continue Asphalt at Bus Loop
- Continue Masonry on Courtyard Wall
- Continue Erecting Structural Steel at Addition
- Continue Reception Drywall and Trim Out



Steel in Courtyard




Bus Loop

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 07/07/2023



Masonry on Courtyard Walls

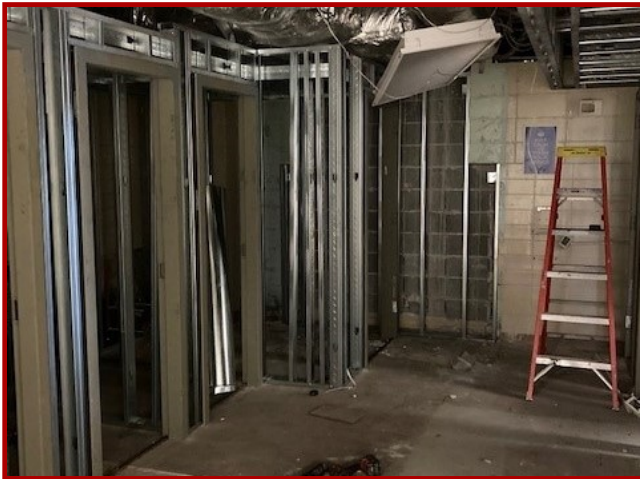

Framing in Restroom

## This Week: 07/03/23—07/07/23

- Began Framing in RR
- Began MEP Rough-In in RR
- Curbs Complete
- Continued Masonry on Courtyard Walls
- Continued Exterior Framing at Front Office
- Began Sheathing at Front Office
- Final Prepped for Asphalt at Bus Loop

## Next Week: 07/10/23—07/14/23

- Continue Masonry on Courtyard Walls
- Continue MEP Rough-In in RR
- Begin Drywall in RR
- Begin Erection of Structural Steel
- Begin Pouring Asphalt at Bus Loop



Exterior Framing & Sheathing at Front Office



Framing in Restroom

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 06/23/2023



Bus Loop



Demo in RR

## This Week: 06/19/23—06/23/23

- Under slab Plumbing In RR
- Waterproofing Aux Classroom
- Structural Steel work on Front Of Building and Office Area
- 90% of Curbs Complete

## Next Week: 06/26/23—06/30/23

- Demo Last Approach
- Tie Curbs in at Street
- Brick Laying on Aux Classroom
- Framing front exterior of building and Office
- MEP Rough In in RR



Front Office



Front Drive

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 06/16/2023



**Auxiliary Classroom**



**Demo in RR**

## **This Week: 06/12/23—06/16/23**

- Finish Office Demo
- Finish RR Demo
- Finish Grading West Bus Loop
- Survey For Curb
- Setting Up Curb Strings For Curb Machine

## **Next Week: 06/19/23—06/23/23**

- Framing in Office
- Under Slab Plumbing in RR
- Waterproofing at Addition
- Front Curb Work Begins



**Front Office**



**CMU Demo**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 06/09/2023



Restroom Demo



Classroom Addition Slab Prep

## **This Week: 06/05/23—06/09/23**

- Finish Canopy Demo
- Finish Demo Existing Bus Loop
- RR Demo Cont.
- Office Demo Cont.

## **Next Week: 06/12/23—06/16/23**

- Curbs To Be Poured At Front Of School
- Rough In Plumbing In RR
- Rough in HVAC In RR
- Learning Stair Brick Laying Begins



Canopy Demo Complete



Existing Bus Loop Grading

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 06/02/2023



**Restroom CMU Demo**



**Classroom Addition Slab Prep**

## **This Week: 05/30/23—06/02/23**

- Interior RR Demo
- Demo Existing Bus Loop Begins
- Continue Grading New Bus Loop
- Canopy Demo Begins

## **Next Week: 06/05/23—06/09/23**

- Interior RR Demo Cont.
- Front Office Demo Begins
- Poor Slab for Classroom Addition
- Bus Loop Demo Cont.



**Canopy Demo**



**Existing Bus Loop Demo**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 05/26/2023



Auxiliary Classroom Entrance



Front Bus Loop Grading

## This Week: 05/22/23—05/26/23

- Complete CMU Masonry Walls
- Continue MEP Rough-In
- Begin Grading Front Bus Loop
- Begin Demo prep for interior reno

## Next Week: 05/29/23—06/02/23

- Exterior Demo Existing Bus Loop
- Begin Canopy Demo
- Begin Interior Restroom Demo
- Begin MEP Demo



Courtyard CMU Wall



Auxiliary Classroom

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 05/19/2023



Auxiliary Classroom CMU



Auxiliary Classroom Entrance

## This Week: 05/15/23—05/19/23

- Continue CMU Masonry Walls
- Continue MEP Rough-In
- Layout for Front Drive Grading
- Demo Walkthrough

## Next Week: 05/22/23—05/26/23

- Complete CMU at Classroom
- Begin Exterior Demo
- Begin Interior Demo
- Complete MEP Rough-In at CMU
- Begin Grading at Front Bus Loop

Weather Days this week: (1) Days



Courtyard CMU Wall



Leave-out Section to Finish Courtyard

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 05/05/2023



**Poured Step Footings**



**Poured Classroom Footings**

## **This Week: 05/01/23—05/05/23**

- Continue Addition Foundations
- Begin CMU Masonry Walls
- Protection of existing utilities
- Layout of New Gas Connection

## **Next Week: 05/08/23—05/12/23**

- Complete Addition Foundations
- Continue Masonry CMU for Addition
- Begin Underground MEP
- Begin Grading at Front Bus Loop

**Weather Days this week:** (0) Days



**Placed Rebar for Next Pour**



**Foundation Prep at Utilities**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 04/28/2023



**Poured A Line Footing**



**Poured Pier Footings**

## **This Week: 04/24/23—04/28/23**

- Complete building pad
- Continue Addition Foundations
- Begin Layout for Masonry

## **Next Week: 05/01/23—05/05/23**

- Continue Addition Foundations
- Begin CMU for Addition
- Begin Underground MEP

**Weather Days this week: (0) Days**




**West Footing Layout at Addition**



**Completed Grading**

# Hocker Grove Middle School WEEKLY PROGRESS REPORT 04/21/2023

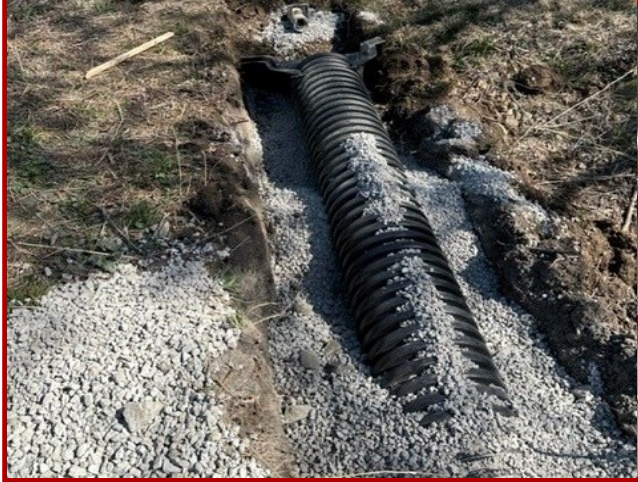

Extend Drainage Pipe to Retention Area



Installed Storm Structure

## **This Week: 04/17/23—04/21/23**

- Complete Addition Utilities
- Begin Addition Foundations
- Begin Layout for Masonry

## **Next Week: 04/24/23—04/28/23**

- Continue Addition Foundations
- Begin Underground MEP
- Begin CMU for Addition

**Weather Days this week:** (1) Days



Grading for Foundations



Tied-In Drainage Basin
