

SM Trailridge Middle School WEEKLY PROGRESS REPORT 12/08/2023



Exterior Concrete Pour



Exterior Metal Panel System

This Week: 12/04/23—12/08/23

- Pour Exterior Concrete
- Vestibule Glazing Install
- Continue Drywall and Ceilings
- Metal Panel System Continues
- Access Control Rough/Install
- Begin Wall Tile
- Begin Prime & Painting

Next Week: 12/11/23—12/15/23

- Complete Exterior Concrete
- Continue Drywall Tape & Finish
- Continue Drop Ceiling Install
- Continue Metal Panel System
- Set Gas Lines & RTU's
- Continue Finishes
- MEP Trim Out

Weather Days this week:

- (0) Days



Insulating Overhead MEP



Lobby Tape & Finish

SM Trailridge Middle School WEEKLY PROGRESS REPORT 11/22/2022



Glazing at New Entrance



Drywall Tape & Finish

This Week: 11/20/23—11/24/23

- Glazing Install
- Begin Temp. Heating Addition
- Begin Drywall and Ceiling Hangers
- Complete Overhead MEP Rough-In
- Form & Pour Interior Ramp
- Metal Panel System Begins

Next Week: 11/27/23—12/01/23


- Complete Glazing Install
- Prep & Layout Exterior Concrete
- Continue Drywall Tape & Finish
- Continue Drop Ceiling Install
- Continue Metal Panel System
- Prepare for RTU Next Week

Weather Days this week:

- (0) Days



Back of House Drywall Begins

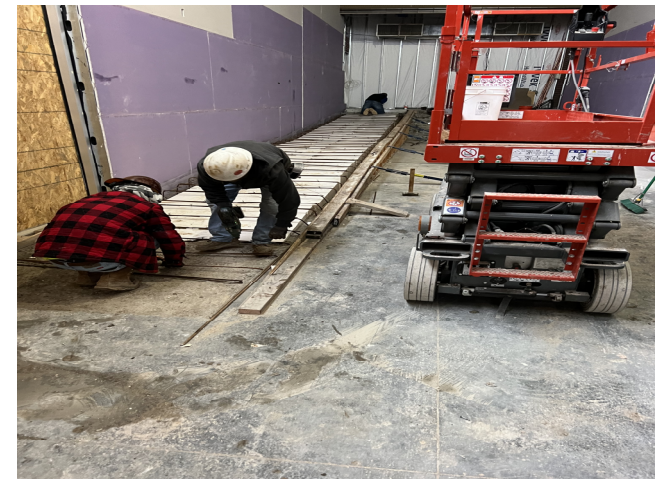

Lobby Ramp Form & Pour

SM Trailridge Middle School WEEKLY PROGRESS REPORT 12/15/2023



Metal Panel System



Lobby Finishes Ongoing

This Week: 12/11/23—12/15/23

- Continue Drywall and Ceilings
- Metal Panel System Continues
- Access Control Rough/Install
- Begin Wall & Ramp Tile
- Continue Prime & Painting
- MEP Trim Out
- Take Down Temp. Barricade
- Epoxy Flooring Complete
- RTU's Set

Next Week: 12/18/23—12/22/23

- Fine Grading For Landscaping
- Landscaping Install
- Remaining Glazing Install
- Continue Metal Panel System
- Set Gas Lines & RTU Start Up
- Office Carpeting Install
- Set RR Plumbing Fixtures
- Complete Wall Tile
- MEP Trim Out

Weather Days this week: (0)



Hallway Finishes



Epoxy Floor Complete
