




Mary E. Britton Middle School

➤ **Completed Work:**

- ICF at Area A and Area C to 95%
- ICF at Storm Shelter (Awaiting inspections to pour)
- Platform Area C/D remaining hollow core (3 sections) to be placed 1/4/24. Completes all Hollow Core
- Roof Joist and Decking at Area A and Area C
- CMU continuing at Area E/F behind Cafeteria
- CMU (4") and top out to deck in Gym and Locker Room Area
- Continuing Fire Sprinkler and MEP Rough ins above ceiling and floor to floor connections
- KY American Water completed underground Fire/Domestic line. Currently Flush and Test
- Geothermal continuing to install Zone piping at field

➤ **Upcoming Work/Look Ahead:**

- Complete ICF Building A and C
- Continue ICF at Storm Shelter and Area E
- Complete Masonry at Cafeteria/Gym Wall
- Test Gym and Locker Room to receive Block Filler
- Continue brick veneer work
- Continue Roof Decking Area A and Area C
- Start Roof Decking at Cafeteria
- Continue Sprinkler and MEP Rough Ins All Areas
- Continue Geothermal Piping under ground
- Start Gas Line Work to Building
- Start Field Measuring for Casework and Lockers

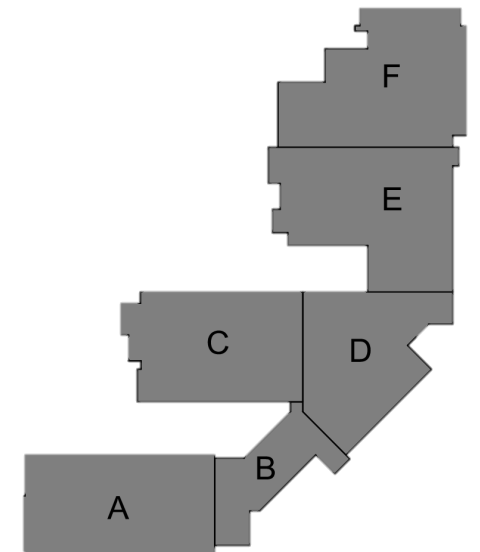

Mary E. Britton Middle School

Area A – ICF at End Wall Continues



Week Ending January 5, 2024

Mary E. Britton Middle School



Area A – Steel Roof Decking Started



Week Ending January 5, 2024

Mary E. Britton Middle School



Area C – Mezzanine Topping Slab Poured



Week Ending January 5, 2024



Mary E. Britton Middle School

Area E – CMU at Stage Continuing



Week Ending January 5, 2024

Mary E. Britton Middle School



Area E – Restroom Plumbing Roughins Continue



Week Ending January 5, 2024

Mary E. Britton Middle School



Area E – Storm Shelter ICF continues



Week Ending January 5, 2024

Mary E. Britton Middle School



Area F – Brick Continuing Around Gym



Week Ending January 5, 2024

Mary E. Britton Middle School



Area F – Gym CMU Veneer Complete



Week Ending January 5, 2024
