
Completed Work:

- ICF forms at Area E
- Structural Steel detailing roof curbs and misc. details
- Structural Steel finishing remaining joist and Deck at C and A
- Masonry CMU topping out at Kitchen and Mechanical Room to deck
- Grouting remaining Hollow Core Planks in Area B, D, C and Above Stage
- Framing Soffit Area C second floor
- Framing Exterior Wall at Kitchen
- Continue Roofing at Area F
- Block Fill at Gym and Locker Room
- Installing duct in Gym and Area A-C
- Continue Temporary Heating and Winterizing All Areas
- Continue above ceiling rough ins of plumbing, electrical and sprinkler systems
- > Continuing geothermal underground as weather permits

Upcoming Work/Look Ahead:

- > Pour next ICF lift on 1/31/24 (one pour remaining to top out)
- Start ICF in Area D
- Schedule next topping slab pour at mechanical mezzanines
- Continue CMU at Area E to joist bearing height
- > Continue CMU at Area B and D to joist bearing height
- Finish Roof Joist and Decking at Area A
- Continue Metal Stud Framing
- Dry in Kitchen Area Roofing
- Continue MEP and Sprinkler multiple areas
- Finish setting Equipment on Area C mechanical platform





Aerial – Overall Progress






Area B – 2nd Floor Corridor Hollow Core Planks Set





Area E – CMU in Corridors Complete

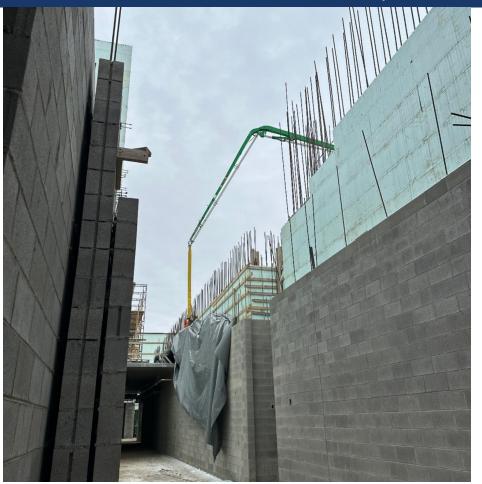




Area E – Storm Shelter ICF Continues





Area E – Storm Shelter Louver Framing

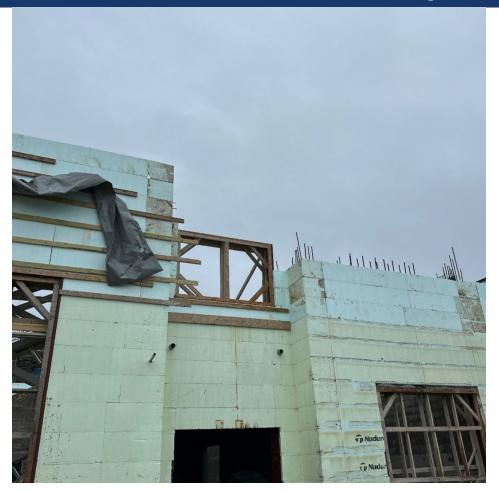




Area E – Storm Shelter Steel Lintels Above Windows





Area F - CMU Block Fill Started in the Locker Rooms

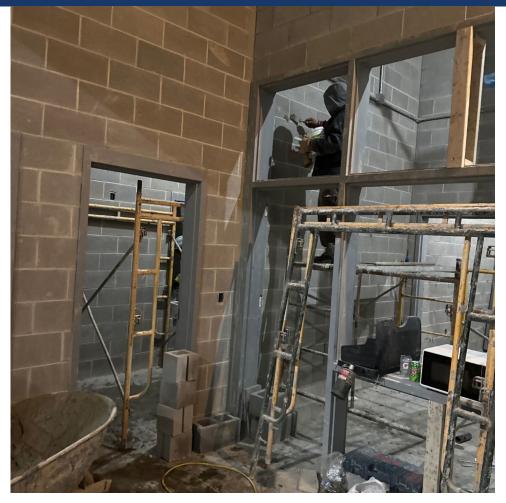



Area F – Roofing Over Kitchen and Mechanical Room

