




Mary E. Britton Middle School

➤ Completed Work:

- ICF Area E – Second Pour Complete, Installing Forms to Parapet level
- CMU Continuing at Area E/F, B (Roof Bearing Wall)
- Hollow Core Plank Stage Grouting Finished this Week
- Structural Steel Area C and Misc. Steel Beams/Lintels installing
- Roof Blocking at Area A
- Roof installing at Kitchen/Mechanical Room
- Metal Stud Framing Area A – Second Floor and Exterior Area F.
- Painting Block Fill at Gym/Locker Room
- Control Joint Caulking Gym/Locker Room
- Joint Prep for Air Barrier at Area B
- Loading all Mezzanine Mechanical Equipment Area A, C and F
- Continuing MEP and Sprinkler Rough-In for Walls and Above Ceiling
- Installing Geothermal Underground Zone Piping

➤ Upcoming Work/Look Ahead:

- Pour final lift at Storm Shelter ICF Forms
- Finish Roof at Area A and Area C
- Continue Roof Blocking area A and C for Roof Installation (2 Weeks from Start of Sloped Roofs)
- Continue Metal Stud Framing Interior and Exterior
- Continue Air Barrier Installation
- Finish CMU Area E/F and B/D common corridors to Roof Bearing
- Continue Expansion Joint Caulking
- Continue Block Fill at Area A (Conditions Permitting)
- Continue MEP and Sprinkler Rough-Ins
- Complete Block Fill of Mechanical room and Set Switch Gear
- Continue Geothermal Underground Piping
- Set Generator in Generator Room
- Start Area D Exterior Wall Stala and ICF

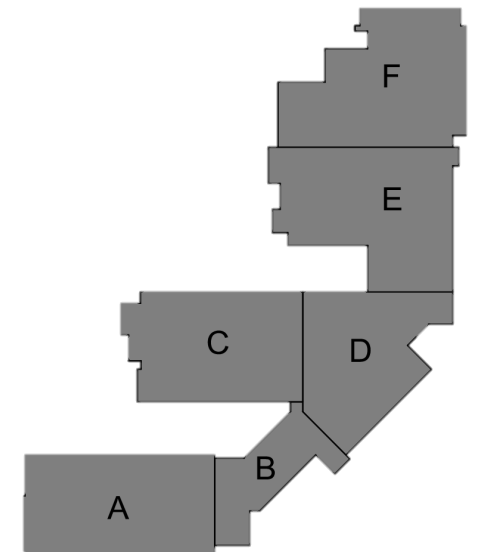

Mary E. Britton Middle School

Area A – Above Ceiling and Soffit Framing Continues in Corridors



Week Ending February 2, 2024

Mary E. Britton Middle School



Area B – 2nd Floor Media Center Flex Spaces Continue



Week Ending February 2, 2024



Mary E. Britton Middle School

Area B - Corridor



Week Ending February 2, 2024

Mary E. Britton Middle School



Area D – 2nd Floor Restroom CMU Continues



Week Ending February 2, 2024

Mary E. Britton Middle School



Area E – Cafeteria CMU at Stage Continues



Week Ending February 2, 2024

Mary E. Britton Middle School



Area E – ICF Continues at Strom Shelter



Week Ending February 2, 2024


Mary E. Britton Middle School

Area F – Brick and Air Barrier Installed at Gym



Week Ending February 2, 2024

Mary E. Britton Middle School



Mezzanine – Setting Units



Week Ending February 2, 2024
