




# hollis \_\_\_\_<sup>architects</sup>



LHS TENNIS COURTS



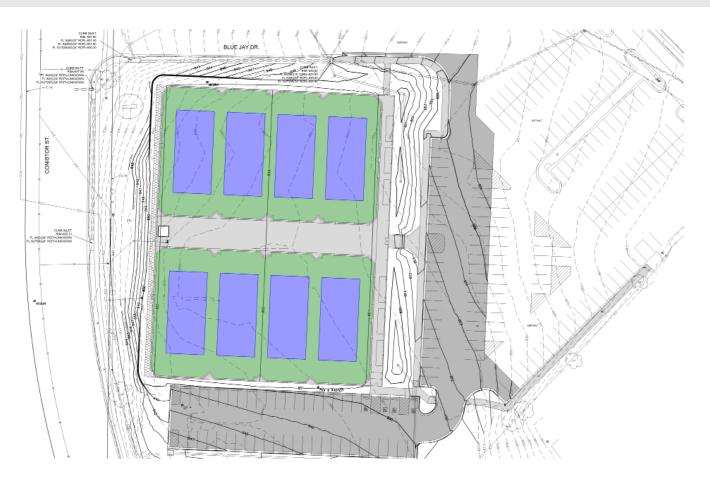

## Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- . 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023 Construction Complete: Fall 2023

## WEEKLY PROGRESS REPORT Liberty Public Schools



#### **PUBLIC SCHOOLS**

## **PROJECT STATUS**

Courts Substantially CompleteTurned Over 10/31Final Punch List Items Being Completed



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North

## UPCOMING

Project Completion October 2023





## WEEKLY PROGRESS REPORT





South Courts Looking West




Center Spectator Concourse Looking West



LHS BASEBALL & SOFTBALL





## Liberty High School Baseball/Softball Complex

#### **Baseball Field**

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

#### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

#### Multi-purpose Field

· Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023 Construction Complete: Summer 2024

## WEEKLY PROGRESS REPORT Baseball Softball 02/12/2024

## **PROJECT STATUS**

#### LHS

-Baseball Turf Installation Ongoing -Baseball Backstop Paving Complete -Baseball Dugouts Painting Complete

-Aux Field Grading Ongoing -Aux MEP Underground Ongoing

-Softball Field Site Utilities Ongoing -Softball Dugout CMU Complete -Softball Field Grading Ongoing

#### UPCOMING


LHS --Baseball Bullpens -Baseball Batting Tunnel

-Aux Finish Grading -Aux Field Irrigation

-Softball MEP Underground -Softball Concrete Curbs & Fence Posts

Project Completion Baseball March 2024/Softball May 2024





LHS - Baseball (Ready for Turf)



LHS - Softball



**PUBLIC SCHOOLS** 

LHS - Baseball Dugouts (Painted)




LHS - Softball



LNHS BASEBALL & SOFTBALL







## Liberty North High School Baseball/Softball Complex

#### **Baseball Field**

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

#### **Softball Field**

- Increased Field Dimensions 194'(L) 200'(C) 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023 Construction Complete: Summer 2024

#### WEEKLY PROGRESS REPORT Baseball Softball 2/12/2024 Liberty Public Schools



### **PUBLIC SCHOOLS**

## **PROJECT STATUS**

#### LNHS

- Baseball Turf Installation Ongoing
- Baseball Backstop Netting Complete
- Baseball Champion Wall Ongoing
- Baseball Bullpen Ongoing

-Softball Field Drainage Ongoing -Softball MEP Ongoing

-Concourse Paving Complete

#### UPCOMING

LNHS--Baseball Athletic Equipment Installation

-Softball Finish Grading -Softball Turf Subgrade -Softball Fence Post & Perimeter Curb

Project Completion Baseball March 2024/Softball May 2024





LNHS - Baseball



LNHS - Baseball (Backstop Netting Installed)



LNHS - Baseball



LNHS - Baseball



## DISTRICT WIDE LED LIGHTING UPGRADES



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

## WEEKLY PROGRESS REPORT Liberty Public Schools



#### **PUBLIC SCHOOLS**

#### **PROJECT STATUS**

South Valley MS - Upgrades Complete

Discovery MS - Upgrades Complete

EPiC Elementary - Upgrades Complete

Liberty North High School - Upgrades Ongoing

### UPCOMING

Evergy Inspections - All Four Schools Emergency LED Fixtures

Project Completion December 2023





Liberty North HS



Liberty North HS



Liberty North HS



Liberty North HS

## WEEKLY PROGRESS REPORT Liberty Public Schools



#### **PUBLIC SCHOOLS**

## **PROJECT STATUS**

South Valley MS- Upgrades Complete Discovery MS - Upgrades Complete EPiC Elementary - Upgrades Complete LNHS - Upgrades Ongoing

## UPCOMING

Evergy Inspections All Four Schools Emergency LED Fixtures

Project Completion December 2023





South Valley Middle School



**Discovery Middle School** 



South Valley Middle School



**Discovery Middle School** 



## WEEKLY PROGRESS REPORT





Epic Elementary



Liberty North High School



Epic Elementary




Liberty North High School



## **EPIC ELEMENTARY ADDITION**






## **EPiC Elementary Addition**

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025



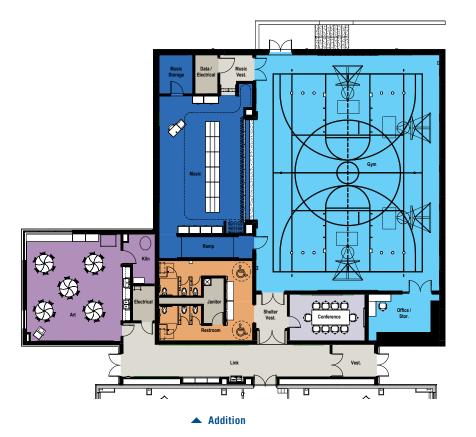



A Renovation Area

#### WEEKLY PROGRESS REPORT Storm Shelters 02/12/2024 Liberty Public Schools



#### **PUBLIC SCHOOLS**

### **PROJECT STATUS**

- EPiC Elementary
- Mobilization Complete
- Construction Fencing in Place
- Public Utilities Ongoing

## UPCOMING

EPiC Elementary -Site Grading -Building Pad -Plumbing Underground

Project Completion EPIC Feb 2025/DMS&SVMS June 2025





**EPiC Elementary - Public Utilities** 



EPiC Elementary - Public Utilities



**EPiC Elementary - Public Utilities** 



EPiC Elementary - Public Utilities




## **DISCOVERY MIDDLE SCHOOL**









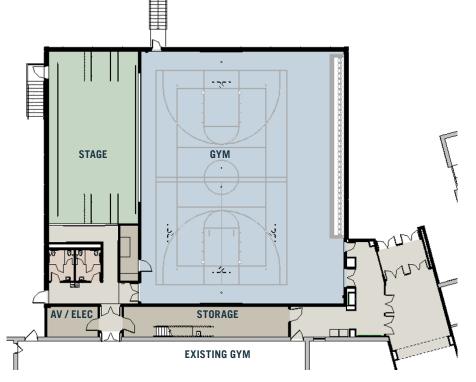

## **Discovery Middle School**

- 11,000 square foot additionICC 500 rated shelter
  - Additional PE space
  - Raised performance stage
  - Theatrical AV and lighting
- Increased audience capacity
  Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025




## SOUTH VALLEY MIDDLE SCHOOL









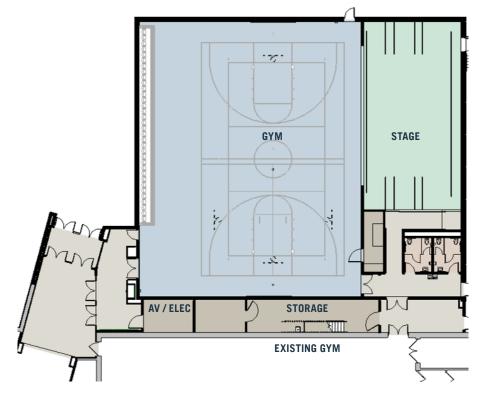

## South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025



## **DISTRIBUTION CENTER**





## **Distribution Center**

- · 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025





#### WEEKLY PROGRESS REPORT Distribution Center 2/12/24 Liberty Public Schools



#### **PUBLIC SCHOOLS**

## 2/12/24

### **PROJECT STATUS**

- Temp fence complete
- Access roads complete
- Site demo complete
- Barn demo complete
- Deep fills ongoing

## UPCOMING

- Site Utilities begin 2/12/24
- Flowfill existing storm line 1
- Storm line 4 & 5
- Replacing water line

Project Completion June 2025





Site Grading



Existing Drive Demo



Site Grading



Existing Drive Demo



## WEEKLY PROGRESS REPORT

## 2/12/24





Site Grading



Temp Road (Asphalt Millings)



Overall Site









Fine Arts Kid's Zone Technology Shared Amenities Building Systems Future Phase



## District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- · Shell space for future growth
- · Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

## WEEKLY PROGRESS REPORT Liberty Public Schools



## 2/9/24

## **PROJECT STATUS**

District Technology Center: -Began Framing Walls -Openings for New Windows Complete -MEP Demolition Complete -MEP Overhead Rough In Began -Plumbing In Wall Rough In Began -Concrete Sitework Began -Storm Drain Lines Complete -Masonry Build Back at Mechanical Rooms Complete

## UPCOMING

District Technology Center: -MEP In Wall Rough In -Complete MEP Overhead Rough-IN -Generator/XFMR Pad Install -Continue Concrete Site Work -Begin Drywall Installation -Begin Glazing System Install -Begin Communications Install

Project Completion June 2024






District Technology Center



District Technology Center



District Technology Center

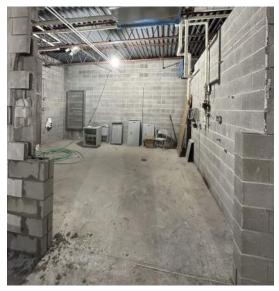

District Technology Center



## WEEKLY PROGRESS REPORT

## 2/9/24







District Technology Center



District Technology Center

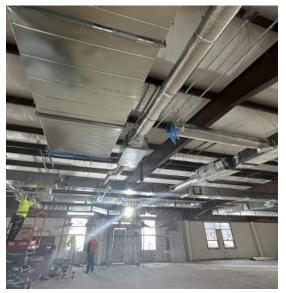

District Technology Center

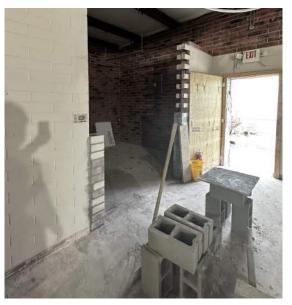

District Technology Center









## Hertiage Middle School

• 39,000 square feet academic renovation

Grade level neighborhoods with flex collaboration spaces

Integrated SPED resources


Renovated cafeteria & scramble

Restroom renovations

Exterior masonry repair & window replacement

Elevator replacement

 Projected Construction Schedule: Spring 2024–Fall 2025





LEVEL 2



LEVEL 1



LEVEL O




## LIBERTY HIGH SCHOOL









#### PHASE 2

## Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025





## LIBERTY ACADEMY










## **Shop Building**

- .1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large
  Projects
- Projected Construction Schedule: Spring 2024–Spring 2025





## LIBERTY ACADEMY

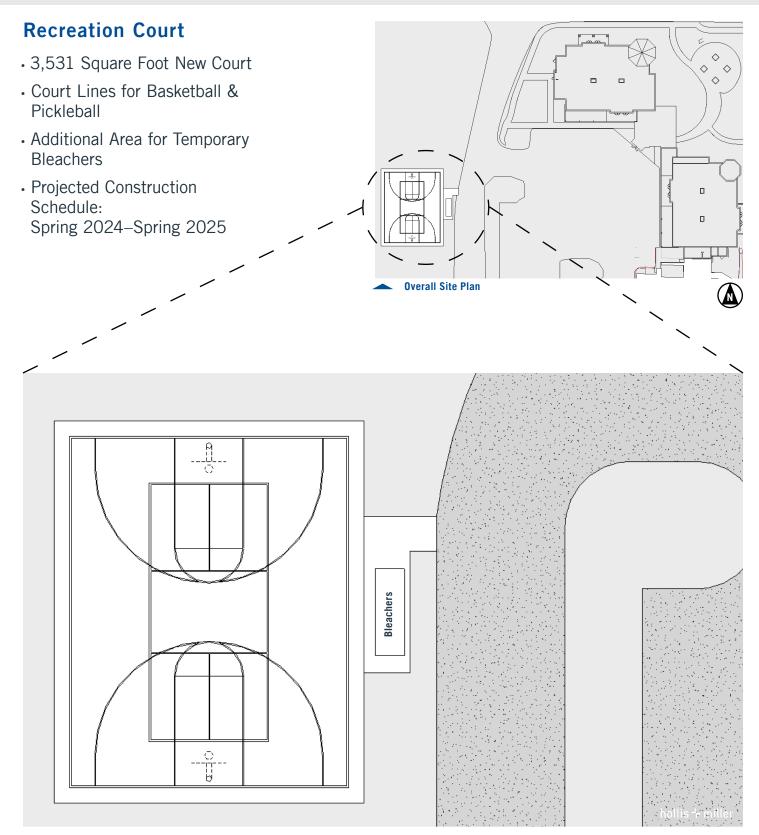




## **ALEXANDER DONIPHAN ELEMENTARY**

## **Interior Renovation**

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule: May 2024 - August 2025

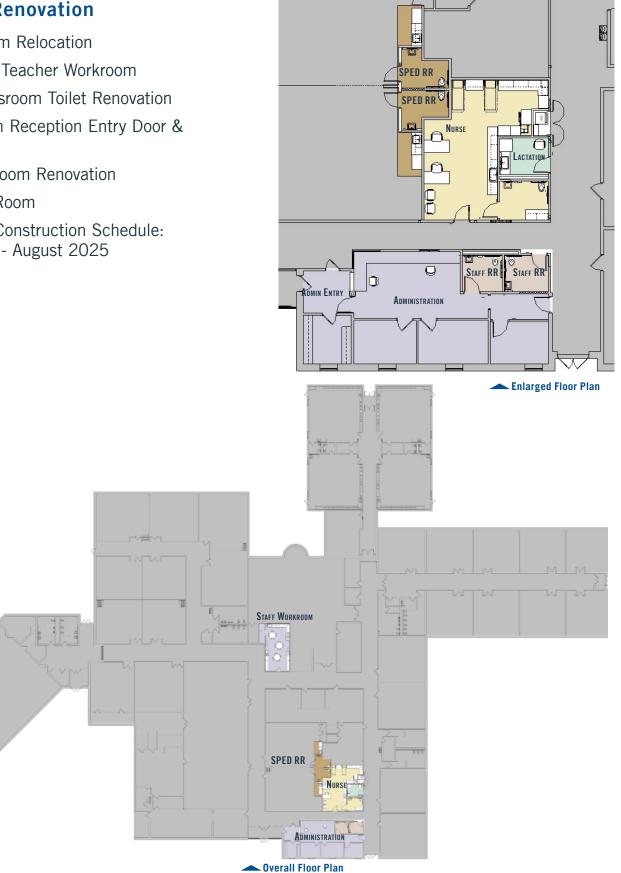




## **RIDGEVIEW ELEMENTARY**

## **Interior Renovation**

- Nurse Room Renovation
- Adminstration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule: May 2024 - August 2025



Administration

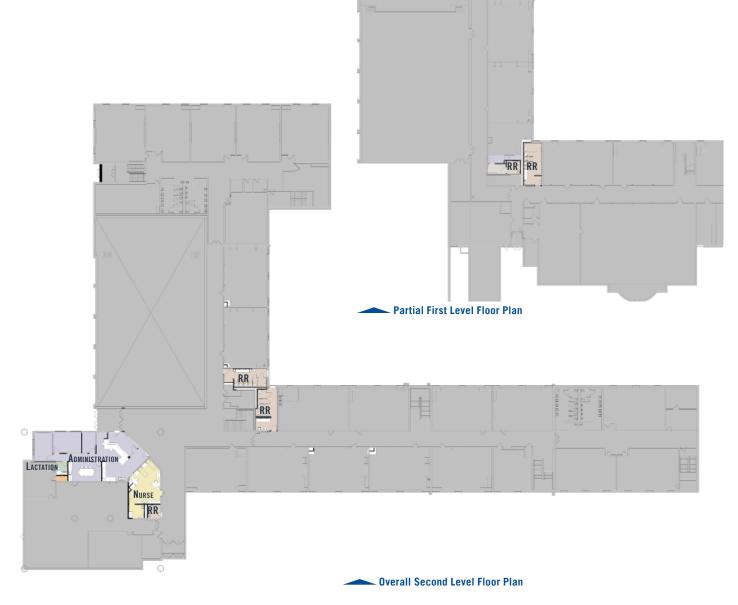



## **RIDGEVIEW ELEMENTARY**

## **Interior Renovation**

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule: May 2024 - August 2025



Administration

