



ID	Description	Original Duration	Start	Finish
General				
10	Notice to Proceed	0	12/05/22A	
20	Mobilize	1	12/05/22A	01/18/23A
30	Erosion Control	10	12/06/22A	12/30/22A
422	Approved Micropile Shop Drawings	3	12/06/22A	04/25/23A
423	Approved Grandstand Shop Drawings	1	06/16/23A	06/16/23A
412	Fence	15	09/18/23	10/06/23
415	Demo Track Surface	5	09/18/23	09/22/23
417	Resurface Track	10	12/01/23	12/14/23
418	Stripe Track	10	12/15/23	12/28/23
420	Final Site Inspection	0		12/28/23
430	OAC Walk Thru	0	12/29/23	
440	Punch List	10	12/29/23	01/11/24
450	Final Turnover	0		01/11/24
Home Side				
50	Site Demo (Home)	25	01/03/23A	02/06/23A
120	Site Grading/Micropile Bench (Home)	40	02/07/23A	05/15/23A
140	Storm Drainage	45	02/13/23A	06/27/23A
130	Micropiles Bench D	7	04/21/23A	06/09/23A
180	Form & Place Handicap Access Ramp Walls	60	05/01/23A	09/22/23
170	Sanitary Sewer	15	06/05/23A	06/23/23A
132	Micropiles Bench A	9	06/26/23A	07/06/23A
160	Water Distribution	15	07/18/23	08/07/23
134	Micropiles Bench B	9	08/08/23	08/18/23
150	Slope Stabilization	20	08/21/23	09/15/23
250	Concourse Concrete	30	09/15/23	10/26/23
136	Micropiles Bench C	9	09/18/23	09/28/23
210	Footings (Home)	20	09/22/23	10/19/23
190	Handicap Access Ramp Walls Cure Time	20	09/25/23	10/20/23
220	Grandstand Erection (Home)	30	10/20/23	11/30/23
200	Handicap Access Flat Work	15	10/23/23	11/10/23
416	Hang Doors, install hardware	5	10/26/23	11/01/23
413	Site Handrails	10	11/13/23	11/24/23
Visitor's Side				
40	Site Demo (Visitor)	10	12/20/22A	01/02/23A
60	Bench for Micropiles (Visitor)	20	01/03/23A	04/18/23A

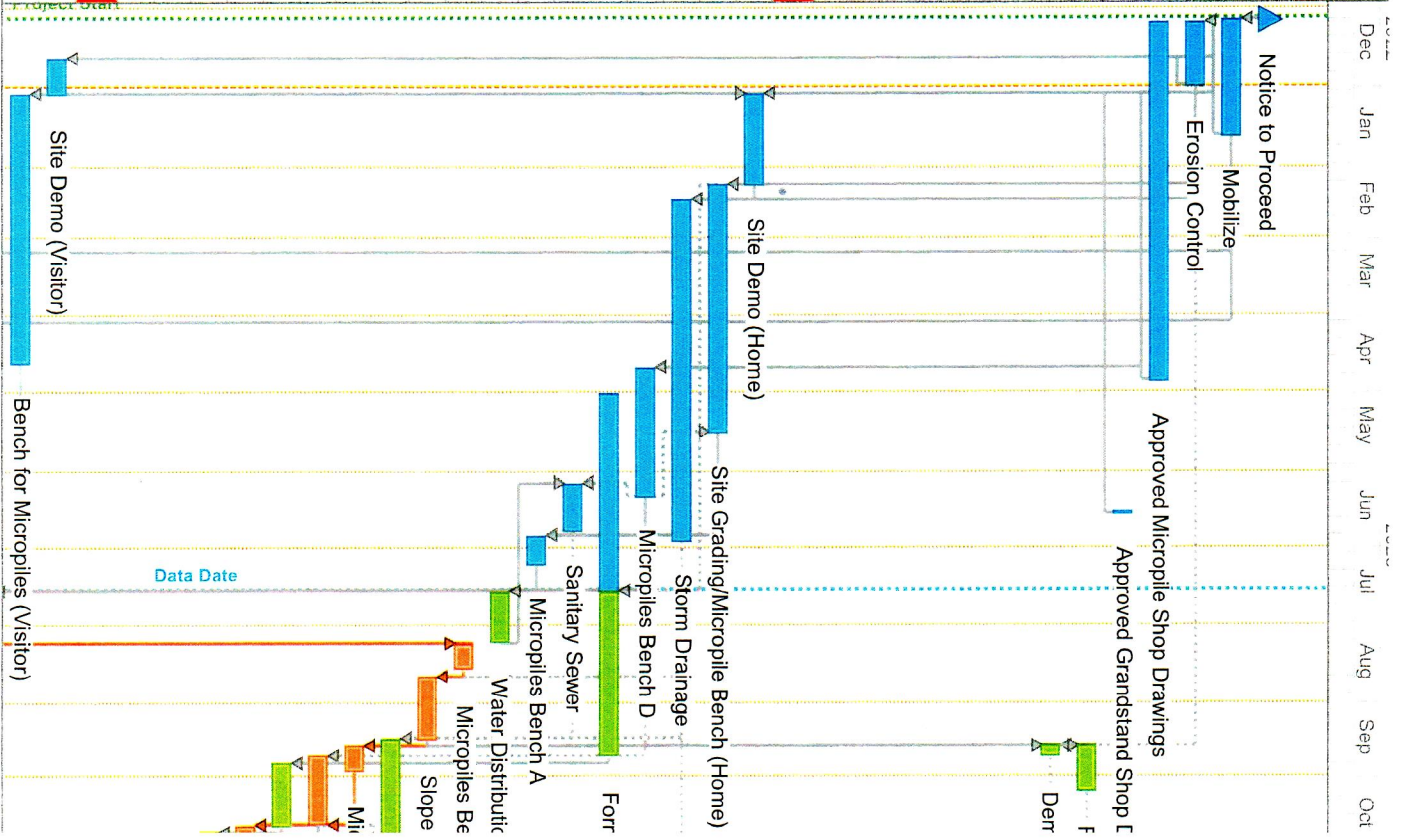

Start Date: 12/05/22
 Finish Date: 01/11/24
 Data Date: 07/18/23
 Run Date: 07/19/23

ID	Description	Original Duration	Start	Finish
70	Microplies (Visitor)	15	07/07/23A	08/07/23
80	Footings (Visitor)	10	08/08/23	08/21/23
90	Form & Place Retaining Wall (Visitor)	15	08/22/23	09/11/23
100	Retaining Wall Cure Time (Visitor)	20	09/12/23	10/09/23
110	Site Grading (Visitor)	15	09/26/23	10/16/23
230	Slab/Sidewalk (Visitor)	15	10/17/23	11/06/23
240	Grandstand Erection (Visitor)	10	11/07/23	11/20/23
Press Box				
428	Demolition Permit	0	02/15/23A	
260	Sawcut Concrete (Press Box)	5	03/06/23A	03/10/23A
290	Interior Demolition	10	04/03/23A	04/10/23A
270	Rough-in Plumbing	10	04/10/23A	04/17/23A
280	Place Concrete	1	07/18/23	07/18/23
340	Framing	10	07/18/23	07/31/23
380	Remove & Replace Siding	20	07/18/23	08/14/23
300	Masonry Walls	15	07/19/23	08/08/23
427	HVAC Installation	10	07/19/23	08/01/23
350	Hang & Finish Walls	10	08/01/23	08/14/23
390	Electrical Rough In	10	08/01/23	08/14/23
360	Frame Ceiling	10	08/15/23	08/28/23
419	Install Windows	10	08/15/23	08/28/23
370	Hang & Finish Ceiling	10	08/29/23	09/11/23
400	Hang Elec Fixtures	5	08/29/23	09/04/23
310	Epoxy Floor	5	09/05/23	09/11/23
320	Paint	10	09/12/23	09/25/23
330	Set Fixtures	5	09/26/23	10/02/23
414	Millwork	15	09/26/23	10/16/23
410	Final Building Inspection	0		10/16/23
425	Tile Carpeting and Base	7	10/17/23	10/25/23

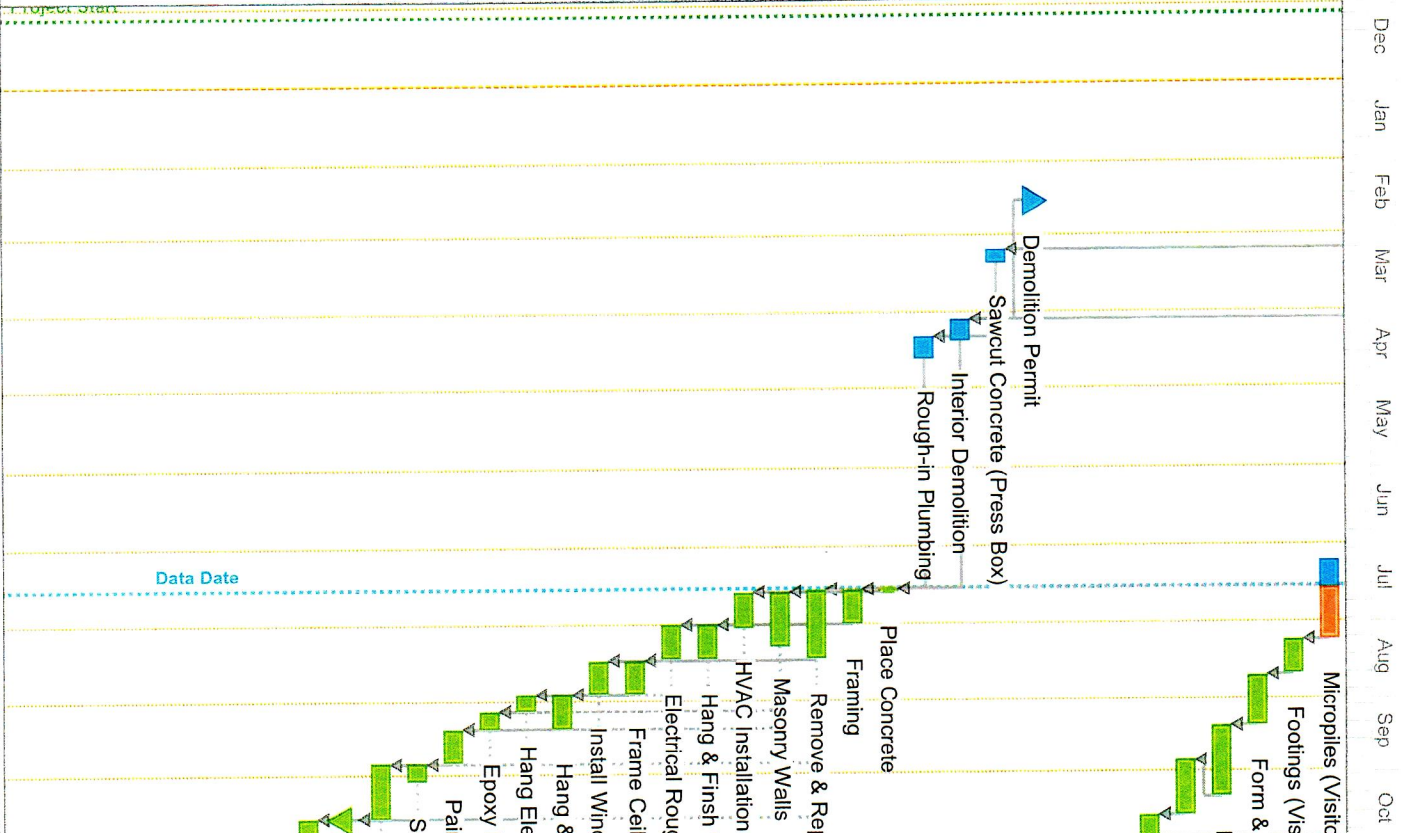

Start Date: 12/05/22
 Finish Date: 01/11/24
 Data Date: 07/18/23
 Run Date: 07/19/23
