


Completed Work:

- ICF Complete Area D
- > Topping Slab Prep at Area D and Stage Platform
- Canopy Columns Complete
- Continuing CMU at Strom Shelter
- Area A structural steel complete
- Continuing Area C structure over stair tower
- Continuing roof blocking area C, D and E
- Exterior Framing at Locker room and Mechanical Mezz Complete
- Framing Area A at 98%, Framing at Area C to 95%
- Framing Platform IDF Area A
- ➤ MEP and Sprinkler rough in multiple areas
- > Start piping for Geothermal at Area F and Area A
- Geothermal work progressing at well field
- Electric switch gear set in the building.


Upcoming Work/Look Ahead:

- Finish all ICF by weeks end
- Continue CMU Load Bear Walls (Estimated 92% Complete all areas)
- Complete Structural Steel Area A
- Complete Roof Dry-In in Area A and C.
- Complete all Framing Area A and Area C
- Continue Exterior Framing at Area E and Area C
- Continue Brick Veneer
- > Continue Painting (Block Fill). Gym Deck and Structure Painting to start next week
- Continue MEP and Sprinkler Rough Ins
- Complete Underground Zone Piping at Geothermal Field
- Continue Site Electrical (Light Pole Bases)






Area A – Corridor Soffit Framing and MEP Continues

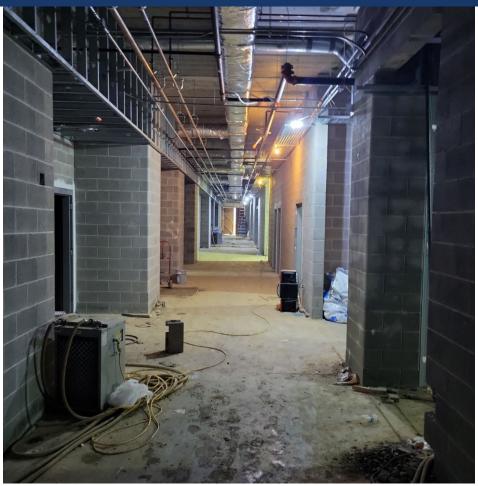




Area A – Wood Blocking at Roof Continues

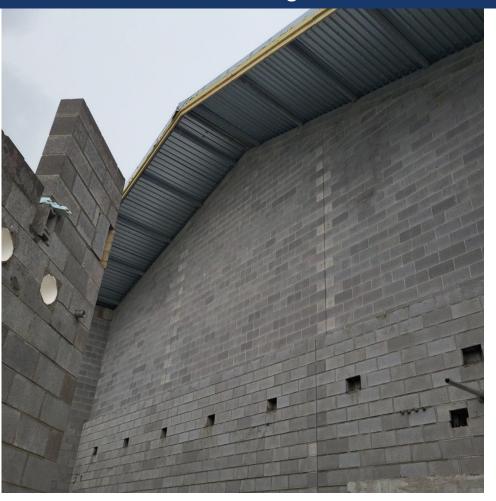




Area B – Above Ceiling MEP Started at Admin

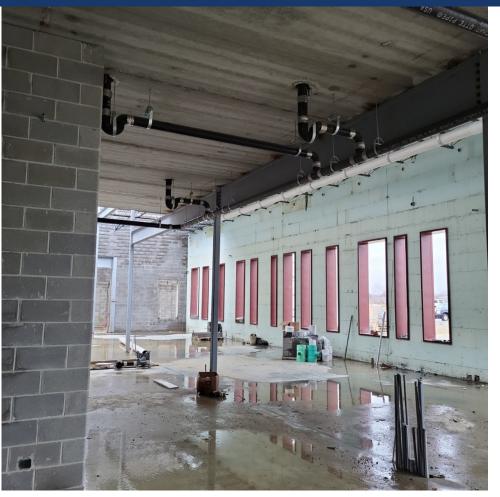




Area C – MEP Rough-ins on Mezzanine

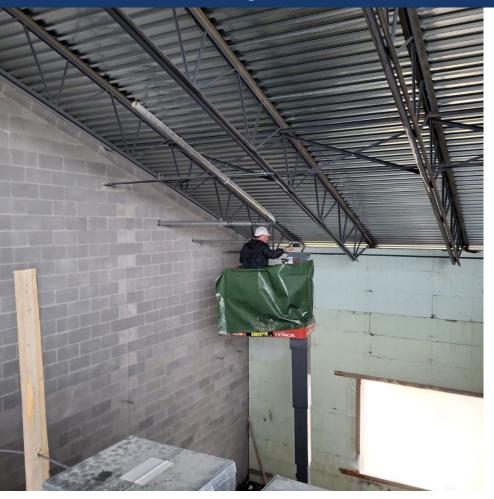




Area D – Corridor Slab prep for last pour

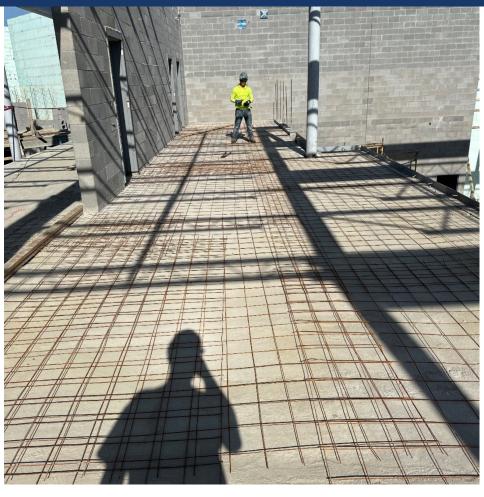



Area D – Media Center ICF Complete

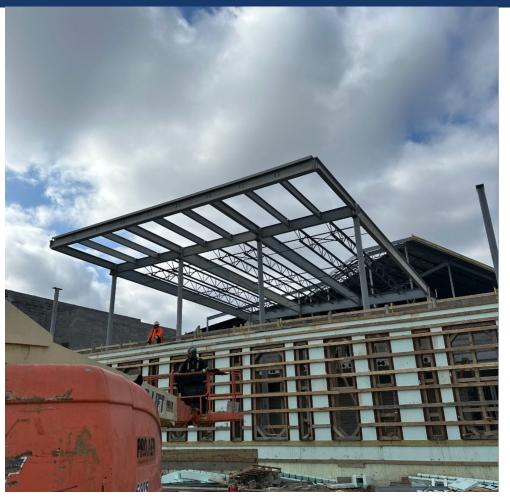



Area D – Media Center Roof Structure Ongoing





Area E – Cafeteria Roof Deck Installing

