




# Mary E. Britton Middle School

## ➤ Completed Work:

- All ICF Complete
- Canopy Foundations Complete
- Topping Slab at Stage Complete
- Topping Slab in Area D at 70%
- Continuing Topping Slab Prep at Area C
- Continue CMU at Area E Corridor
- Continue CMU at Area D and E Corridor
- Continuing Steel Erection at Area D. Area B at 90%
- Continuing Blocking for Roof
- Continuing In-Wall Blocking Area A and Area C
- Continuing Framing at Platform Elevation Areas A and C
- Continuing Sprinkler and MEP Rough Ins Multiple Areas
- Switch Gear has been set

## ➤ Upcoming Work/Look Ahead:

- Topping Slab at Area C
- Start Dock Concrete Slab
- Complete Roof Area Structural Steel Area B and Area D
- Complete Roof Area C
- Roofing Area C and Cafeteria
- Continue Block Fill and Caulking in Area C and A
- Dry-fall Painting in Gym
- Continue Sprinkler at Area C Second Floor
- Cleanup all Areas

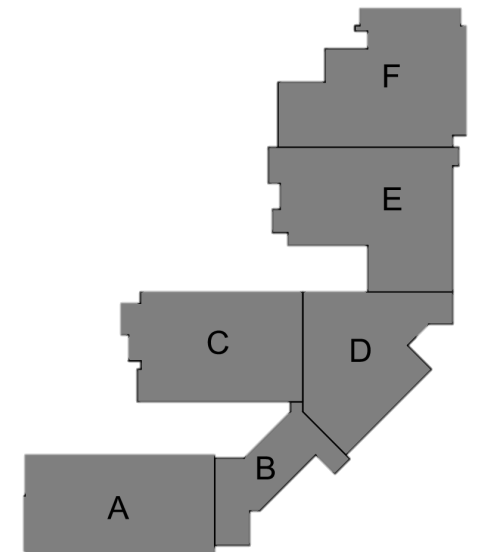

# Mary E. Britton Middle School



Area A - Curtain Wall Support Steel Install has begun in Stair



Week Ending March 8, 2024

# Mary E. Britton Middle School



Area B - Roof Steel started above 2<sup>nd</sup> Floor Corridor



Week Ending March 8, 2024

# Mary E. Britton Middle School




Area B – Family Resource Center Roof Steel Complete



Week Ending March 8, 2024

# Mary E. Britton Middle School



Area B - Main Entry Steel Roof Supports has begun



Week Ending March 8, 2024

# Mary E. Britton Middle School



## Area C – Mezzanine Concrete Slab Prep



Week Ending March 8, 2024

# Mary E. Britton Middle School



## Area D - 2nd Floor Slab Pour at Flex Spaces



Week Ending March 8, 2024

# Mary E. Britton Middle School



## Area D - Media Center Roof Steel Continues



Week Ending March 8, 2024

# Mary E. Britton Middle School



## Area E - Cafeteria Metal Box Outs at Windows



Week Ending March 8, 2024
