
## **MONTHLY REFFERENDUM REPORT DETAILED - as of February 29, 2024**



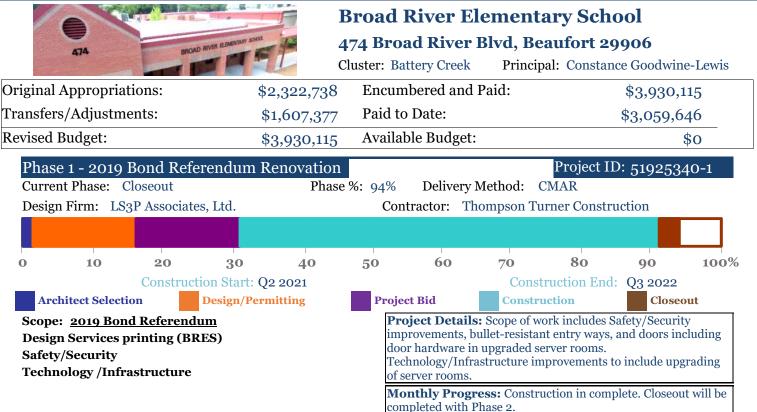

Phase 2 - 2019 Bond Referendum Renovation Project ID: 51925340-2											
Current Phase: Construction				Phase %: 85% Delivery Method:				CMAR			
Design	n Firm: LS3	P Associate	es, Ltd.	Contractor: Thompson Turner Construction							
0	10	20	30	40	50	60	70	80	90	100%	
Co				Construction Start: Q2 2022			Cons	Construction End: Q3 2023			
Architect Selection Design/Perm				itting	Project Bid		Constr	Construction		Closeout	
						Project Details: Scope of work includes Safety/Security					
CM Pre-Con Services (BRES)						improvements to the cameras and notification systems.					
Design Services (BRES)						Technology/Infrastructure improvements to include sound, wireless access, and lighting.					
Safety/Security						Monthly Progress: Construction is nearing completion.					
Technology /Infrastructure						Cutover is complete and final punch is in progress.					
Technology undrer \$5,000									<u> </u>	<u> </u>	
Utility Upgra	Services for des	r Technolo	ogy								
