
## **MONTHLY REFFERENDUM REPORT DETAILED - as of January 31, 2024**



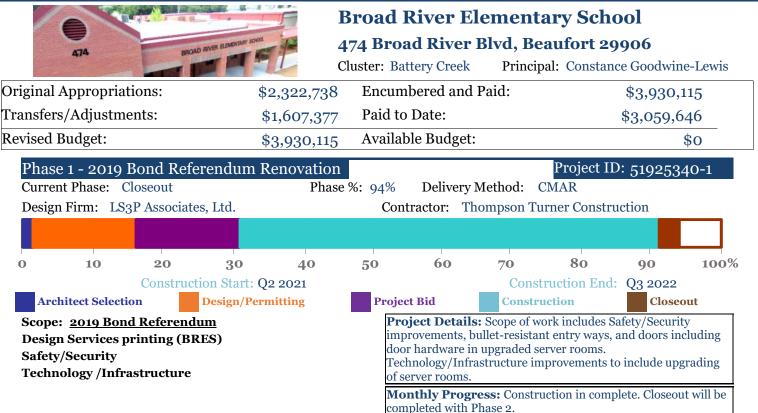

Phase 2 - 2019 Bond Referendum Renovation Project ID: 51925340-2										0-2
Current Phase: Construction				Phase %: 85% Delivery Method:				CMAR		
Design	n Firm: LS3	P Associat	es, Ltd.	Contractor: Thompson Turner Construction						
0	10	20	30	40	50	60	70	80	90	100%
Со				Constructio	onstruction Start: Q2 2022 Co			nstruction End: Q3 2023		
Architect Selection Design/Permi				itting	Project Bid Con		Constr	struction Closeout		ut
Scope: 2019 Bond Referendum						Project Details: Scope of work includes Safety/Security				
CM Pre-Con Services (BRES)						improvements to the cameras and notification systems. Technology/Infrastructure improvements to include sound,				
Design Services (BRES)						wireless access, and lighting.				
Safety/Security						Monthly Progress: Construction is nearing completion.				
Technology /Infrastructure						Cutover is complete and final punch is in progress.				
Techn	ology undre	r \$5,000				<u> </u>		-		
Utility Services for Technology Upgrades										
upgra	ues									
