


Measure BB Bond

21st Century Classroom Improvements
March 26, 2024



CUMMING
GROUP



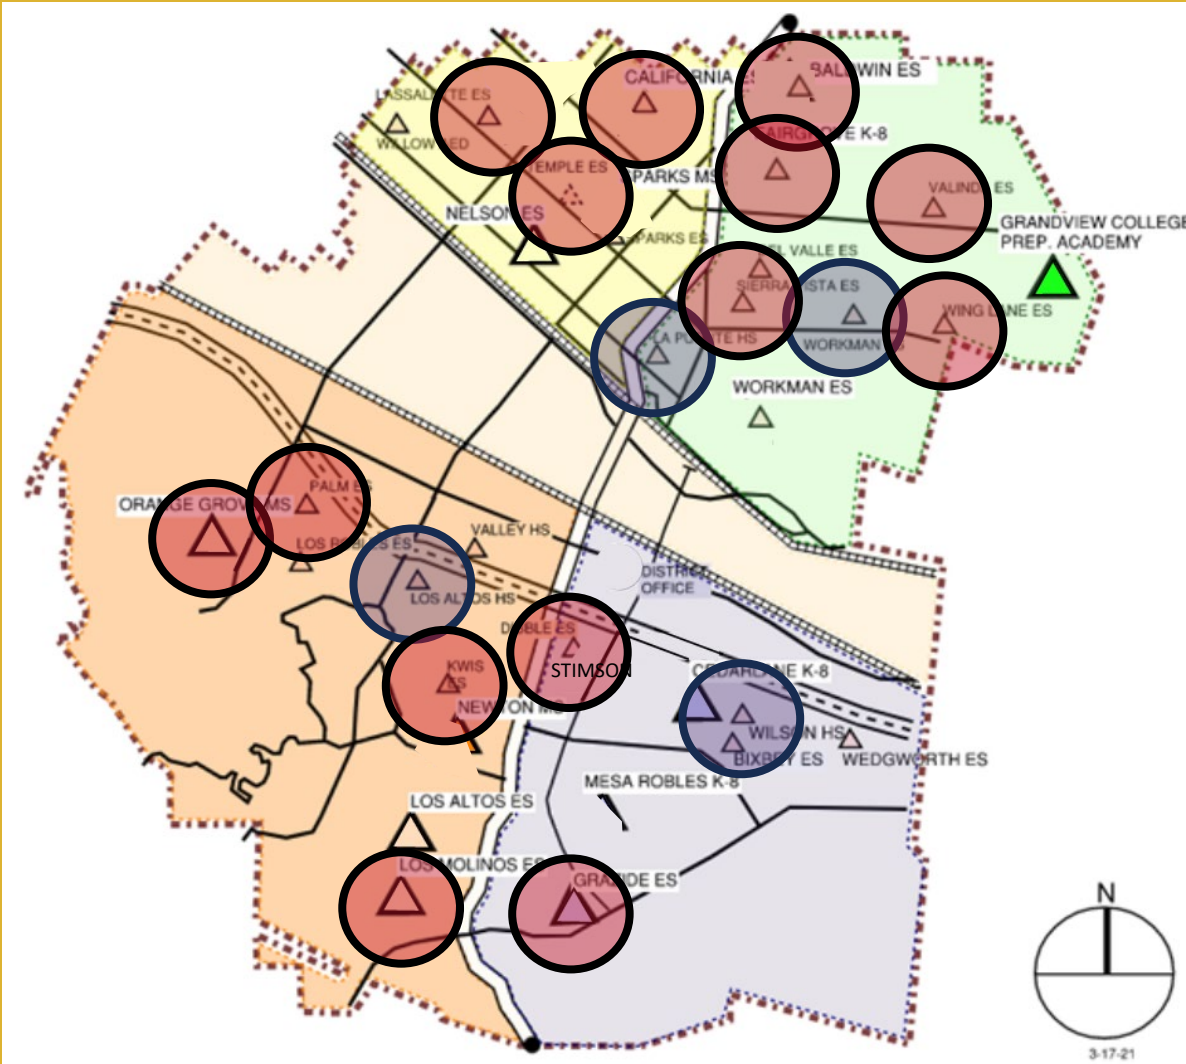

**IN PROGRESS
CONSTRUCTION**

- La Puente HS
- Workman HS
- Los Altos HS
- Wilson HS
- Stimson EC

AT DSA FOR REVIEW

- California ES this month
- Baldwin ES this month
- Los Molinos ES
- Grazide ES

IN DESIGN

- Kwis ES
- Lassalette ES
- Fairgrove K-8
- Orange Grove MS
- Sierra Vista MS
- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES

IN PROPOSAL PHASE

- Valley Alternative

COMPLETED

- Nelson ES**
- Los Altos ES**
- Workman ES**
- Mesa Robles K-8**
- Cedarlane K-8**
- Sparks MS**
- Newton MS**
- Grandview K-8**

PHASE B PROGRESS

- 1. Baldwin ES Construction Documents to DSA 1/23/2024 In Back-Check Process Out By 4/25/2024
- 2. California ES Construction Documents to DSA 1/23/2024 In Back-Check Process Out By 4/25/2024

Anticipated Construction Start Fall of 2024

- 3. Los Molinos ES Construction Documents at DSA 3/12/2024 Anticipated Plan Check Completion TBD
- 4. Graziade ES Construction Documents at DSA 3/12/2024 Anticipated Plan Check Completion TBD

Anticipated Construction Start Winter of 2024

- 5. Kwis ES Construction Documents Design Development
- 6. Lassalette ES Construction Documents Design Development

Anticipated Construction Start New Year of 2025

- 7. Palm ES Construction Documents Design Development Schematic Design
- 8. Valinda ES Construction Documents Design Development Schematic Design

Anticipated Construction Start Spring of 2025

- 9. Fairgrove K-8 Construction Documents Design Development
- 10. Orange Grove MS Construction Documents Schematic Design

Anticipated Construction Start Summer of 2025

- 11. Sierra Vista Construction Documents Design Contract Award
- 12. Sparks ES Construction Documents Design Contract Award

Anticipated Construction Start Summer -Fall of 2025

- 13. Wing Lane ES Construction Documents Design Contract Award
- 14. Valley Alternative Construction Documents Design Proposal


Anticipated Construction Start Fall of 2025



HIGH SCHOOL
REFRESH
PROJECTS


HIGH SCHOOL REFRESH #1

- Scope Limited to **Replacement of Finishes**
- **Benefits:**
 - Avoid DSA Review Requirements
 - Saving Time
 - Improvements Starting Sooner
 - Conserving Bond Funds

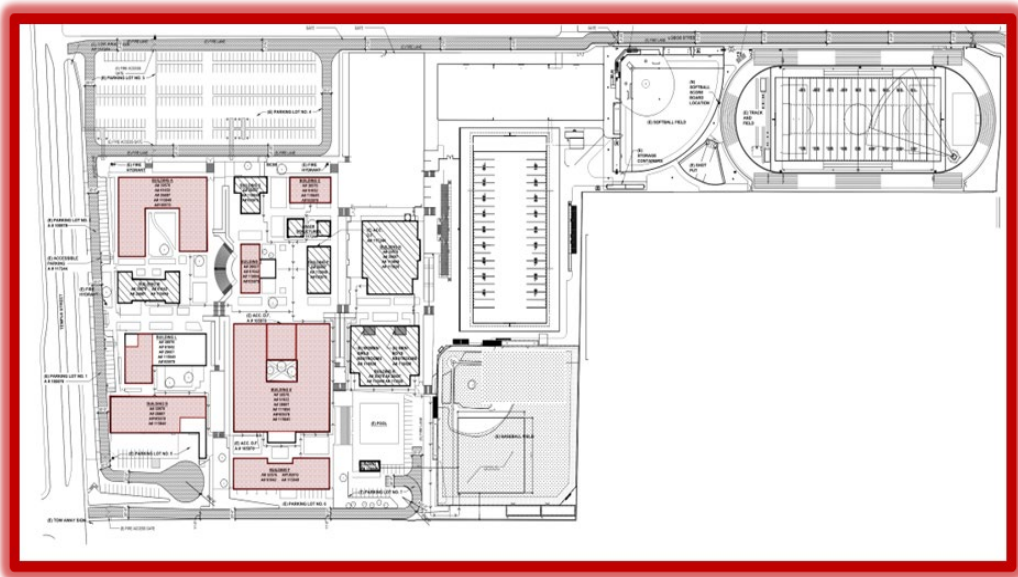

WORKMAN HIGH SCHOOL
43 CLASSROOMS

- New LVT Flooring
- New Wall Base
- New Paint, Repair, Prep.
 - Walls
 - Trim
 - Ceilings
 - Doors
 - Windows
- New Grilles at Heat Pumps
- Repair and Replace Damaged Ceiling Tile
- Repaint Ceiling Grid
- Interior Brick cleaning
- Re-lamp at light (By District)
- Deep Cleaning
- Hazmat Abatement

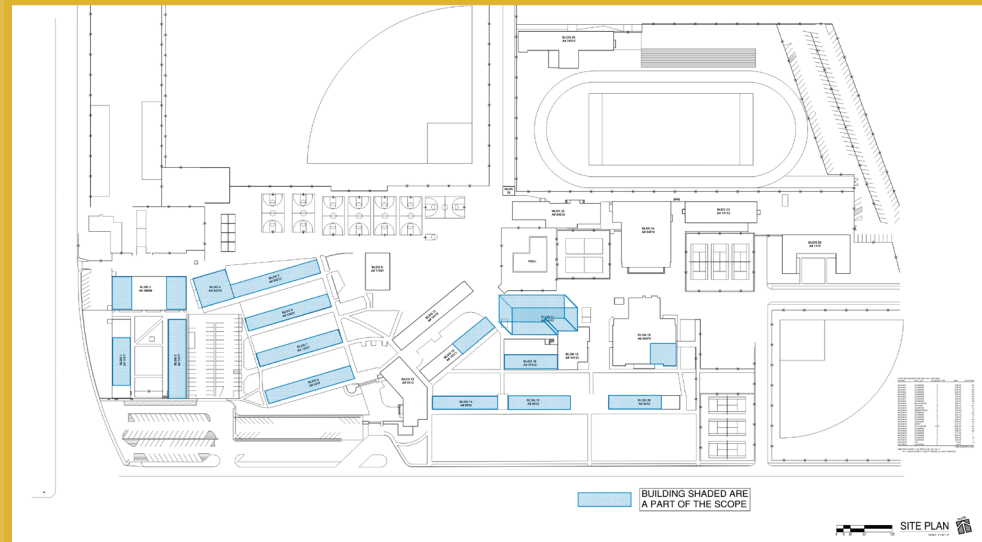

LA PUENTE HIGH SCHOOL
55 CLASSROOMS


REFRESH GROUP #1

Workman Classroom Phase 1 Complete

Phase 2: Demo Has Begun




Room A-12 Primer coat

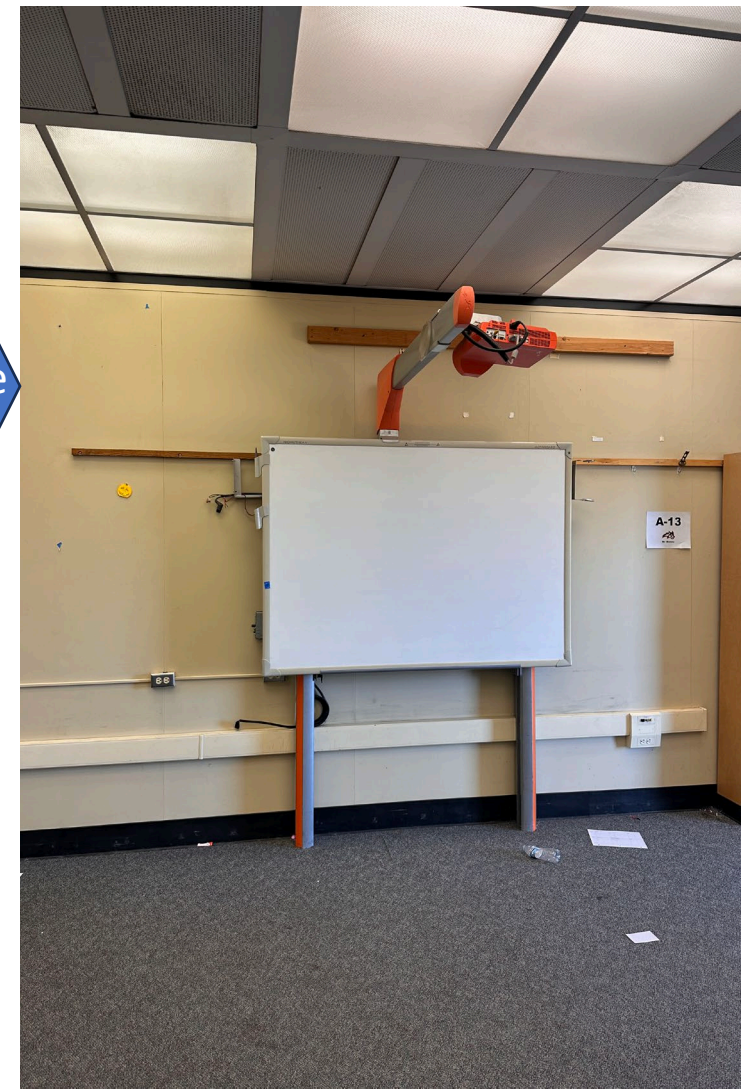


Room A-11 Demo

REFRESH GROUP #1


La Puente HS - Phase 1 Complete
Phase 2: Classroom 2, Before &
During Refresh




HIGH SCHOOL REFRESH #2

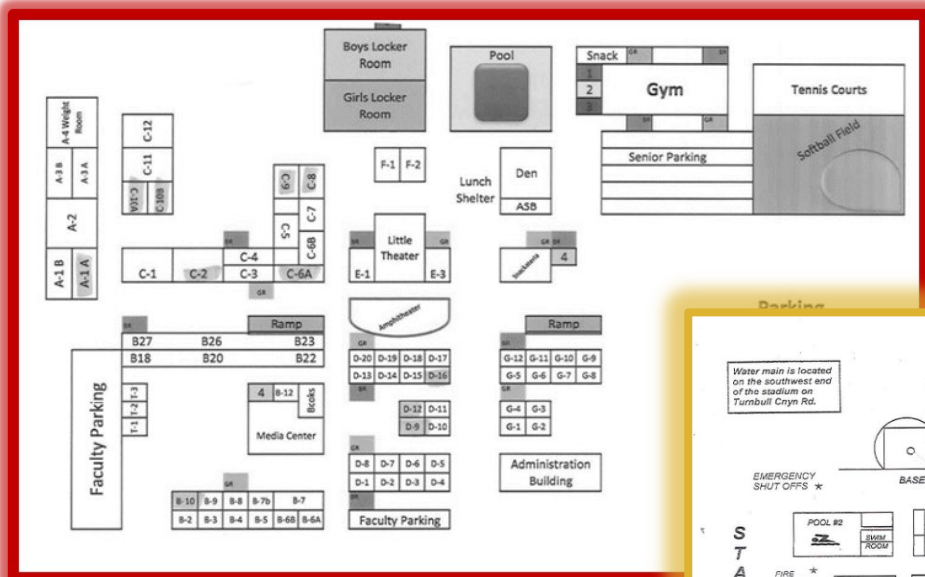

WILSON HIGH SCHOOL
59 CLASSROOMS

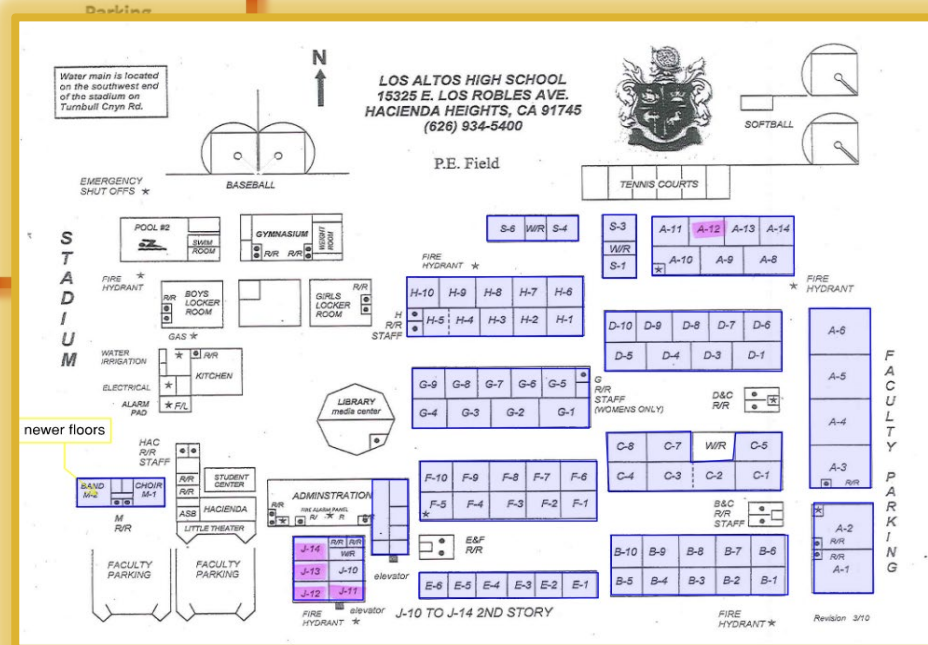




LOS ALTOS HIGH SCHOOL
69 CLASSROOMS

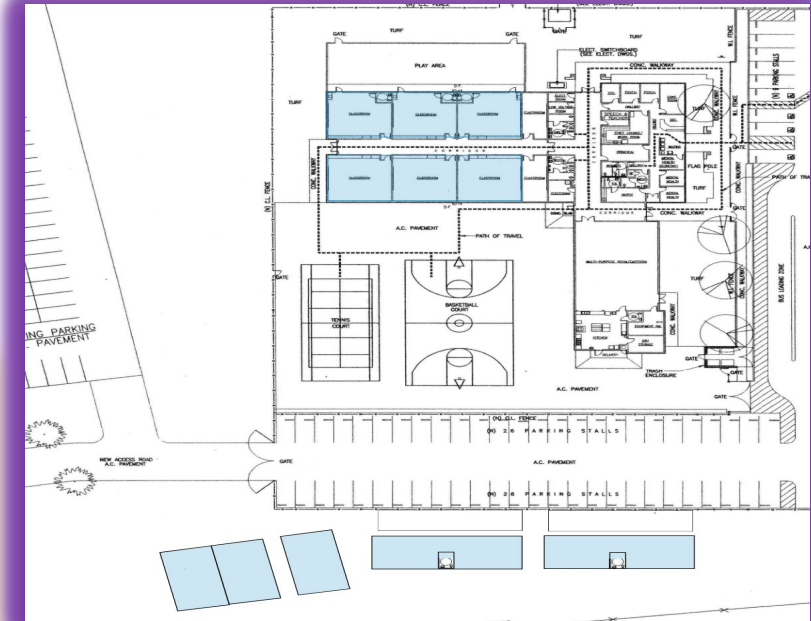

STIMSON LEARNING CENTER
10 CLASSROOMS

REFRESH GROUP #2

Wilson HS Phase 1 Classroom C-12 During New Floor Prep

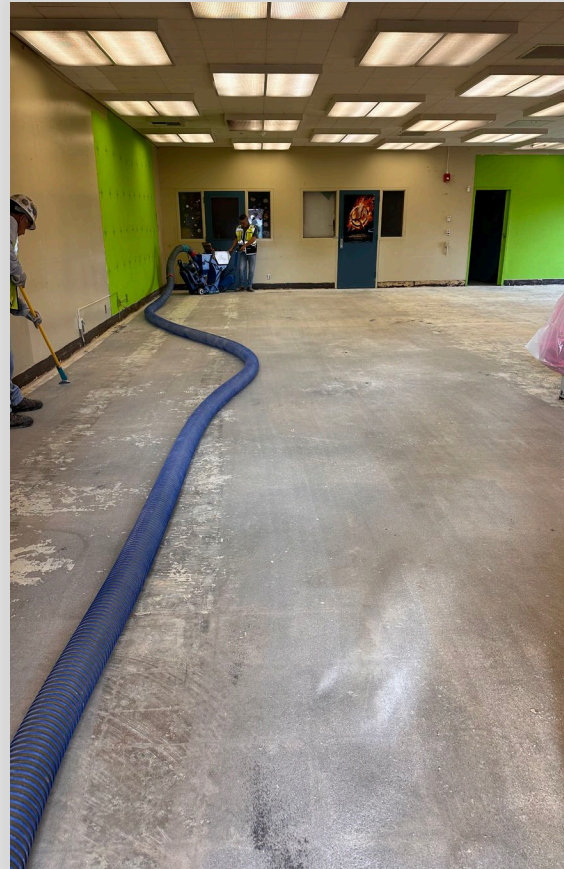

REFRESH GROUP #2

Los Altos HS Phase 1
Classroom B-4. Before and
During Demo





QUESTIONS & ANSWERS
