




Mary E. Britton Middle School

➤ Completed Work:

- Structural Steel at Strom Shelter Nearing Completion
- Handrails are Near Welding Completion. Ship Ladders Area A Complete
- CMU Platform G301 roughly 30% complete
- Continue CMU Plumbing Walls Area A 1st Floor
- Freezer/Cooler Slab is prepped for Pour Next Week
- Prep Topping Slab G301 Corridor. Pour Stop Plates Installed for Pour Next Week
- Painters Began Spraying Walls this week in Area C
- Membrane Roofing at Cafeteria and Main Entrance Lobby Complete
- Continue Hanging Sheet Rock Area A 1st Floor
- Dense Glass near Completion at Area B
- Continue Pulling Feeder Wire all Panels
- Continuing to Excavate Geothermal Lines to Building Connection
- Topping Slab prep at 2nd Floor Area B/D Corridor complete for Pour on 4/13
- Mechanical Platform 2nd Floor Area B Prepped and Ready for Pour on 4/13
- Continue Roof Blocking Area E

➤ Upcoming Work/Look Ahead:

- Pour Cooler/Freezer Slab and G301 Platform
- Start Area C Handrails Platform
- Continue Structural Steel at Gym Lobby Following Masonry
- Complete Load Bearing Masonry and Misc. Masonry infills
- Continue Exterior Framing
- Continue Brick Laying
- Continue Block Fill at Area C and Start Block Fill at Kitchen
- Finish Hanging Sheetrock Area A 1st Floor then move to Second Floor
- Continue MEP and Sprinkler Rough In and Equipment Connections
- Continue Pulling Main Building Power
- Finish Geothermal Piping to the Building
- Prep and Pour Sidewalks for Loading Dock
- Install Stala Frames and Door Frames throughout Various Areas
- Start ACM Panels 4/22 to 4/26

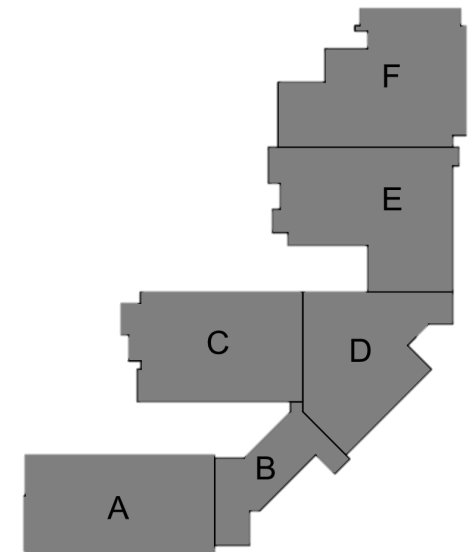

Mary E. Britton Middle School

Area A – Air Barrier on ICF Continues



Week Ending April 12, 2024

Mary E. Britton Middle School




Area A – block Filler, Soffit Framing and MEP Roughins



Mary E. Britton Middle School




Area B- Mezzanine Units Set

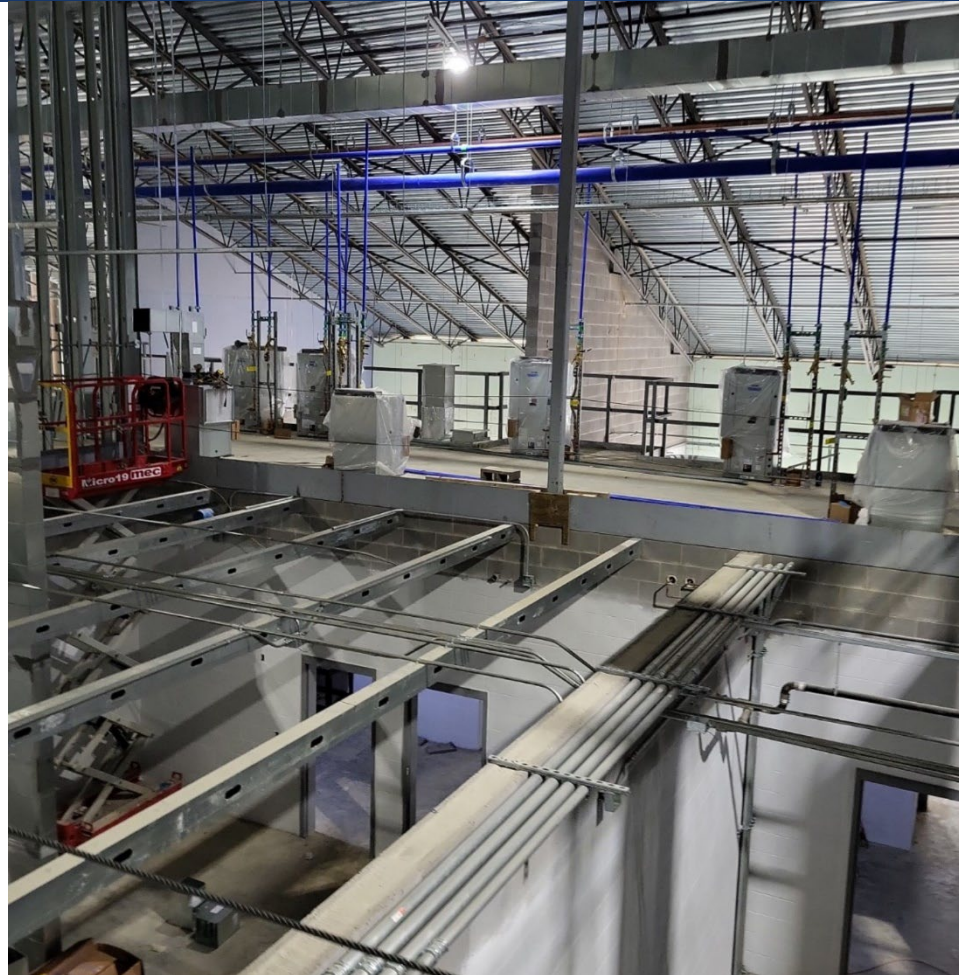

Week Ending April 12, 2024

Mary E. Britton Middle School



Area B – 2nd Floor Slab Prep for Concrete Topping



Week Ending April 12, 2024

Mary E. Britton Middle School



Area D – Media Center Roof Decking Installed



Week Ending April 12, 2024

Mary E. Britton Middle School



Area E – Storm Shelter Steel at Roof Continues



Week Ending April 12, 2024

Mary E. Britton Middle School



Area F – Kitchen Loading Dock Wall Poured



Week Ending April 12, 2024



Mary E. Britton Middle School

Area F – Kitchen Roof Continues



Week Ending April 12, 2024
