




Mary E. Britton Middle School

➤ Completed Work:

- Structural Steel at Storm Shelter Near Completion pending Material
- Handrails Complete Area A. Started Handrails Area C
- CMU Platform G301 roughly 90% complete
- Continue CMU Plumbing Walls Area A 2nd Floor
- Freezer/Cooler Slab is prepped for Pour on 4/23
- Prep Topping Slab G301 Corridor. Pour Stop Plates Installed for Pour on 4/23
- Block Fill finished at 2 floor Area C. Starting on 1st Floor Area C
- Finish Steel Decking at Area D for Roof
- Continue Hanging Sheet Rock Area A 1st Floor in Classrooms and Soffits
- Dense Glass Complete at Area B Mechanical Platform, Continue at Gym
- Continue Pulling Feeder Wire all Panels
- Continuing to Excavate Geothermal Lines to Building Connection
- Topping Slab Area B/D Corridor is Poured
- Mechanical Platform Area B is Poured

➤ Upcoming Work/Look Ahead:

- Pour Cooler/Freezer Slab and G301 Platform on 4/23
- Stairs 8 Weeks out
- Roofing Panels 7 Weeks out
- Start Terrazzo in the Coming Weeks
- Start Membrane Roofing at Area B/D
- Continue Brick Laying
- Continue Block Fill at Area C 1st Floor and Start Block Fill at Kitchen
- Finish Hanging Sheetrock Area A 1st Floor then move to Second Floor
- Continue MEP and Sprinkler Rough In and Equipment Connections
- Continue Pulling Main Building Power. 2-3 Weeks out of Full Power
- Finish Geothermal Piping to the Building
- Prep and Pour Sidewalks for Loading Dock
- Continue Misc. Roof Blocking
- Start ACM Panels 4/22 to 4/26

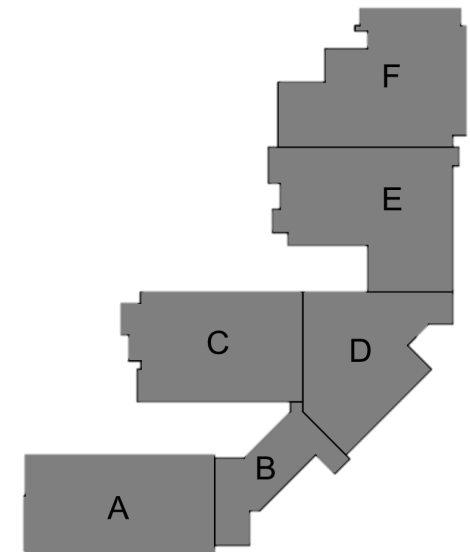

Mary E. Britton Middle School



Area A – Interior Gyp Board Starting Over



Week Ending April 19, 2024

Mary E. Britton Middle School



Area C – Framing above Flex Space for Ceilings Continues



Week Ending April 19, 2024

Mary E. Britton Middle School



Area D - Media Center Framing at Overlook Complete



Week Ending April 19, 2024

Mary E. Britton Middle School



Area D – Media Center Framing at Overhang Complete




Week Ending April 19, 2024

Mary E. Britton Middle School



Area D – Corridor Concrete Topping Poured

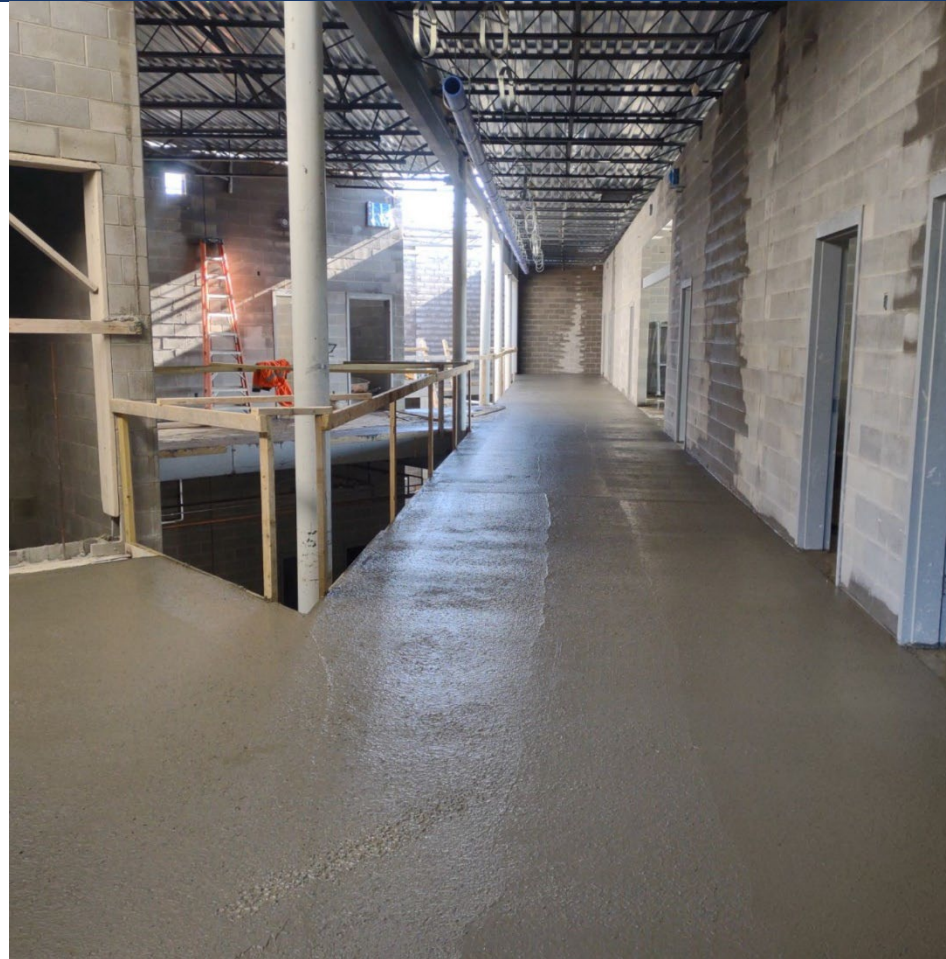

Week Ending April 19, 2024

Mary E. Britton Middle School



Area F – Roof Access Door Installed



Week Ending April 19, 2024

Mary E. Britton Middle School



Overall – Roofing is Ongoing Around Building



Week Ending April 19, 2024

Mary E. Britton Middle School



Site – Vault Connections to Building Ongoing



Week Ending April 19, 2024
