




# Mary E. Britton Middle School

- **Completed Work:**
  - Topping Slabs Complete
  - Cooler Freezer Slab Complete
  - Continuing Concrete at Dock/Entry
  - CMU at Area E/F at 95%. Load Bearing CMU complete by Friday
  - Continuing Structural Steel at Storm Shelter
  - Continuing Handrail at Platforms
  - Continuing Exterior Metal Stud Framing and Furring Area B, Area F and Area D
  - Continuing Sheet Rock Hanging Area A Second Floor
  - Continuing Finishing Drywall Area A First Floor
  - Continuing Block Fill and Caulking Area C First Floor
  - Installing Exterior Peel and Stick Membrane
  - Continuing Sprinkler Above Ceiling Area C
  - Continuing Plumbing and Mechanical Rough Ins and Equipment Installation
  - Continuing Mechanical Duct Work Area C and Area F Platforms
  - Finished Geothermal Vault Work and Installing Pipe to Mechanical Room. Complete by end of the week
- **Upcoming Work/Look Ahead:**
  - Continue Dock Concrete pending trench drain arrival
  - Complete Masonry Load Bearing
  - Continue Misc. Masonry walls, Rubbing and Patching
  - Continue Decking at Storm Shelter
  - Set Bar Joist and Decking at F100 Corridor and Main Entry
  - Exterior Framing and Interior Framing Continuing
  - Start Installing ACM Panels at Gym above Locker Room
  - Start Mobilizing Terrazzo Flooring
  - Continue Block Fill, Finish C and Move to Kitchen
  - Full Building Power Friday 4/26/24
  - Start Exterior Finish Grading at Islands
  - Continue Sprinkler, Plumbing and Mechanical Equipment Systems
  - Continue Brick Veneer with additional crews
  - Complete Geothermal System, Flush and Test

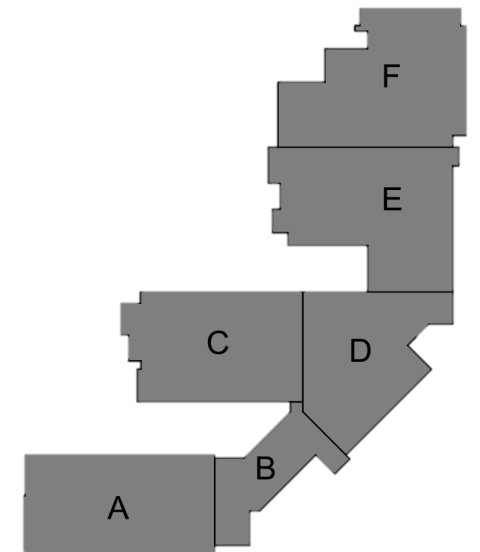

# Mary E. Britton Middle School



Area A – Ceiling Structure Complete at Flex Classrom



Week Ending April 26, 2024



# Mary E. Britton Middle School

Area C – CMU Blockfill Continuing



Week Ending April 26, 2024



# Mary E. Britton Middle School



## Area C – Louvers Installed



Week Ending April 26, 2024

# Mary E. Britton Middle School



## Area D – Roof Joist Installed



Week Ending April 26, 2024



# Mary E. Britton Middle School

Area E – Stud Framing at Window Boxouts Continues



Week Ending April 26, 2024



# Mary E. Britton Middle School

## Area F – Gym Furring for Metal Panels



Week Ending April 26, 2024

# Mary E. Britton Middle School



Area F – Loading Dock Brick Started



Week Ending April 26, 2024



# Mary E. Britton Middle School



## Area F – Mechanical Units Going up to the Mezzanine



Week Ending April 26, 2024
