

# Project Update

## St. Pius X Catholic School

December 1, 2023



**WE BUILD GREAT** SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .

# Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



**PARRISH**  
CONSTRUCTION GROUP

**TEAMS**

**WE BUILD GREAT**

## ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none"><li>Catholic Education of North Georgia, Inc.</li><li>St. Pius X Catholic High School</li></ul>	<ul style="list-style-type: none"><li>CDH Architecture</li></ul>	<ul style="list-style-type: none"><li>David Loudermilk, Project Director</li><li>Alex Johnson, Project Manager</li><li>Hoyt Clance, Superintendent</li><li>Trey DeRieux, Project Engineer</li><li>Drew Plunkett, Asst. Superintendent</li></ul>



**PARRISH**  
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

# SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	3
OCTOBER 2023	31	3	1
NOVEMBER 2023	30	5	2
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITWORK	80%
FOUNDATIONS	75%
UNDERGROUND UTILITIES	95%
SLAB ON GRADE/DECK	100%
STEEL	95%
ELECTRICAL	60%
PLUMBING	60%
MECHANICAL	65%
ROOFING	95%



PARISH  
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT \_\_\_\_\_.

## WEEKLY PROGRESS UPDATE

- METAL FRAMING AND DRYWALL CONTINUED
- MEP OVERHEAD CONTINUED
- BUILDING BRICK CONTINUED
- BLOCKFILL CONTINUED
- SWITCHBACK RAMP FOUNDATIONS POURED
- ROOF TOP UNITS SET
- WINDOWS/STOREFRONT CONTINUED



**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
<b>Site Work</b>		
GRADING AND UTILITIES	RUBY-COLLINS	90%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
<b>Building Systems</b>		
MECHANICAL	GEORGIA MECHANICAL	65%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	60%
PLUMBING	POLK COUNTY PUBLIC SERVICE	60%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	80%
<b>Building Structure</b>		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	100%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	95%
EXTERIOR WALLS	PARRISH MASONRY	100%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	90%



**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	90%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	75%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	55%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%








**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## PROGRESS UPDATE

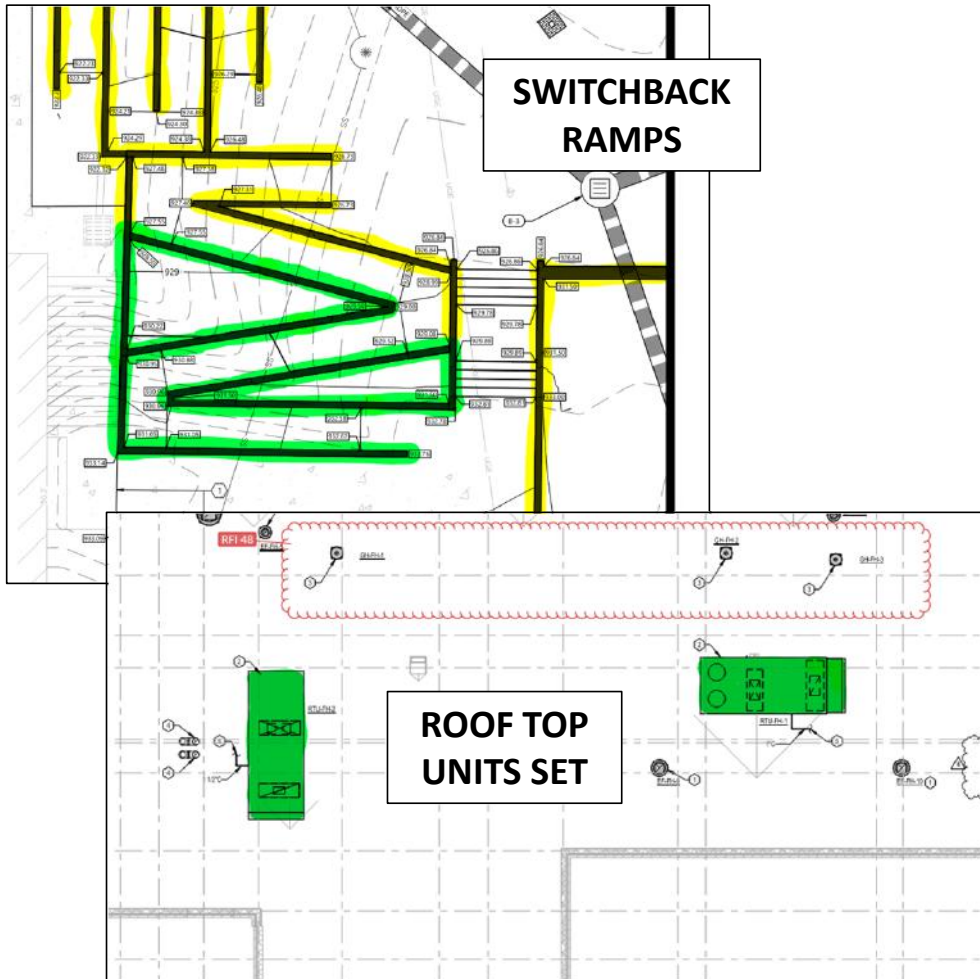

**GREEN HIGHLIGHTED SECTIONS  
HAVE BEEN COMPLETED; YELLOW  
HIGHLIGHTED IN PROGRESS**

**FRAMING & DRYWALL  
CONTINUED; MEP OVERHEAD  
CONTINUED; ROOF TOP UNITS  
SET; SWITCHBACK RAMPS  
CONTINUED**

**BUILDING BRICK SHOULD FINISH  
UP NEXT WEEK; SWITCHBACK  
RAMPS CONTINUED NEXT WEEK;  
BLOCKFILL SHOULD FINISH UP  
NEXT WEEK**



**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS



**SETTING ROOF TOP UNITS**



**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS

**WALLS FORMED FOR THE SWITCHBACK  
RAMPS**





**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS

**BRICK CONTINUED**






**PARISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS

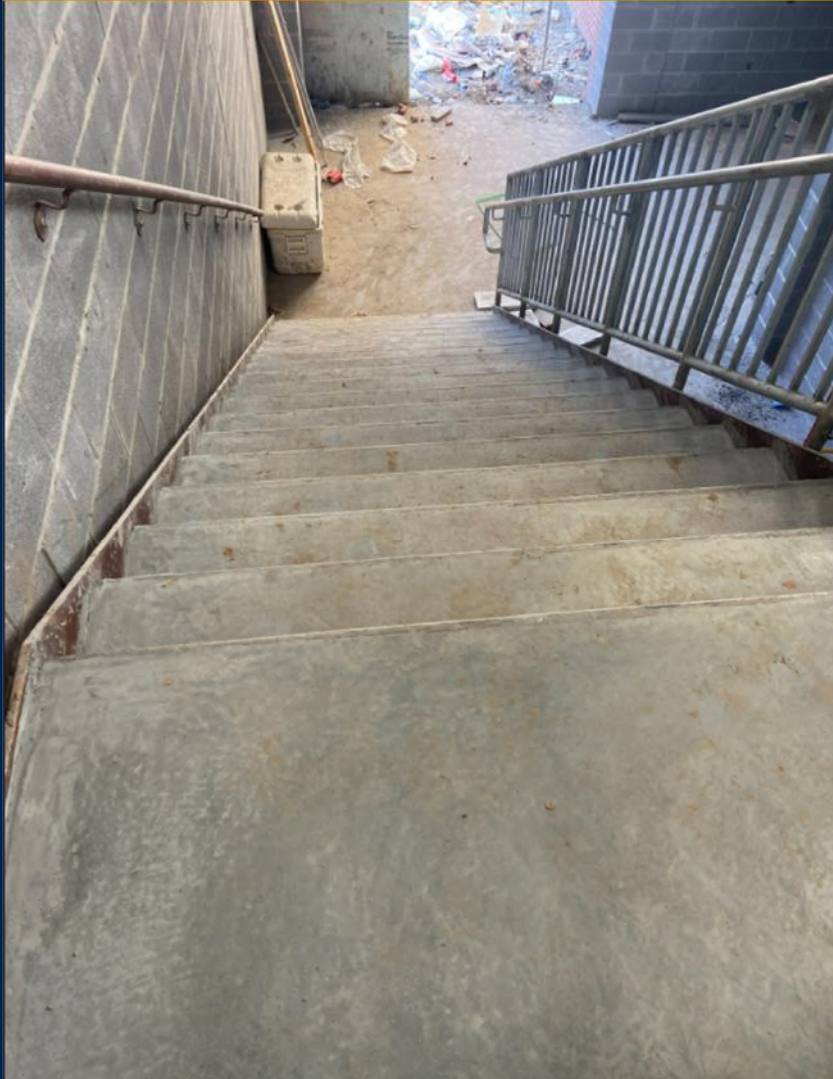

**INTERIOR PAN STAIRS POURED**

# Contact Information



**David Loudermilk**

*Project Director*  
478.256.1839

[dloudermilk@parrishconstruction.com](mailto:dloudermilk@parrishconstruction.com)



**Alex Johnson**

*Project Manager*  
470.540.0047


[ajohnson@parrishconstruction.com](mailto:ajohnson@parrishconstruction.com)



**Art Cofelice**

*Sr. Superintendent*  
770.880.3762

[acofelice@parrishconstruction.com](mailto:acofelice@parrishconstruction.com)

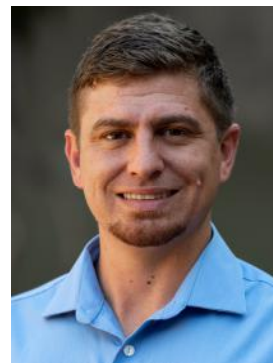

**Zack Cofelice**

*Superintendent*  
470.925.3525

[zcofelice@parrishconstruction.com](mailto:zcofelice@parrishconstruction.com)



**Trey DeRieux**

*Project Engineer*  
470.442.3169

[tderieux@parrishconstruction.com](mailto:tderieux@parrishconstruction.com)



**Drew Plunkett**

*Asst. Superintendent*  
678.215.5193

[dplunkett@parrishconstruction.com](mailto:dplunkett@parrishconstruction.com)

**WE BUILD GREAT** SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .
