

Project Update

St. Pius X Catholic School

December 8, 2023



Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">Catholic Education of North Georgia, Inc.St. Pius X Catholic High School	<ul style="list-style-type: none">CDH Architecture	<ul style="list-style-type: none">David Loudermilk, Project DirectorAlex Johnson, Project ManagerHoyt Clance, SuperintendentTrey DeRieux, Project EngineerDrew Plunkett, Asst. Superintendent



PARRISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	3
OCTOBER 2023	31	3	1
NOVEMBER 2023	30	5	2
DECEMBER 2023	31	8	1
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITEWORK	90%
FOUNDATIONS	85%
UNDERGROUND UTILITIES	100%
SLAB ON GRADE/DECK	100%
STEEL	95%
ELECTRICAL	65%
PLUMBING	65%
MECHANICAL	70%
ROOFING	90%



PARRISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

WEEKLY PROGRESS UPDATE

- MEP OVERHEAD CONTINUED
- BUILDING BRICK CONTINUED
- HANGING SECOND FLOOR SOFFITS
- BLOCKFILL CONTINUED
- LAYING RETAINING WALL BRICK
- SWITCHBACK RAMPS CONTINUED



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	90%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	70%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	65%
PLUMBING	POLK COUNTY PUBLIC SERVICE	65%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	80%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	100%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	95%
EXTERIOR WALLS	PARRISH MASONRY	100%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	100%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	90%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	75%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	70%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

FOUR WEEK LOOK AHEAD

ST. PIUS X CATHOLIC SCHOOL FIELD HOUSE

Project Manager: Alex Johnson

Superintendent: Art Cofelice

4 Week - Near Term Schedule

WEEK OF 12/11 TO 1/5

Work Description	Involved Trades		M	T	W	T	F	SS	SS	M	T	W	T	F	SS	SS	M	T	W	T	F	SS	SS	M	T	W	T	F	SS	SS
		12/11	12/12	12/13	12/14	12/15			12/18	12/19	12/20	12/21	12/22			12/25	12/26	12/27	12/28	12/29			1/1	1/2	1/3	1/4	1/5			
FRAMING & DRYWALL		XXX	XXX	XXX	XXX																									
MEP OVERHEAD		XXX	XXX	XXX	XXX	XXX			XXX	XXX																				
RETAINING WALL BRICK		XXX	XXX	XXX																										
SWITCHBACK RAMPS		XXX	XXX	XXX	XXX	XXX			XXX	XXX	XXX	XXX	XXX												XXX	XXX	XXX	XXX		
WINDOWS/STOREFRONT		XXX	XXX	XXX	XXX	XXX			XXX	XXX	XXX	XXX	XXX												XXX	XXX	XXX	XXX		
CEILING GRID/FRAMING		XXX	XXX	XXX	XXX	XXX			XXX	XXX	XXX	XXX	XXX												XXX	XXX	XXX	XXX		
MEP CEILING/WALL TRIM OUT											XXX	XXX	XXX												XXX	XXX	XXX	XXX		




PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE


WE BUILD GREAT

PROGRESS UPDATE

RETAINING WALL

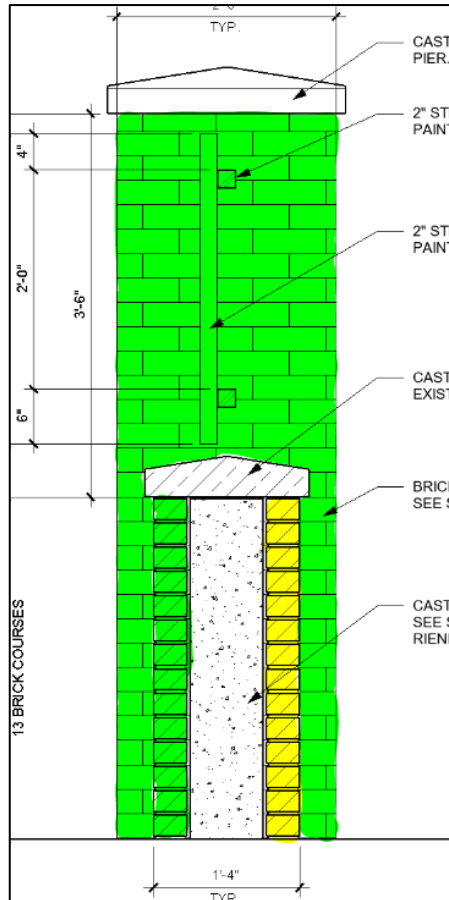

ALUMINUM STOREFRONT

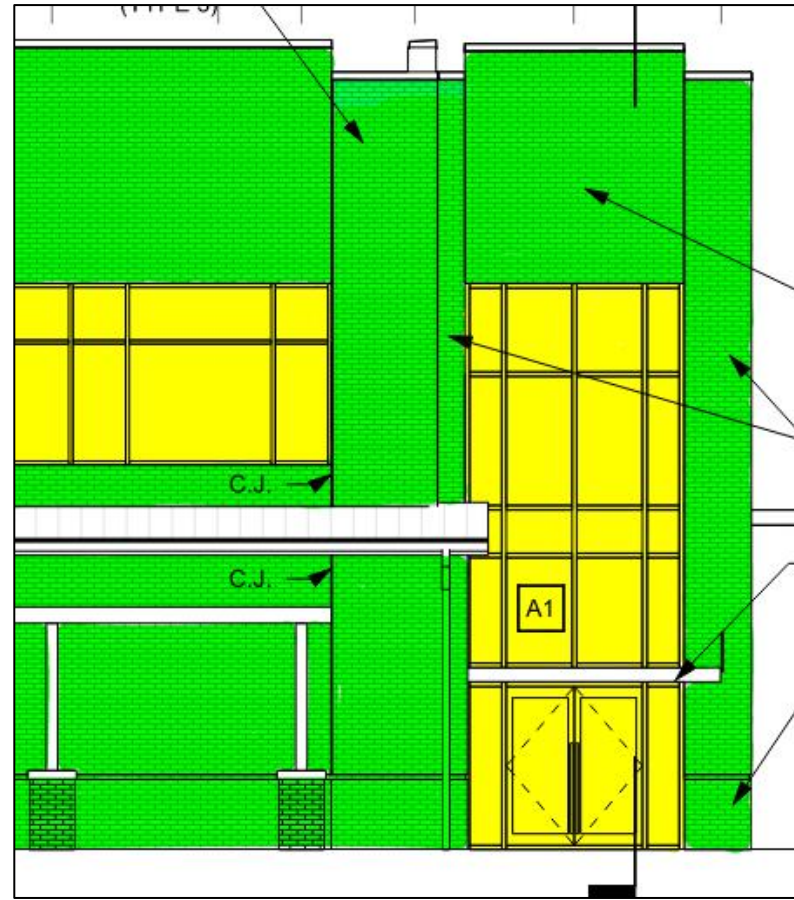

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**RETAINING WALL BRICK
CONTINUED; EXTERIOR
STOREFRONT CONTINUED;
SWITCHBACK RAMP
FOUNDATIONS AND WALLS
CONTINUED**

**EXTERIOR STOREFRONT TO FINISH
NEXT WEEK; INTERIOR
STOREFRONT TO BE IN
PROGRESS; BEGINNING TO START
HANGING CEILING GRID NEXT
WEEK**



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



SWITCHBACK RAMP FOOTERS



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

BRICK AT RETAINING WALL





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

SWITCHBACK RAMP WALLS FORMED UP





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



ROOF TOP UNIT SET

Contact Information



David Loudermilk

Project Director

478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager

470.540.0047

ajohnson@parrishconstruction.com



Art Cofelice

Sr. Superintendent

770.880.3762

acofelice@parrishconstruction.com



Zack Cofelice

Superintendent

470.925.3525

zcofelice@parrishconstruction.com



Trey DeRieux

Project Engineer

470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent

678.215.5193

dplunkett@parrishconstruction.com
