

Project Update

St. Pius X Catholic School

August 11, 2023



Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">• Catholic Education of North Georgia, Inc.• St. Pius X Catholic High School	<ul style="list-style-type: none">• CDH Architecture	<ul style="list-style-type: none">• David Loudermilk, Project Director• Alex Johnson, Project Manager• Hoyt Clance, Superintendent• Trey DeRieux, Project Engineer• Drew Plunkett, Asst. Superintendent



PARISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	2
AUGUST 2023	31	3	1
SEPTEMBER 2023	30	2	-
OCTOBER 2023	31	3	-
NOVEMBER 2023	30	5	-
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITEWORK	60%
FOUNDATIONS	70%
UNDERGROUND UTILITIES	75%
SLAB ON GRADE/DECK	50%
STEEL	0%
ELECTRICAL	0%
PLUMBING	0%
MECHANICAL	0%
ROOFING	0%



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT _____.

WEEKLY PROGRESS UPDATE

- SEWER LINE BORING CONTINUED THIS WEEK
- SITE GRADING CONTINUED
- WORKED ON UPSIZING THE EXISTING SANITARY LINE TOWARDS PLASTER ROAD



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	75%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	0%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	10%
PLUMBING	POLK COUNTY PUBLIC SERVICE	10%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	0%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	50%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	0%
EXTERIOR WALLS	PARRISH MASONRY	0%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	0%



PARISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	0%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%



WE BUILD GREAT

[illegible]





PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT


PROGRESS UPDATE

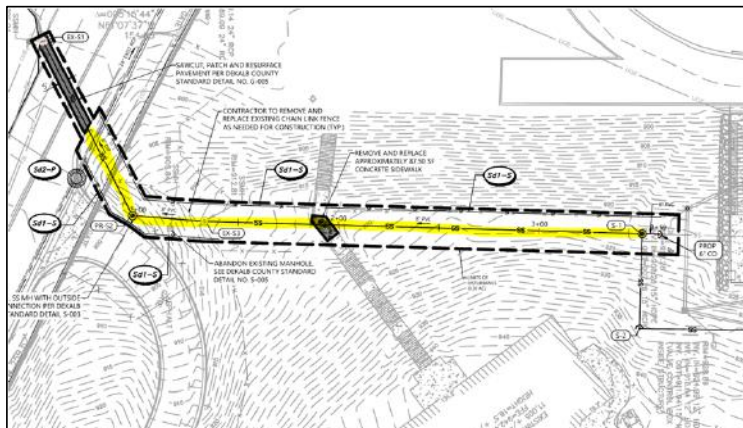

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**BORING CONTINUED THIS WEEK;
SLAB WAS CURING; WORKED ON
UPSIZING THE EXISTING
SANITARY LINE**

**STEEL TO BE DELIVERED NEXT
WEEK AND TO START ERECTING**

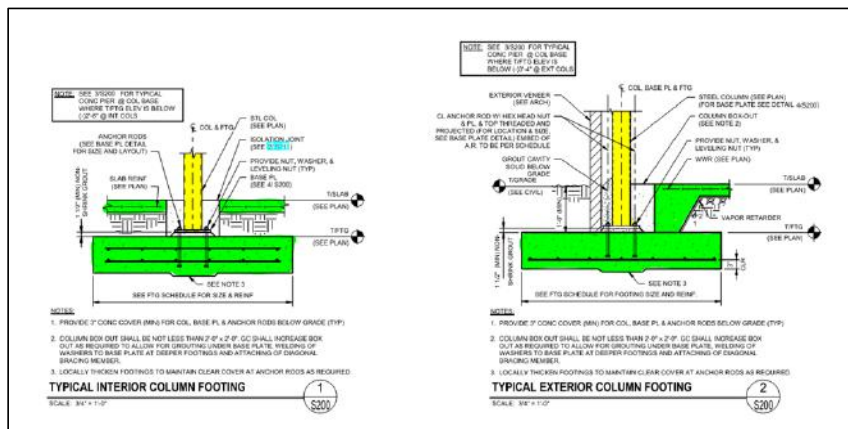



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



PICTURE OF THE SLAB THIS WEEK



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



**WORKING ON UPSIZING THE EXISTING
SANITARY LINE**




PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

**WORKING ON UPSIZING THE EXISTING
SANITARY LINE**

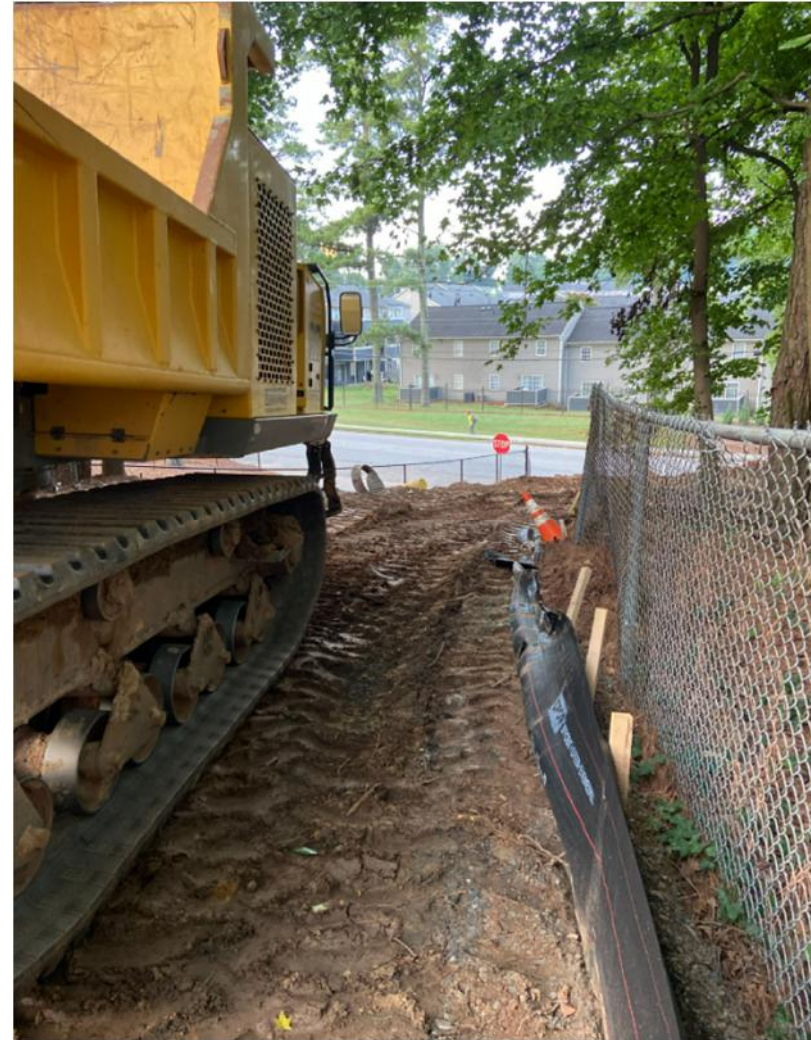



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

OVERALL SITE PHOTO



Contact Information



David Loudermilk

Project Director

478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager

470.540.0047

ajohnson@parrishconstruction.com



Hoyt Clance

Superintendent

478.244.6349

hclance@parrishconstruction.com



Trey DeRieux

Project Engineer

470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent

678.215.5193

dplunkett@parrishconstruction.com
