

# Project Update

## St. Pius X Catholic School

May 26, 2023



# Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH  
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

## ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



| Owner   | Architect/Engineer   | Parrish Construction Group  |
|---|--|---|
| <ul style="list-style-type: none"><li>Catholic Education of North Georgia, Inc.</li><li>St. Pius X Catholic High School</li></ul> | <ul style="list-style-type: none"><li>CDH Architecture</li></ul> | <ul style="list-style-type: none"><li>David Loudermilk, Project Director</li><li>Alex Johnson, Project Manager</li><li>Hoyt Clance, Superintendent</li><li>Trey DeRieux, Project Engineer</li><li>Drew Plunkett, Asst. Superintendent</li></ul> |



PARISH  
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

## SUMMARY REPORT

| Month          | Calendar Days | Planned Weather Days | Claimed Weather Days |
|----------------|---------------|----------------------|----------------------|
| MARCH 2023     | 31            | 6                    | 3                    |
| APRIL 2023     | 30            | 4                    | 4                    |
| MAY 2023       | 31            | 2                    | 1                    |
| JUNE 2023      | 30            | 3                    | -                    |
| JULY 2023      | 31            | 4                    | -                    |
| AUGUST 2023    | 31            | 3                    | -                    |
| SEPTEMBER 2023 | 30            | 2                    | -                    |
| OCTOBER 2023   | 31            | 3                    | -                    |
| NOVEMBER 2023  | 30            | 5                    | -                    |
| DECEMBER 2023  | 31            | 8                    | -                    |
| JANUARY 2024   | 31            | 11                   | -                    |
| FEBRUARY 2024  | 29            | 8                    | -                    |
| MARCH 2024     | 31            | 6                    | -                    |
|                |               |                      |                      |
|                |               |                      |                      |
|                |               |                      |                      |
|                |               |                      |                      |
|                |               |                      |                      |
|                |               |                      |                      |
|                |               |                      |                      |

| Critical Tasks        | % Complete |
|-----------------------|------------|
| SITEWORK              | 30%        |
| FOUNDATIONS           | 0%         |
| UNDERGROUND UTILITIES | 30%        |
| SLAB ON GRADE/DECK    | 0%         |
| STEEL                 | 0%         |
| ELECTRICAL            | 0%         |
| PLUMBING              | 0%         |
| MECHANICAL            | 0%         |
| ROOFING               | 0%         |
|                       |            |





PARISH  
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

## WEEKLY PROGRESS UPDATE

- CONTINUED INSTALLATION OF WATER AND FIRE LINE
- POURED THE RETAINING WALL FOOTINGS
- WORKED ON STRUCTURE S-1 AND S-2 FOR THE SEWER BORING
- BUILDING PAD GRADING



PARRISH  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## SUBCONTRACTOR PROGRESS

| Scope of Work                      | Subcontractor                    | Percent Complete |
|------------------------------------|----------------------------------|------------------|
| Site Work                          |                                  |                  |
| GRADING AND UTILITIES              | RUBY-COLLINS                     | 30%              |
| UNDERGROUND GAS LINE               | POLK COUNTY PUBLIC SERVICE       | 0%               |
|                                    |                                  |                  |
|                                    |                                  |                  |
| Building Systems                   |                                  |                  |
| MECHANICAL                         | GEORGIA MECHANICAL               | 0%               |
| ELECTRICAL                         | ALL STATE ELECTRICAL CONTRACTORS | 0%               |
| PLUMBING                           | POLK COUNTY PUBLIC SERVICE       | 0%               |
| FIRE PROTECTION                    | GAINESVILLE FIRE PROTECTION      | 0%               |
|                                    |                                  |                  |
| Building Structure                 |                                  |                  |
| FOUNDATION AND SLAB ON GRADE (SOG) | PARRISH CONCRETE                 | 0%               |
| STRUCTURAL STEEL FRAMING           | TRINITY FABRICATORS              | 0%               |
| EXTERIOR WALLS                     | PARRISH MASONRY                  | 0%               |
| INTERIOR WALLS                     | PARRISH MASONRY/HOLT & HOLT      | 0%               |



**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

# SUBCONTRACTOR PROGRESS

| Scope of Work      | Subcontractor              | Percent Complete |
|--------------------|----------------------------|------------------|
| Building Envelope  |                            |                  |
| BRICK              | PARRISH MASONRY            | 0%               |
| WINDOWS/STOREFRONT | COMMERCIAL GLASS & MIRRORS | 0%               |
|                    |                            |                  |
| Building Interiors |                            |                  |
| FLOORING           | PERIMETER FLOORS           | 0%               |
| DRYWALL            | HOLT & HOLT                | 0%               |
| CEILINGS           | HOLT & HOLT                | 0%               |
| PAINTING           | MCs PAINTING               | 0%               |
|                    |                            |                  |
|                    |                            |                  |
|                    |                            |                  |
|                    |                            |                  |
|                    |                            |                  |
|                    |                            |                  |



**WE BUILD GREAT**

## WEEK OF 5/29 TO 6/25

[illegible]






PARRISH  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## PROGRESS UPDATE

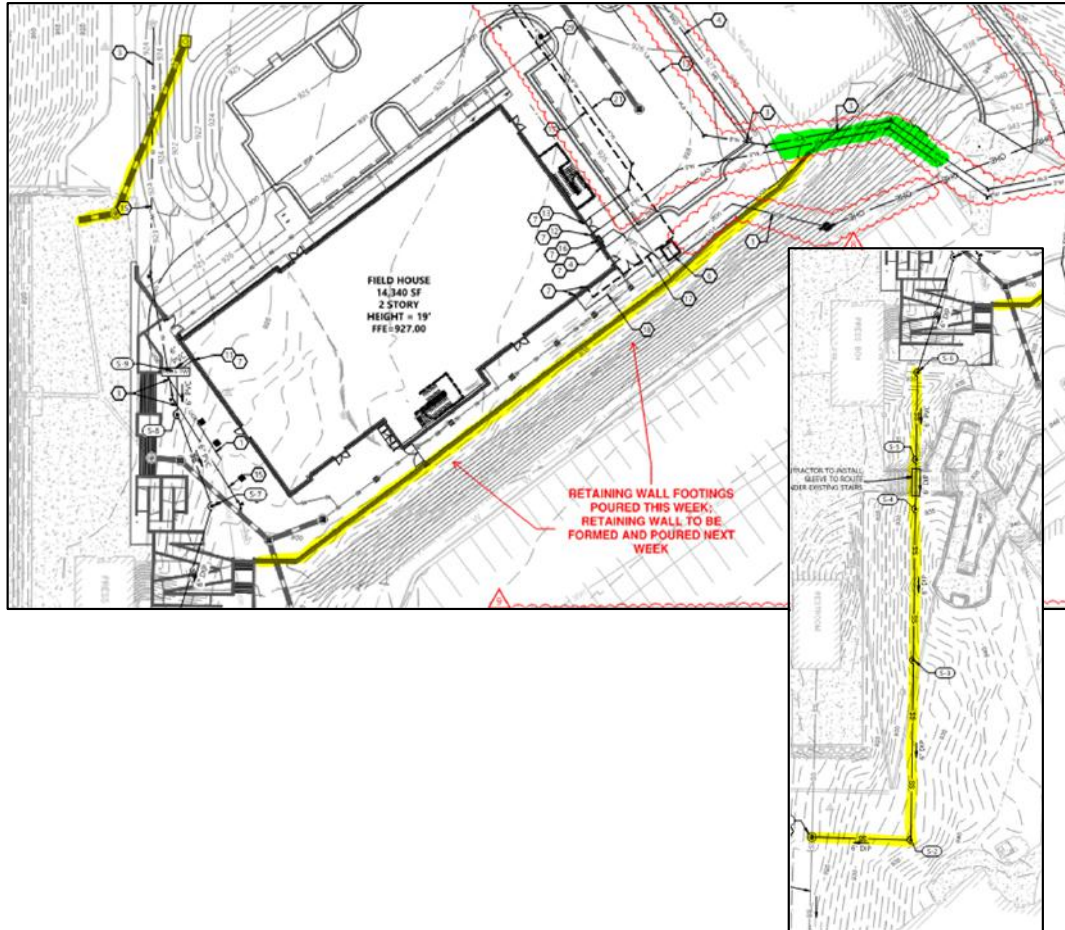

**BROUGHT THE WATER AND FIRE  
LINE TO THE PARKING LOT THIS  
WEEK**

**RETAINING WALL FOOTINGS  
POURED THIS WEEK**

**RETAINING WALL FORM AND  
POUR, SEWER BORING, AND  
STORM LINE 'O' TO BE IN  
PROGRESS NEXT WEEK**



PARRISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS



**WORKING ON SANITARY SEWER  
STRUCTURES**





PARRISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS

### GRADING THE BUILDING PAD





**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS



**RETAINING WALL FOOTING READY TO BE  
POURED**





PARRISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS

### POURING THE RETAINING WALL FOOTING



# Contact Information



**David Loudermilk**

*Project Director*

478.256.1839

[dloudermilk@parrishconstruction.com](mailto:dloudermilk@parrishconstruction.com)



**Alex Johnson**

*Project Manager*

470.540.0047

[ajohnson@parrishconstruction.com](mailto:ajohnson@parrishconstruction.com)



**Hoyt Clance**

*Superintendent*

478.244.6349

[hclance@parrishconstruction.com](mailto:hclance@parrishconstruction.com)



**Trey DeRieux**

*Project Engineer*

470.442.3169

[tderieux@parrishconstruction.com](mailto:tderieux@parrishconstruction.com)



**Drew Plunkett**

*Asst. Superintendent*

678.215.5193

[dplunkett@parrishconstruction.com](mailto:dplunkett@parrishconstruction.com)
