

Project Update

St. Pius X Catholic School

August 18, 2023



Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



| Owner | Architect/Engineer | Parrish Construction Group |
|---|--|---|
| <ul style="list-style-type: none">Catholic Education of North Georgia, Inc.St. Pius X Catholic High School | <ul style="list-style-type: none">CDH Architecture | <ul style="list-style-type: none">David Loudermilk, Project DirectorAlex Johnson, Project ManagerHoyt Clance, SuperintendentTrey DeRieux, Project EngineerDrew Plunkett, Asst. Superintendent |



PARISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

| Month | Calendar Days | Planned Weather Days | Claimed Weather Days |
|----------------|---------------|----------------------|----------------------|
| MARCH 2023 | 31 | 6 | 3 |
| APRIL 2023 | 30 | 4 | 4 |
| MAY 2023 | 31 | 2 | 1 |
| JUNE 2023 | 30 | 3 | 2 |
| JULY 2023 | 31 | 4 | 2 |
| AUGUST 2023 | 31 | 3 | 1 |
| SEPTEMBER 2023 | 30 | 2 | - |
| OCTOBER 2023 | 31 | 3 | - |
| NOVEMBER 2023 | 30 | 5 | - |
| DECEMBER 2023 | 31 | 8 | - |
| JANUARY 2024 | 31 | 11 | - |
| FEBRUARY 2024 | 29 | 8 | - |
| MARCH 2024 | 31 | 6 | - |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |

| Critical Tasks | % Complete |
|-----------------------|------------|
| SITEWORK | 60% |
| FOUNDATIONS | 70% |
| UNDERGROUND UTILITIES | 80% |
| SLAB ON GRADE/DECK | 50% |
| STEEL | 55% |
| ELECTRICAL | 0% |
| PLUMBING | 0% |
| MECHANICAL | 0% |
| ROOFING | 0% |
| | |



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT _____.

WEEKLY PROGRESS UPDATE

- SEWER LINE BORING CONTINUED
- WORKED ON UPSIZING THE EXISTING SANITARY LINE TO PLASTER ROAD
- STEEL DELIVERED
- BEGAN ERECTING STEEL THIS WEEK



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

| Scope of Work | Subcontractor | Percent Complete |
|---|----------------------------------|------------------|
| Site Work | | |
| GRADING AND UTILITIES | RUBY-COLLINS | 80% |
| UNDERGROUND GAS LINE | POLK COUNTY PUBLIC SERVICE | 100% |
| | | |
| | | |
| Building Systems | | |
| MECHANICAL | GEORGIA MECHANICAL | 0% |
| ELECTRICAL | ALL STATE ELECTRICAL CONTRACTORS | 10% |
| PLUMBING | POLK COUNTY PUBLIC SERVICE | 10% |
| FIRE PROTECTION | GAINESVILLE FIRE PROTECTION | 0% |
| | | |
| Building Structure | | |
| FOUNDATION AND SLAB ON GRADE (SOG)/DECK | PARRISH CONCRETE | 50% |
| STRUCTURAL STEEL FRAMING | TRINITY FABRICATORS | 55% |
| EXTERIOR WALLS | PARRISH MASONRY | 0% |
| INTERIOR WALLS | PARRISH MASONRY/HOLT & HOLT | 0% |



PARISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

| Scope of Work | Subcontractor | Percent Complete |
|--------------------|----------------------------|------------------|
| Building Envelope | | |
| BRICK | PARRISH MASONRY | 0% |
| WINDOWS/STOREFRONT | COMMERCIAL GLASS & MIRRORS | 0% |
| | | |
| Building Interiors | | |
| FLOORING | PERIMETER FLOORS | 0% |
| DRYWALL | HOLT & HOLT | 0% |
| CEILINGS | HOLT & HOLT | 0% |
| PAINTING | MCs PAINTING | 0% |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |



PROJECT UPDATE

WE BUILD GREAT

[illegible]



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE


WE BUILD GREAT

PROGRESS UPDATE



**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**BORING CONTINUED THIS WEEK;
CONTINUED UPSIZING THE
EXISTING SANITARY LINE; BEGAN
ERECTING THE STEEL**

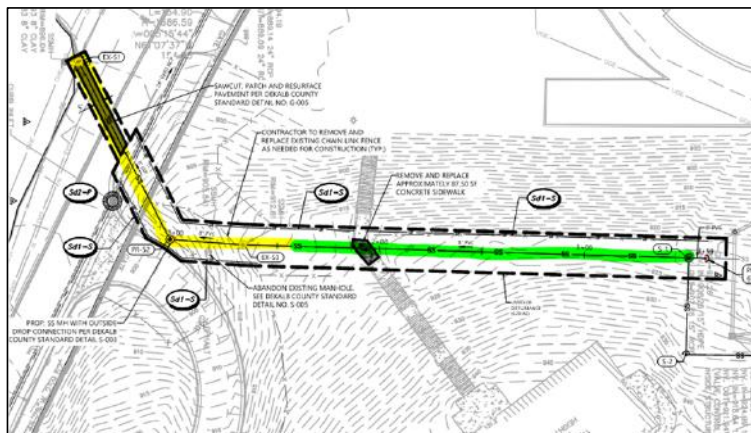

**CONTINUING STEEL ERECTING;
CONTINUING UPSIZING SANITARY
LINE; CONTINUING SANITARY
BORE**



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



STEEL BEING DELIVERED



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

ERECTING STEEL






PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

ERECTING STEEL

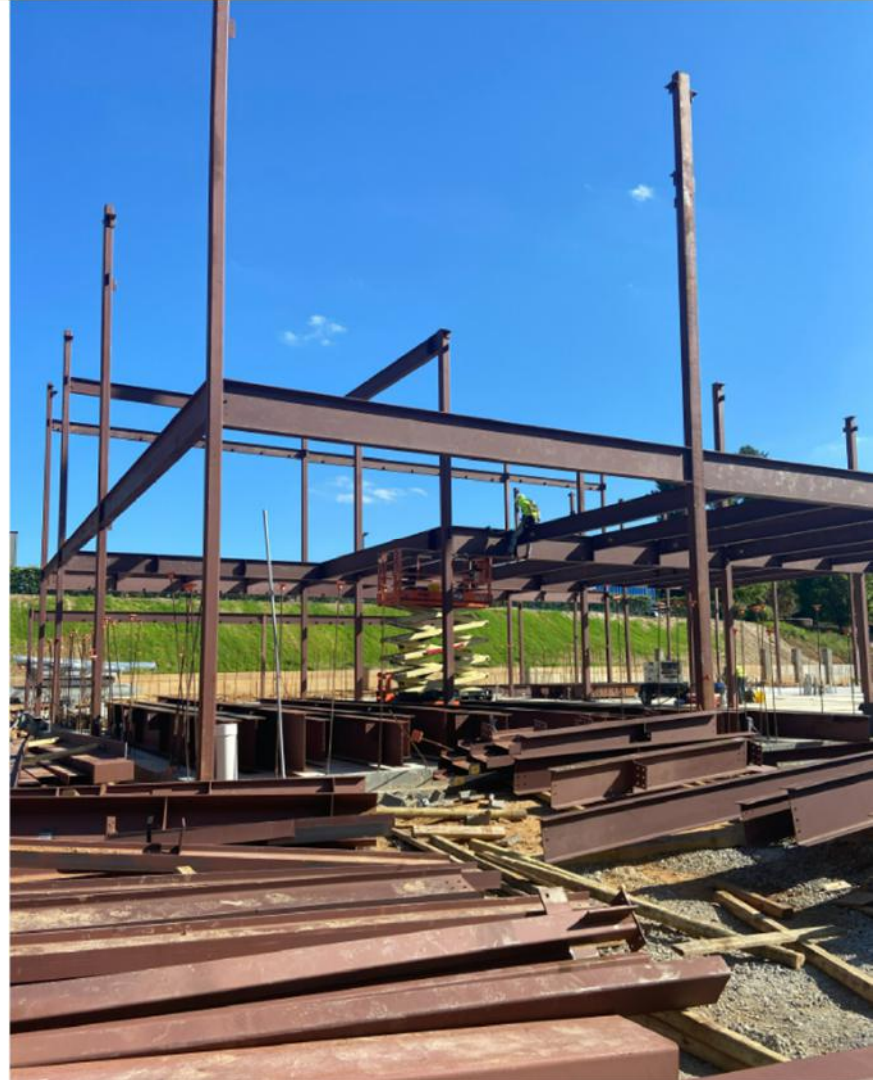



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



Contact Information



David Loudermilk

Project Director

478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager

470.540.0047

ajohnson@parrishconstruction.com



Hoyt Clance

Superintendent

478.244.6349

hclance@parrishconstruction.com



Trey DeRieux

Project Engineer

470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent

678.215.5193

dplunkett@parrishconstruction.com

WE BUILD GREAT

SCHOOLS

INDUSTRIAL FACILITIES

HEALTHCARE FACILITIES

COMMUNITIES

LEADERS

FUTURES .
