

Project Update

St. Pius X Catholic School

June 30, 2023



Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">Catholic Education of North Georgia, Inc.St. Pius X Catholic High School	<ul style="list-style-type: none">CDH Architecture	<ul style="list-style-type: none">David Loudermilk, Project DirectorAlex Johnson, Project ManagerHoyt Clance, SuperintendentTrey DeRieux, Project EngineerDrew Plunkett, Asst. Superintendent



PARISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	-
AUGUST 2023	31	3	-
SEPTEMBER 2023	30	2	-
OCTOBER 2023	31	3	-
NOVEMBER 2023	30	5	-
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITEWORK	45%
FOUNDATIONS	40%
UNDERGROUND UTILITIES	65%
SLAB ON GRADE/DECK	0%
STEEL	0%
ELECTRICAL	0%
PLUMBING	0%
MECHANICAL	0%
ROOFING	0%



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT _____.

WEEKLY PROGRESS UPDATE

- SEWER LINE BORING CONTINUED THIS WEEK
- POURED THE REMAINING FOOTINGS FOR THE BUILDING PAD
- REMAINING CURB FOR THE PARKING LOT POURED



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	50%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	0%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	0%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	0%
PLUMBING	POLK COUNTY PUBLIC SERVICE	0%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	0%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)	PARRISH CONCRETE	30%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	0%
EXTERIOR WALLS	PARRISH MASONRY	0%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	0%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	0%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%



WE BUILD GREAT

ST. PIUS X CATHOLIC SCHOOL FIELD HOUSE

Superintendent: Hoyt Clance/Drew Plunkett

WEEK OF 7/3 TO 7/30

[illegible]




PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE


WE BUILD GREAT

PROGRESS UPDATE

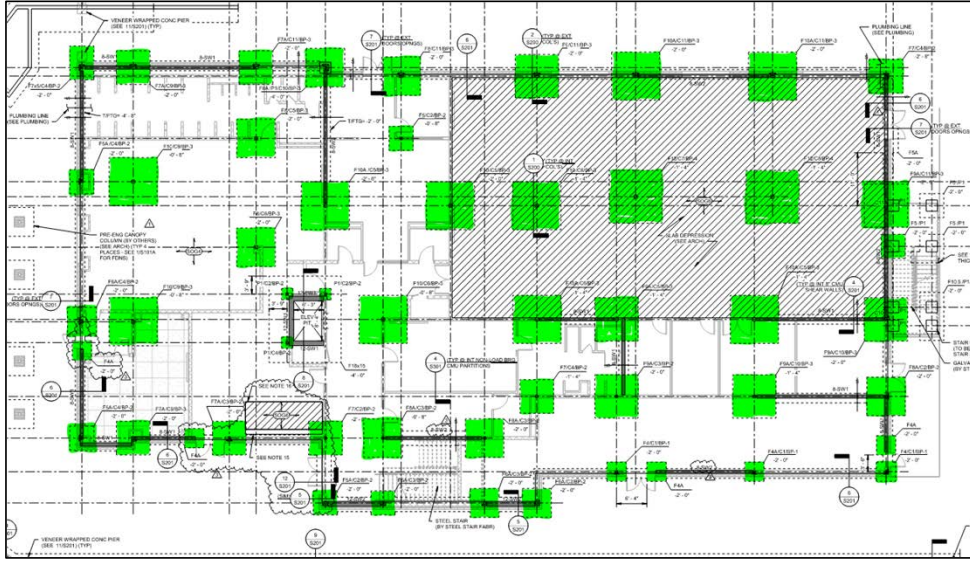

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED**

**REMAINING SPREAD FOOTINGS
POURED THIS WEEK; THE REST OF
THE PARKING LOT CURB AND
GUTTER POURED THIS WEEK;
BORING CONTINUED THIS WEEK**

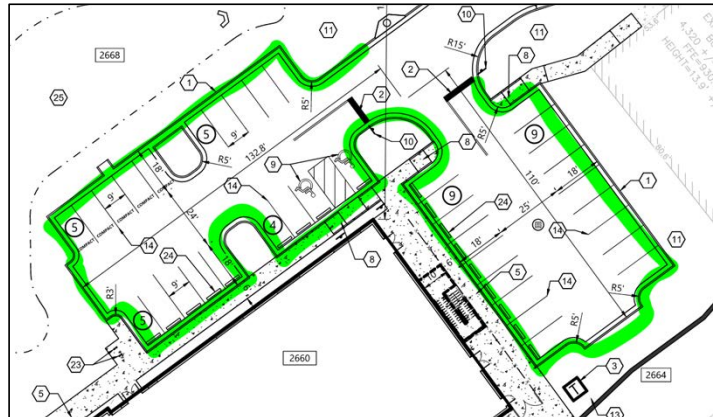

**SEWER LINE BORING TO
CONTINUE NEXT WEEK**

**FOUNDATION BLOCK TO BE LAYED
NEXT WEEK AND SLAB PLUMBING
TO BEGIN**



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



**PARKING LOT CURB FORMED AND READY
TO BE POURED**



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



PARKING LOT CURB POURED



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS

ELEVATOR PIT POURED





PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS

SITE PHOTO



Contact Information



David Loudermilk

Project Director

478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager

470.540.0047

ajohnson@parrishconstruction.com



Hoyt Clance

Superintendent

478.244.6349

hclance@parrishconstruction.com




Trey DeRieux

Project Engineer

470.442.3169

tderieux@parrishconstruction.com

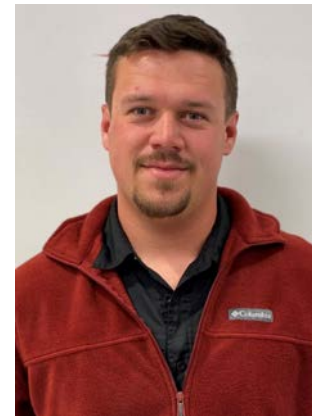

Drew Plunkett

Asst. Superintendent

678.215.5193

dplunkett@parrishconstruction.com
