

# Project Update

## St. Pius X Catholic School

July 28, 2023



# Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH  
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

## ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none"><li>Catholic Education of North Georgia, Inc.</li><li>St. Pius X Catholic High School</li></ul>	<ul style="list-style-type: none"><li>CDH Architecture</li></ul>	<ul style="list-style-type: none"><li>David Loudermilk, Project Director</li><li>Alex Johnson, Project Manager</li><li>Hoyt Clance, Superintendent</li><li>Trey DeRieux, Project Engineer</li><li>Drew Plunkett, Asst. Superintendent</li></ul>



PARISH  
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

## SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	2
AUGUST 2023	31	3	-
SEPTEMBER 2023	30	2	-
OCTOBER 2023	31	3	-
NOVEMBER 2023	30	5	-
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITEWORK	45%
FOUNDATIONS	65%
UNDERGROUND UTILITIES	70%
SLAB ON GRADE/DECK	20%
STEEL	0%
ELECTRICAL	0%
PLUMBING	0%
MECHANICAL	0%
ROOFING	0%



PARISH  
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

## WEEKLY PROGRESS UPDATE

- SEWER LINE BORING CONTINUED THIS WEEK
- SLAB ON GRADE PLUMBING AND ELECTRICAL FINISHED THIS WEEK
- PAVED THE PARKING LOT FOR THE WATER AND FIRE LINE
- PREPPED THE SLAB WITH VAPOR BARRIER, WIRE MESH, AND REBAR



PARRISH  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	55%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	50%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	0%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	10%
PLUMBING	POLK COUNTY PUBLIC SERVICE	10%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	0%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)	PARRISH CONCRETE	50%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	0%
EXTERIOR WALLS	PARRISH MASONRY	0%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	0%





**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

# SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	0%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%



**WE BUILD GREAT**

## ST. PIUS X CATHOLIC SCHOOL FIELD HOUSE

Superintendent: Hoyt Clance/Drew Plunkett

#### 4 Week - Near Term Schedule

WEEK OF 7/31 TO 8/27

[illegible]






PARRISH  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

## PROGRESS UPDATE

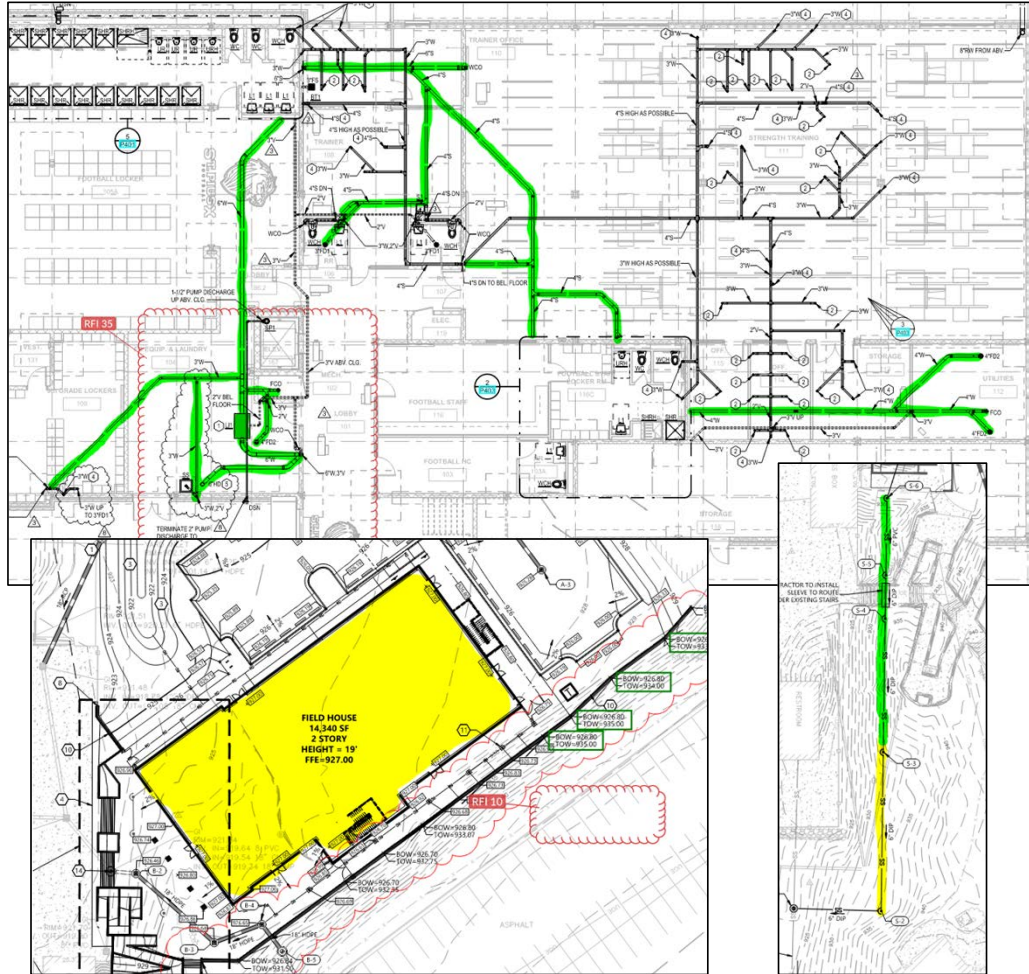

**GREEN HIGHLIGHTED SECTIONS  
HAVE BEEN COMPLETED; YELLOW  
HIGHLIGHTED IN PROGRESS**

**BORING CONTINUED THIS WEEK;  
SOG PLUMBING AND ELECTRICAL  
FINISHED THIS WEEK; SLAB HAS  
BEEN PREPPED FOR POUR**

**SLAB TO BE POURED NEXT WEEK**



PARISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS



**SLAB PLUMBING AND ELECTRICAL  
FINISHED UP THIS WEEK**





PARISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS



**ASPHALT PAVING THROUGH THE PARKING  
LOT**



PARISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS

**SLAB PREPPED TO BE POURED NEXT WEEK**





PARRISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS

### OVERALL SITE PICTURE





# Contact Information



**David Loudermilk**

*Project Director*

478.256.1839

[dloudermilk@parrishconstruction.com](mailto:dloudermilk@parrishconstruction.com)



**Alex Johnson**

*Project Manager*

470.540.0047

[ajohnson@parrishconstruction.com](mailto:ajohnson@parrishconstruction.com)



**Hoyt Clance**

*Superintendent*

478.244.6349

[hclance@parrishconstruction.com](mailto:hclance@parrishconstruction.com)



**Trey DeRieux**

*Project Engineer*

470.442.3169

[tderieux@parrishconstruction.com](mailto:tderieux@parrishconstruction.com)



**Drew Plunkett**

*Asst. Superintendent*

678.215.5193

[dplunkett@parrishconstruction.com](mailto:dplunkett@parrishconstruction.com)
