

# Project Update

## St. Pius X Catholic School

September 8, 2023



# Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information

# ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



PARRISH  
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none"><li>• Catholic Education of North Georgia, Inc.</li><li>• St. Pius X Catholic High School</li></ul>	<ul style="list-style-type: none"><li>• CDH Architecture</li></ul>	<ul style="list-style-type: none"><li>• David Loudermilk, Project Director</li><li>• Alex Johnson, Project Manager</li><li>• Hoyt Clance, Superintendent</li><li>• Trey DeRieux, Project Engineer</li><li>• Drew Plunkett, Asst. Superintendent</li></ul>



# SUMMARY REPORT

**PARRISH**  
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	-
OCTOBER 2023	31	3	-
NOVEMBER 2023	30	5	-
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITWORK	70%
FOUNDATIONS	70%
UNDERGROUND UTILITIES	85%
SLAB ON GRADE/DECK	50%
STEEL	75%
ELECTRICAL	0%
PLUMBING	0%
MECHANICAL	0%
ROOFING	0%



**PARRISH**  
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

- SEWER LINE BORING CONTINUED
- PATCHED ASPHALT AT PLASTER ROAD FROM SEWER LINE UPSIZING
- Poured ISOLATION JOINTS
- CONTINUED STEEL WORK
- INSTALLED HVAC HANGERS ON FIRST FLOOR



**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

# SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
<b>Site Work</b>		
GRADING AND UTILITIES	RUBY-COLLINS	80%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
<b>Building Systems</b>		
MECHANICAL	GEORGIA MECHANICAL	5%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	10%
PLUMBING	POLK COUNTY PUBLIC SERVICE	10%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	0%
<b>Building Structure</b>		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	50%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	75%
EXTERIOR WALLS	PARRISH MASONRY	0%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	0%



**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

# SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	0%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%










**PARRISH**  
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

# PROGRESS UPDATE

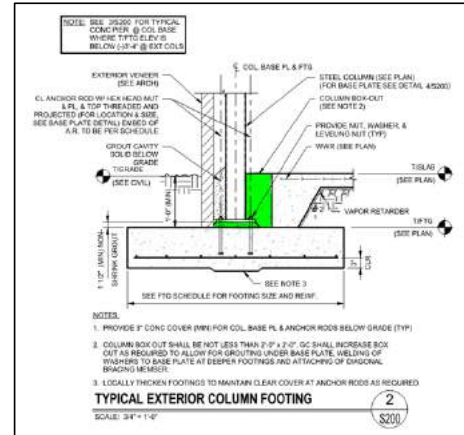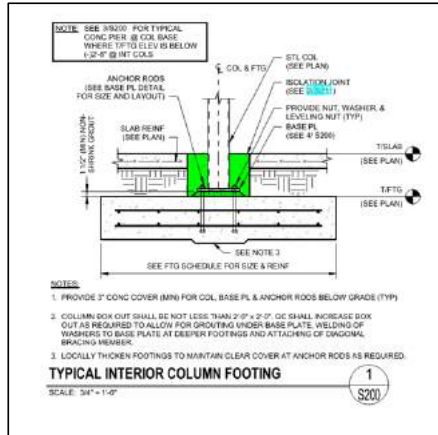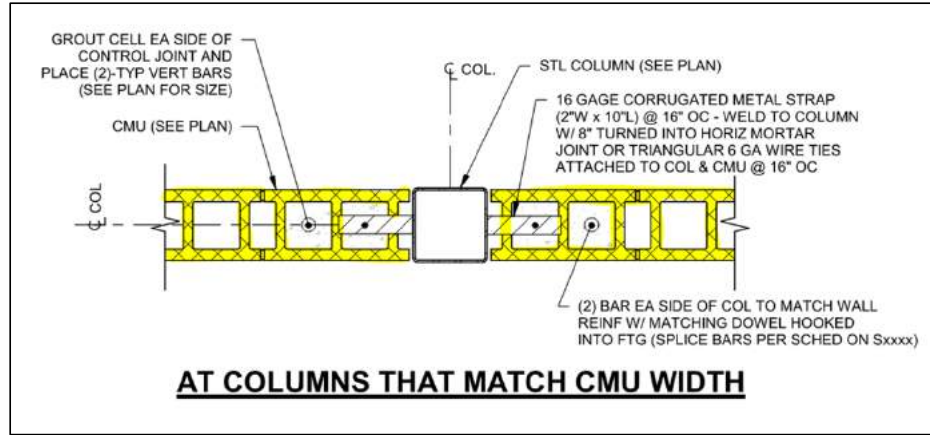

**GREEN HIGHLIGHTED SECTIONS  
HAVE BEEN COMPLETED THIS  
WEEK; YELLOW HIGHLIGHTED IN  
PROGRESS NEXT WEEK**

**BORING CONTINUED THIS WEEK;  
ISOLATION JOINTS WERE  
POURED; STEEL WORK  
CONTINUED; PATCHED ASPHALT  
AT PLASTER ROAD**

**CONTINUING STEEL WORK; CMU  
BLOCK TO START; CONTINUING  
SANITARY BORE; AND SOD POUR  
NEXT WEEK**



PARRISH  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS



**1<sup>ST</sup> FLOOR DECK INSTALLED**



**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_ .

## PROJECT PHOTOS

**ROOF DECK INSTALLED**





**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

## PROJECT PHOTOS

**ISOLATION JOINT POURED**





**PARRISH**  
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT \_\_\_\_\_.

## PROJECT PHOTOS



**OVERALL SITE PHOTO**

# Contact Information



**David Loudermilk**

*Project Director*  
478.256.1839

[dloudermilk@parrishconstruction.com](mailto:dloudermilk@parrishconstruction.com)



**Alex Johnson**

*Project Manager*  
470.540.0047

[ajohnson@parrishconstruction.com](mailto:ajohnson@parrishconstruction.com)



**Hoyt Clance**

*Superintendent*  
478.244.6349

[hclance@parrishconstruction.com](mailto:hclance@parrishconstruction.com)



**Trey DeRieux**

*Project Engineer*  
470.442.3169

[tderieux@parrishconstruction.com](mailto:tderieux@parrishconstruction.com)



**Drew Plunkett**

*Asst. Superintendent*  
678.215.5193

[dplunkett@parrishconstruction.com](mailto:dplunkett@parrishconstruction.com)
