

Project Update

St. Pius X Catholic School

November 3, 2023



WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .

Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">Catholic Education of North Georgia, Inc.St. Pius X Catholic High School	<ul style="list-style-type: none">CDH Architecture	<ul style="list-style-type: none">David Loudermilk, Project DirectorAlex Johnson, Project ManagerHoyt Clance, SuperintendentTrey DeRieux, Project EngineerDrew Plunkett, Asst. Superintendent



PARRISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	3
OCTOBER 2023	31	3	1
NOVEMBER 2023	30	5	-
DECEMBER 2023	31	8	-
JANUARY 2024	31	11	-
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITWORK	80%
FOUNDATIONS	75%
UNDERGROUND UTILITIES	95%
SLAB ON GRADE/DECK	100%
STEEL	95%
ELECTRICAL	40%
PLUMBING	50%
MECHANICAL	40%
ROOFING	95%



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT

WEEKLY PROGRESS UPDATE

- INTERIOR CMU AND METAL FRAMING CONTINUED
- MEP OVERHEAD CONTINUED
 - 1st FLOOR PLUMBING AND ELECTRICAL COMPLETED
- STARTED LAYING BRICK
- STARTED BLOCKFILL ON 1ST FLOOR
- SWITCHBACK RAMP TO START FOUNDATIONS THIS COMING WEEK



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	85%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	40%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	40%
PLUMBING	POLK COUNTY PUBLIC SERVICE	50%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	70%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	100%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	95%
EXTERIOR WALLS	PARRISH MASONRY	100%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	85%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	15%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	0%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	0%
CEILINGS	HOLT & HOLT	0%
PAINTING	MCs PAINTING	0%





PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

PROGRESS UPDATE

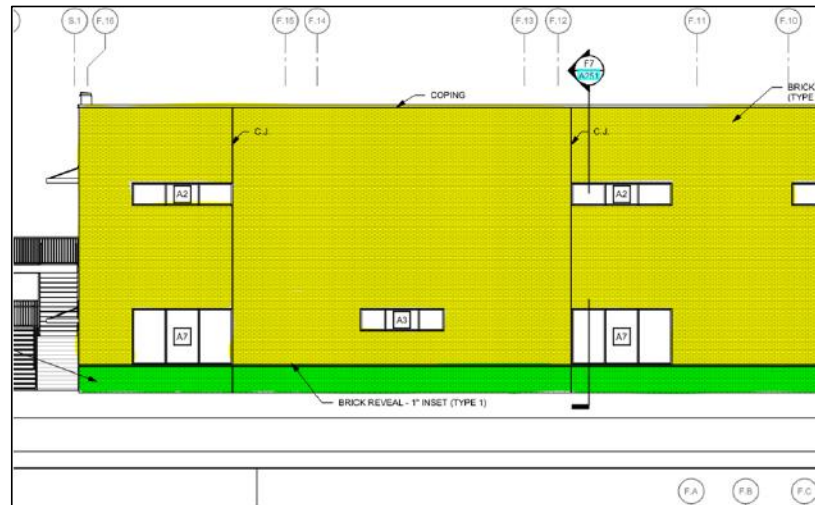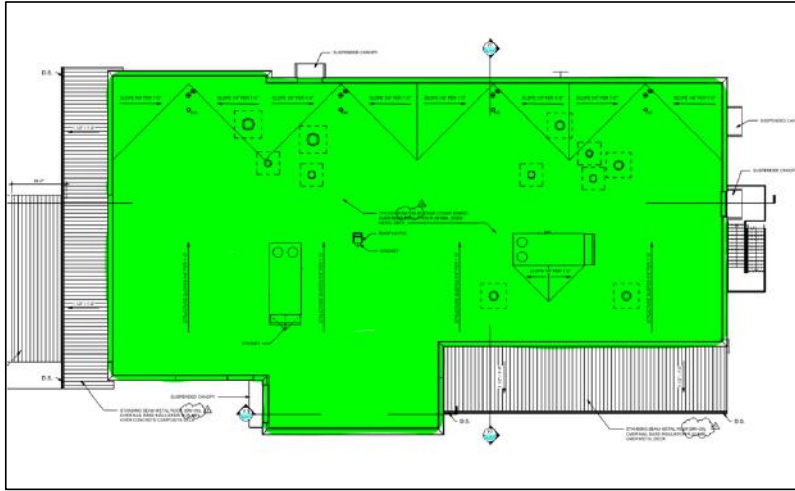

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**INTERIOR CMU AND FRAMING
CONTINUED THIS WEEK; MEP
OVERHEAD CONTINUED;
ROOFING HAS BEEN COMPLETED;
STARTED LAYING EXTERIOR BRICK**

**BRICK CONTINUED NEXT WEEK;
MEP OVERHEAD TO CONTINUE;
SWITCHBACK RAMPS TO START
NEXT WEEK**



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



**MEP OVERHEAD AND BLOCKFILL IN THE
WEIGHT ROOM**



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

**FRAMING INTERIOR WALLS ON THE 2ND
FLOOR**





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS

**WATERPROOFING EXTERIOR CMU
GETTING READY TO START THE BRICK**





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS



BEGINNING TO LAY BRICK

Contact Information



David Loudermilk

Project Director
478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager
470.540.0047

ajohnson@parrishconstruction.com



Art Cofelice

Sr. Superintendent
770.880.3762

acofelice@parrishconstruction.com



Zack Cofelice

Superintendent
470.925.3525

zcofelice@parrishconstruction.com



Trey DeRieux

Project Engineer
470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent
678.215.5193

dplunkett@parrishconstruction.com

WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .
